

GALLERY AT FAT VILLAGE

DATE 8-16-22


EXHIBIT 4

Page 1 of 2

ID	Task Name	Duration	Start	Finish	September	October	November	December	January	February	March	April	May	June	July	August	September	October	November	December	January	February	March	April	May	June	July	August	September	October
1	Tower	480 days	Mon 10/31/22	Fri 8/30/24																										
2	Notice to Proceed	1 day	Mon 10/31/22	Mon 10/31/22																										
3	Survey	5 days	Tue 11/1/22	Mon 11/7/22																										
4	Property line/Corners/BenchMark	5 days	Tue 11/1/22	Mon 11/7/22																										
5	Site Prep	10 days	Tue 11/8/22	Mon 11/21/22																										
6	Clear and Grub site	10 days	Tue 11/8/22	Mon 11/21/22																										
7	Install Site Fence	1 day	Thu 11/17/22	Thu 11/17/22																										
8	Vibro Foundation	24 days	Tue 11/22/22	Fri 12/23/22																										
9	Mobilize	5 days	Tue 11/22/22	Mon 11/28/22																										
10	Vibro Compaction	15 days	Tue 11/29/22	Mon 12/19/22																										
11	Demobilize	4 days	Tue 12/20/22	Fri 12/23/22																										
12	Site infill	10 days	Tue 12/20/22	Mon 1/2/23																										
13	Raise site fill 7'0"NGVD	10 days	Tue 12/20/22	Mon 1/2/23																										
14	Foundations	60 days	Tue 1/3/23	Mon 3/27/23																										
15	Pour A	20 days	Tue 1/3/23	Mon 1/30/23																										
16	Pour B	20 days	Tue 1/31/23	Mon 2/27/23																										
17	Tower Crane	15 days	Tue 1/31/23	Mon 2/20/23																										
18	Excavate Crane Pad	2 days	Tue 1/31/23	Wed 2/1/23																										
19	Install Rebar	5 days	Thu 2/2/23	Wed 2/8/23																										
20	Set Crane Pad Stools	1 day	Thu 2/9/23	Thu 2/9/23																										
21	Place Crane Pad	1 day	Fri 2/10/23	Fri 2/10/23																										
22	Install Crane	5 days	Mon 2/13/23	Fri 2/17/23																										
23	Crane Sign Off	1 day	Mon 2/20/23	Mon 2/20/23																										
24	Civil Site Improved	20 days	Tue 2/28/23	Mon 3/27/23																										
25	Install Structures	10 days	Tue 2/28/23	Mon 3/13/23																										
26	Install Sanitary	10 days	Tue 3/7/23	Mon 3/20/23																										
27	Install Storm	10 days	Tue 3/14/23	Mon 3/27/23																										
28	Shell	145 days	Tue 3/28/23	Mon 10/16/23																										
29	1st Verticals	18 days	Tue 3/28/23	Thu 4/20/23																										
30	2nd Floor	18 days	Fri 4/21/23	Tue 5/16/23																										
31	3rd Floor	12 days	Wed 5/17/23	Thu 6/1/23																										
32	4th Floor	12 days	Fri 6/2/23	Mon 6/19/23																										
33	5th Floor	12 days	Tue 6/20/23	Wed 7/5/23																										
34	6th Floor	12 days	Thu 7/6/23	Fri 7/21/23																										
35	7th Floor	8 days	Mon 7/24/23	Wed 8/2/23																										
36	8th Floor	8 days	Thu 8/3/23	Mon 8/14/23																										
37	9th Floor	7 days	Tue 8/15/23	Wed 8/23/23																										
38	10th Floor	7 days	Thu 8/24/23	Fri 9/1/23																										
39	11th Floor	7 days	Mon 9/4/23	Tue 9/12/23																										
40	12 Floor	7 days	Wed 9/13/23	Thu 9/21/23																										
41	Roof	7 days	Fri 9/22/23	Mon 10/2/23																										
42	Upper Roof	5 days	Tue 10/3/23	Mon 10/9/23																										
43	Uper Roof Parapets	5 days	Tue 10/10/23	Mon 10/16/23																										
44	SOG	5 days	Tue 10/10/23	Mon 10/16/23																										
45	Exterior Envelope	75 days	Mon 7/24/23	Fri 11/3/23																										
46	2nd Floor	20 days	Mon 7/24/23	Fri 8/18/23																										
47	3rd Floor	20 days	Mon 7/31/23	Fri 8/25/23																										
48	4th Floor	20 days	Mon 8/7/23	Fri 9/1/23																										
49	5th Floor	20 days	Mon 8/14/23	Fri 9/8/23																										
50	6th Floor	20 days	Mon 8/21/23	Fri 9/15/23																										
51	7th Floor	15 days	Mon 8/28/23	Fri 9/15/23																										

Project: 8-16-22 Schedule Date: Tue 8/16/22	Task		Summary		Inactive Milestone		Duration-only		Start-only		External Milestone		Manual Progress	
	Split		Project Summary		Inactive Summary		Manual Summary Rollup		Finish-only		Deadline			
	Milestone		Inactive Task		Manual Task		Manual Summary		External Tasks		Progress			

GALLERY AT FAT VILLAGE

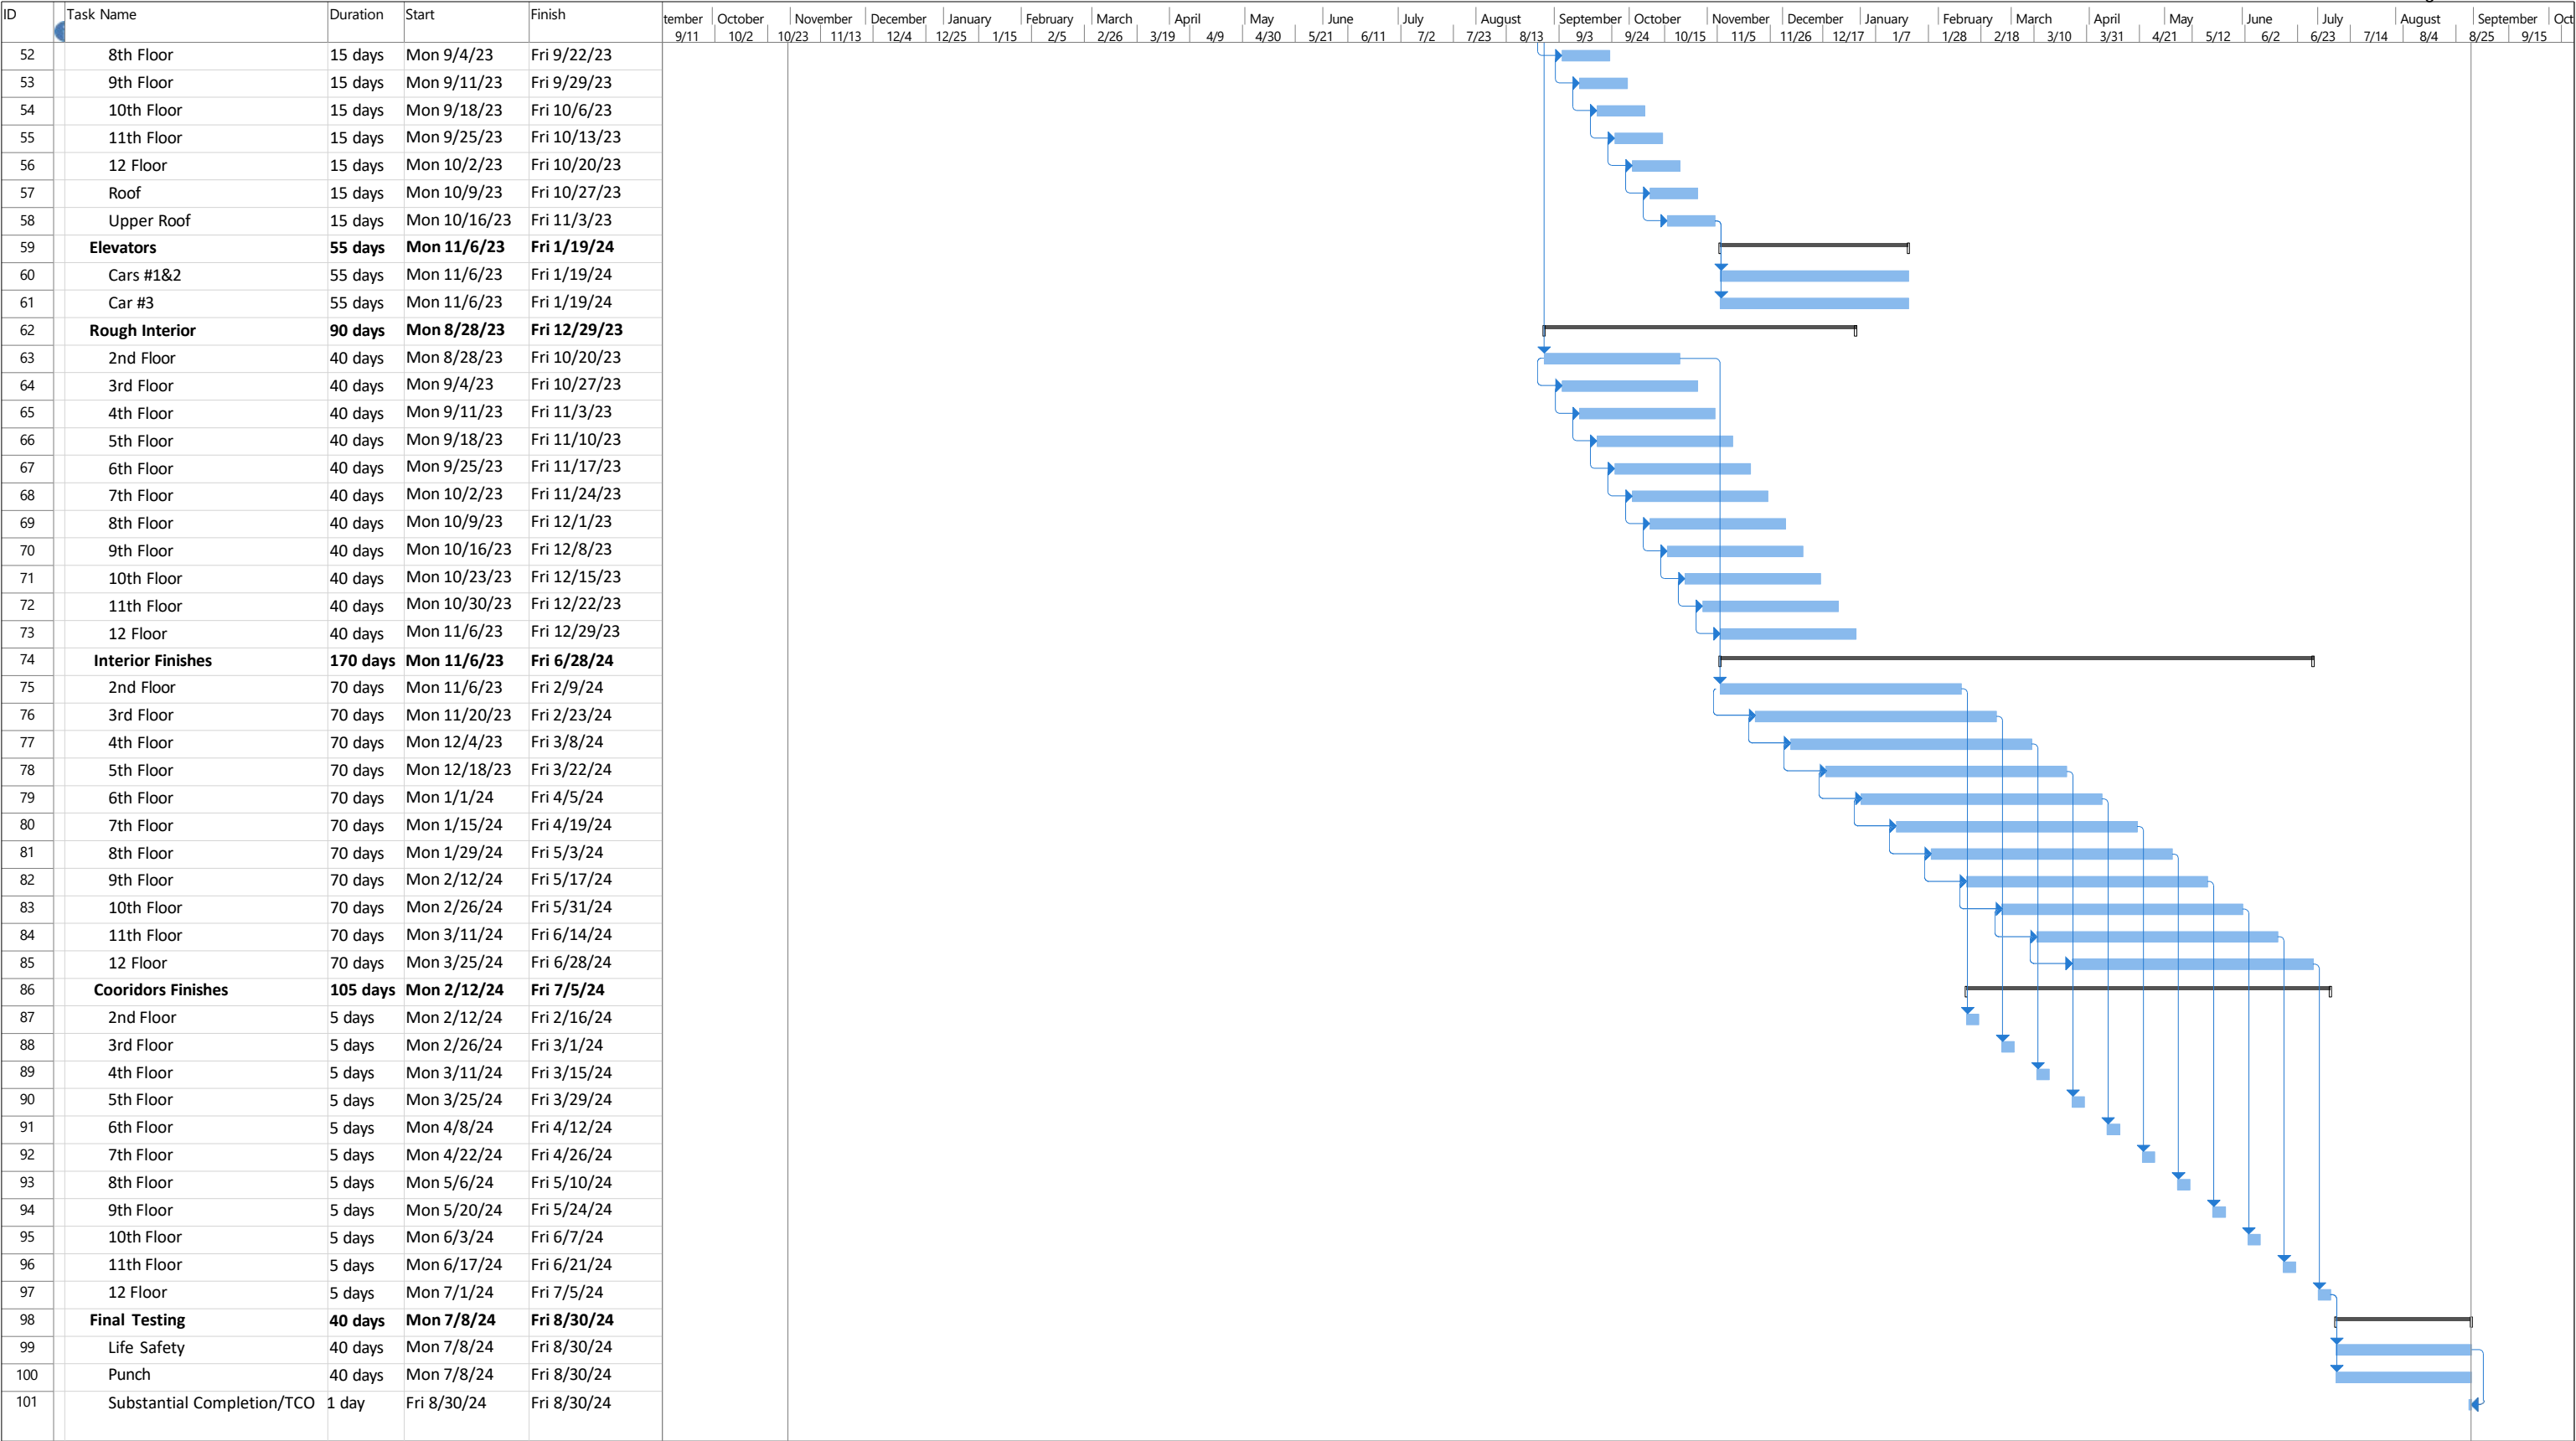

Project: 8-16-22 Schedule
Date: Tue 8/16/22

Task

Split

Milestone

.....

◆

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

◆

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Progress

◆

↓

Manual Progress
