

CHANGE ORDER NO: 3

BOARD REGULAR

Project: - Port Everglades Wayfinding Sign Project

Contract: PNC2117560C1 Vend: HORSEPOWER ELECTRIC INC

The following changes are hereby authorized upon approval of the Board and his/her signature below.

Description of Changes, Reasons Therefore, and Cost and/or Time Changes For Each:

Cost Basis: Negotiated Lump Sum, Negotiated Lump Sum, Negotiated Lump Sum, Negotiated Lump Sum, Negotiated Lump Sum


	AMOUNT	TIME
ORIGINAL CONTRACT	\$3,631,302.65	275
PREV APPROVED CHANGE ORDERS	\$63,310.30	280
THIS CHANGE ORDER NO. 3	\$360,889.44	328
REVISED CONTRACT AMOUNT	\$4,055,502.39	883
PENDING CHANGE ORDERS	\$360,889.44	328

	Current	- Apprvd CO	- This CO	= Remaining
Admin Allowance	5.00	1.74		3.26

INCREASE CONTRACT AMOUNT BY \$360,889.44

INCREASE CONTRACT PERIOD BY 328 Days


No Consultant

Signature:  Date: 8/2/22

Name: MICHAEL MARTINEZ

HORSEPOWER ELECTRIC INC Representative

P.B. Recommended By PORT EVERGLADES -SEAPORT ENGINEERING & CONSTRUCTION DIVISION Project Manager

Signature:  Date: 8/3/22

Claude Gentil

Recommended By PORT EVERGLADES -SEAPORT ENGINEERING & CONSTRUCTION DIVISION Contract Administrator

Signature:  Date: 8/6/2022

John Foglesong Division Director

Recommended By Port Everglades Department Director

Signature:  Date: 9-16-22

Jonathan Daniels, Department Director

Approved By Broward County Board Of County Commissioners

Signature: _____ Date: _____

Name: _____

Name: _____

COPY FOR: MINUTES, CONTRACTOR, PURCHASING, CONSULTANT, SUPERVISING AGENCY, BUDGET, DEPARTMENT

8/1/2022

Percentages may not total exactly, due to rounding

Source: ContractsCentral - A Service Of The Purchasing Division

DRAFT DRAFT DRAFT DRAFT

CHANGE ORDER NO: 3

BOARD REGULAR

Project: - Port Everglades Wayfinding Sign Project

Contract: PNC2117560C1 Vend: HORSEPOWER ELECTRIC INC

The following changes are hereby authorized upon approval of the Board and his/her signature below.

Description of Changes, Reasons Therefore, and Cost and/or Time Changes For Each:

Cost Basis: Negotiated Lump Sum, Negotiated Lump Sum, Negotiated Lump Sum, Negotiated Lump Sum, Negotiated Lump Sum

Line Nbr.1	TIME EXTENSION - OWNER REQUESTED CHANGES - Additional Time with Cost	\$0.00	328
Description : Time Extension to implement CO No. 3			
Reason : Additional enhancement were requested by the end user to improve visitors overall experience.			
Cause : User requested scope			
Line Nbr.2	USER REQUESTED ENHANCEMENTS - User Requested Enhancements	\$12,300.00	0
Description : New Item PNC211560C1--01-52 - Fabricate and install adhesive overlays with parking and arrows symbols over existing sign panels. Quantity of forty one (41) at a unit price of \$300.00 for a line item total of \$12,300 increase to the contract.			
Reason : Additional enhancement were requested by the end user to improve visitors overall experience.			
Cause : User requested scope			
Line Nbr.3	USER REQUESTED ENHANCEMENTS - User Requested Enhancements	\$6,000.51	0
Description : New Item PNC211560C1--01-53 - Relocate FL-B_07 sign panel to FL-C_04 side B outer most position. Quantity of one (1) at a unit price of \$6,000.51 and an increase to the contract of \$6,000.51.			
Reason : Additional enhancement were requested by the end user to improve visitors overall experience.			
Cause : User requested scope			
Line Nbr.4	USER REQUESTED ENHANCEMENTS - User Requested Enhancements	\$2,039.20	0
Description : New Item PNC211560C1--01-54 - Furnish and install Banner CT_2 on spare post and new foundation. Quantity of one (1) at a unit price of \$2,039.20 and an increase to the contract amount of \$2,039.20.			
Reason : Additional enhancement were requested by the end user to improve visitors overall experience.			
Cause : User requested scope			

COPY FOR: MINUTES, CONTRACTOR, PURCHASING, CONSULTANT, SUPERVISING AGENCY, BUDGET, DEPARTMENT

8/1/2022

Percentages may not total exactly, due to rounding

Source: ContractsCentral

DRAFT DRAFT DRAFT DRAFT

CHANGE ORDER NO: 3

BOARD REGULAR

Project: - Port Everglades Wayfinding Sign Project

Contract: PNC2117560C1 Vend: HORSEPOWER ELECTRIC INC

The following changes are hereby authorized upon approval of the Board and his/her signature below.

Description of Changes, Reasons Therefore, and Cost and/or Time Changes For Each:

Cost Basis: Negotiated Lump Sum, Negotiated Lump Sum, Negotiated Lump Sum, Negotiated Lump Sum, Negotiated Lump Sum

Line Nbr.5	USER REQUESTED ENHANCEMENTS - User Requested Enhancements	\$4,940.51	0
Description :	New Item PNC211560C1--01-55 - Furnish and install DIR_T18 on spare posts and new foundation. Quantity of one (1) at a unit price of \$4,940.51 and an increase to the contract amount of \$4,940.51.		
Reason :	Additional enhancement were requested by the end user to improve visitors overall experience.		
Cause :	User requested scope		
Line Nbr.6	USER REQUESTED ENHANCEMENTS - User Requested Enhancements	\$221,898.59	0
Description :	New Item PNC211560C1--01-56 - Furnish and install MON_2 Sign, complete with posts and foundations. Quantity of one (1) at a unit price of \$221,898.59 and an increase to the contract amount of \$221,898.59.		
Reason :	Additional enhancement were requested by the end user to improve visitors overall experience.		
Cause :	User requested scope		
Line Nbr.7	USER REQUESTED ENHANCEMENTS - User Requested Enhancements	\$6,657.50	0
Description :	New Item PNC211560C1--01-57 - Furnish and install DIR Snook/Palm on existing post, replacing existing panel. Quantity of three (3) at a unit price of \$2,219.17 resulting on an increase to the contract amount of \$6,657.50.		
Reason :	Additional enhancement were requested by the end user to improve visitors overall experience.		
Cause :	User requested scope		
Line Nbr.8	USER REQUESTED ENHANCEMENTS - User Requested Enhancements	\$6,000.51	0
Description :	New Item PNC211560C1--01-58 - Furnish and install FL-D_04 Snook/Palm in existing frame, re-use arrow, icon and frame. Quantity of one (1) at a unit price of \$6,000.51 resulting on an increase to the contract amount of \$6,000.51		
Reason :	Additional enhancement were requested by the end user to improve visitors overall experience.		
Cause :	User requested scope		

COPY FOR: MINUTES, CONTRACTOR, PURCHASING, CONSULTANT, SUPERVISING AGENCY, BUDGET, DEPARTMENT

8/1/2022

Percentages may not total exactly, due to rounding

Source: ContractsCentral

DRAFT DRAFT DRAFT DRAFT

CHANGE ORDER NO: 3

BOARD REGULAR

Project: - Port Everglades Wayfinding Sign Project

Contract: PNC2117560C1 Vend: HORSEPOWER ELECTRIC INC

The following changes are hereby authorized upon approval of the Board and his/her signature below.

Description of Changes, Reasons Therefore, and Cost and/or Time Changes For Each:

Cost Basis: Negotiated Lump Sum, Negotiated Lump Sum, Negotiated Lump Sum, Negotiated Lump Sum, Negotiated Lump Sum

Line Nbr.9	USER REQUESTED ENHANCEMENTS - User Requested Enhancements	\$4,940.51	0
Description : New Item PNC211560C1--01-59 - Install spare Heron T2-4 Sign on FL-D_06 South Side of sign. Quantity of 1 at a unit price of \$4,940.51 resulting on an increase to contract amount of \$4,940.51.			
Reason : Additional enhancement were requested by the end user to improve visitors overall experience.			
Cause : User requested scope			
Line Nbr.10	USER REQUESTED ENHANCEMENTS - User Requested Enhancements	\$6,000.51	0
Description : New Item PNC211560C1--01-60 Furnish and install Heron T-18 sign panel, complete with new icon, arrow, install on FL-D_06 north side of sign. Quantity of one (1) at a unit price of \$6,000.51 resulting on an increase to contract amount of \$6,000.51.			
Reason : Additional enhancement were requested by the end user to improve visitors overall experience.			
Cause : User requested scope			
Line Nbr.11	USER REQUESTED ENHANCEMENTS - User Requested Enhancements	\$8,603.82	0
Description : New Item PNC211560C1--01-61 - Furnish and install sign panels to replace existing T4-GTA, re-use icons, arrows, and frames. Quantity of three (3) at a unit price of \$2,867.94 resulting on an increase to contract amount of \$8,603.82.			
Reason : Additional enhancement were requested by the end user to improve visitors overall experience.			
Cause : User requested scope			
Line Nbr.12	USER REQUESTED ENHANCEMENTS - User Requested Enhancements	\$4,631.78	0
Description : New Item PNC211560C1--01-62 Furnish and install Heron Icons and adhesive overlays I595 to cover I75 icons for T4 GTA signs. Quantity of 2 at a unit price of \$2,315.89			
Reason : Additional enhancement were requested by the end user to improve visitors overall experience.			
Cause : User requested scope			

COPY FOR: MINUTES, CONTRACTOR, PURCHASING, CONSULTANT, SUPERVISING AGENCY, BUDGET, DEPARTMENT

8/1/2022

Percentages may not total exactly, due to rounding

Source: ContractsCentral

DRAFT DRAFT DRAFT DRAFT

CHANGE ORDER NO: 3

BOARD REGULAR

Project: - Port Everglades Wayfinding Sign Project

Contract: PNC2117560C1 Vend: HORSEPOWER ELECTRIC INC

The following changes are hereby authorized upon approval of the Board and his/her signature below.

Description of Changes, Reasons Therefore, and Cost and/or Time Changes For Each:

Cost Basis: Negotiated Lump Sum, Negotiated Lump Sum, Negotiated Lump Sum, Negotiated Lump Sum, Negotiated Lump Sum

Line Nbr.13	USER REQUESTED ENHANCEMENTS - User Requested Enhancements	\$68,876.00	0
Description : New Item PNC211560C1--01-63 - Install spare DMS sign on building canopy with all necessary structural supports, fiber optic connections, directional boring and electrical supply from existing electrical panel. Quantity of 1 LS at a unit rate of \$68,876.00 resulting on an increase to the contract amount of \$68,876.00			
Reason : Additional enhancement were requested by the end user to improve visitors overall experience.			
Cause : User requested scope			
Line Nbr.14	USER REQUESTED ENHANCEMENTS - User Requested Enhancements	\$8,000.00	0
Description : New Item PNC211560C1--01-64 - Provide engineering drawings for the installation of DMS sign on existing building canopy. Quantity of 1 LS of \$8,000.00 resulting on an increase to the contract in the amount of \$8,000.00			
Reason : Additional enhancement were requested by the end user in proximity of reaching the project's original substantial completion to improve visitors overall experience.			
Cause : User requested scope			

Total Change Order **\$360,889.44** **328**

PURCHASING INFORMATION				
PO : PO SEA2000024		Folder : 0	RX :	
Original Award :	Approved Amendments :	0	Approved COs :	2
\$3,631,302.65	\$0.00		\$63,310.30	
275 Days	0 Days		280 Days	
Previous Revised :				
This REGULAR Change Order:		INCREASE	\$360,889.44	INCREASE 328 Days
New Revised Contract:			\$4,055,502.39	883 Days

COPY FOR: MINUTES, CONTRACTOR, PURCHASING, CONSULTANT, SUPERVISING AGENCY, BUDGET, DEPARTMENT

8/1/2022


Percentages may not total exactly, due to rounding

Source: ContractsCentral

[illegible]

SCOPE

- EIGHT (8) LARGE WHITE Ps WITH BLUE BACKGROUND ADHESIVE OVERLAY.
 - ONE (1) OVERSIZED WHITE P WITH BLUE BACKGROUND ADHESIVE OVERLAY.
 - FIVE (5) WHITE ARROWS ON BLUE BACKGROUND ADHESIVE OVERLAY.
 - SEVEN (7) SMALL WHITE Ps WITH BLUE BACKGROUND ADHESIVE OVERLAY.
 - SEVEN (7) WHITE ARROW ON GREEN BACKGROUND ADHESIVE OVERLAY.
 - ELEVEN (11) WHITE ARROW ON ORANGE BACKGROUND ADHESIVE OVERLAY.
 - ONE (1) COMPLETE HERON SIGN MOUNT ON FL-B-07 RELOCATE EXIT TO BACK OF FL-C_04 OUTSIDE 3RD POSITION
 - ONE (1) BANNER CT-2 WITH RIGHT ARROW (VERIFY WE HAVE SPARE POST).
 - ONE (1) DIR-SMALL T18 U TURN (ON SPARE SUPPORT POSTS).
 - MON-2 SIGN -NEW COMPLETE, SE CORNER OF ELLER AND SE 19TH AVE.
 - THREE (3) NEW DIR SNOOK/PALM (REUSE ARROW AND ICON, MOUNT.)
 - ONE (1) FL-D_04 SNOOK PANEL (REUSE ARROW AND ICON, FRAME.)
 - ONE (1) INSTALL SPARE HERON T2-4 SIGN, ADD TO FL-D_06 SOUTH FACE
 - ONE (1) HERON T-18 PANEL, ICON, ARROW, ADD TO FL-D_06 NORTH FACE
 - THREE (3) NEW SIGN PANELS FOR EXISTING T4-GTA (RE-USE ICONS, ARROWS, FRAMES)
 - TWO MODS TO EXISTING SIGNS OVER CANOPY T4-GTA, INCLUDES
 - TWO (2) I-595 ADHESIVE SIGNS TO COVER I-75 SIGNS T4-GTA AREA
- INSTALL SPARE DMS SIGN ON T21 FASCIA WALL - FIELD COORDINATION AND DESIGN REQUIRED,

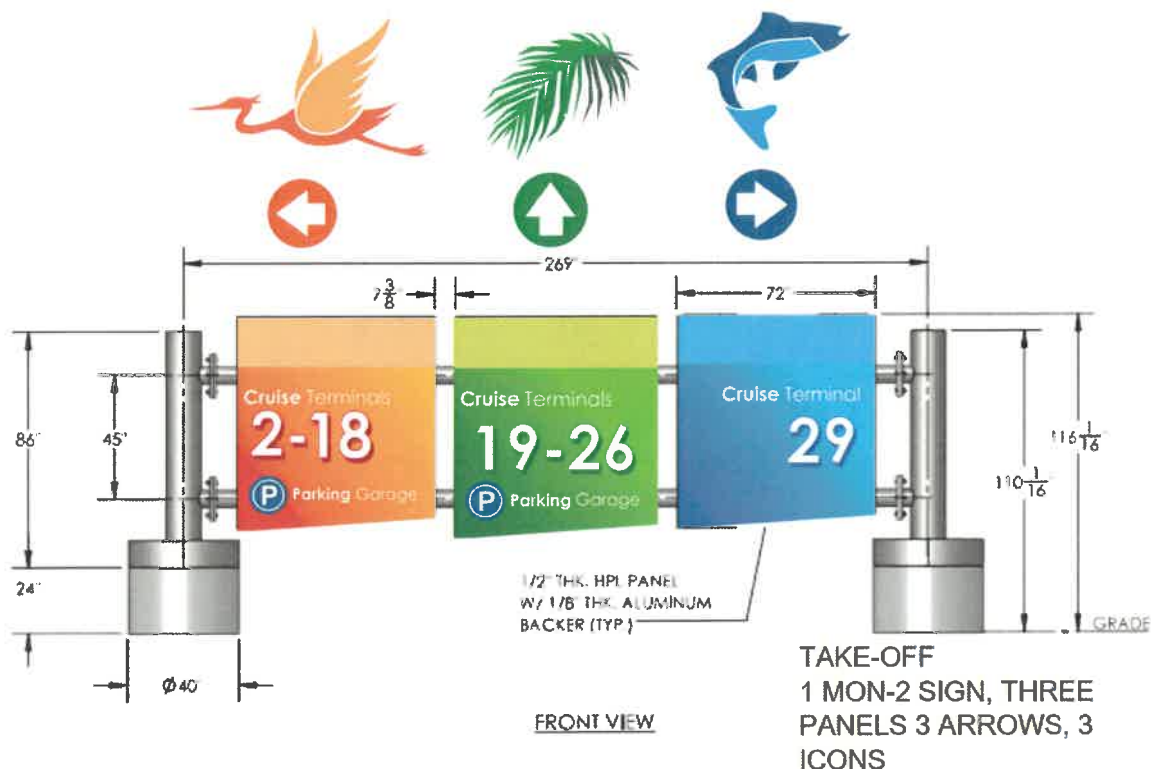



MODS TO FL-C_04 HERON - ADD "P" TOP RIGHT





MODS TO BANNER SNOOK - ADD "P" BOTTOM LEFT





MODS TO BANNER SNOOK - ADD "P" BOTTOM LEFT





MODS TO BANNER SNOOK - ADD "P" BOTTOM LEFT





MODS TO BANNER SNOOK - ADD "P" BOTTOM LEFT





MODS TO BANNER SNOOK - ADD "P" BOTTOM LEFT





DIR_16, 17, 18 NEW PANELS - REUSE ARROW AND ICON


3'-2" x 3'-7" SAME AS ORIGINAL





DIR_16, 17, 18 NEW PANELS - REUSE ARROW AND ICON

3'-2" x 3'-7" SAME AS ORIGINAL

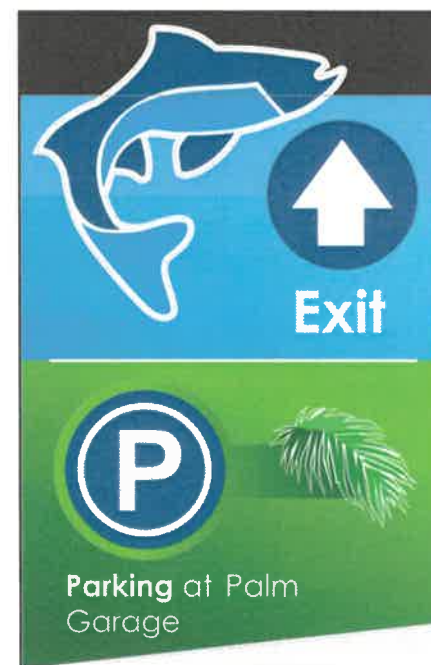



FL-D_04 NEW FACE PANELS, REUSE ICON AND ARROW




6'-0" x 6'-6" SAME AS ORIGINAL





DIR_16, 17, 18 NEW PANELS - REUSE ARROW AND ICON

3'-2" x 3'-7" SAME AS ORIGINAL

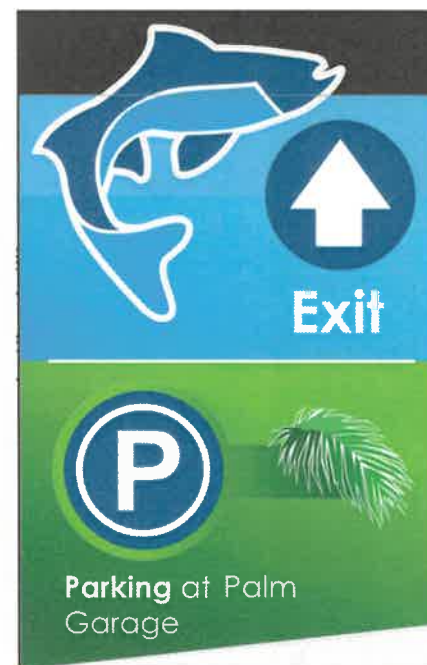



BANNER 19- 26 - ADD "P" AND UP ARROW





BANNER 19- 26 - ADD "P" AND UP ARROW





BANNER 21- 25 - ADD "P" AND UP ARROW





BANNER 21- 25 - ADD "P" AND UP ARROW



BANNER 19 - ADD UP ARROW





BANNER 21 - ADD UP ARROW (COVER





FL-B_07

- MOVE EXIT SIGN TO BACK OF FL-C_04
 - INSTALL HERON 2-18 FABRICATE NEW
- RIGHT HAND HERON, RIGHT ARROW





MODS TO BANNER HERON - ADD UP ARROW BOTTOM
LEFT



MODS TO FL-E_01 - ADD UP "P" TOP RIGHT





MODS TO FL-D_02 - ADD UP "P" BOTTOM RIGHT CORNER
"P" IS OVERSIZED TO COVER ORANGE ARROW IN WHITE
CIRCLE






MODS TO BANNER HERON - ADD UP ARROW BOTTOM
LEFT





MODS TO FL-B_06: ADD FROM SPARE PANEL ON FRAME,
UP ARROW AND RIGHT HANDED HERON, MOUNT ON
OUTSIDE

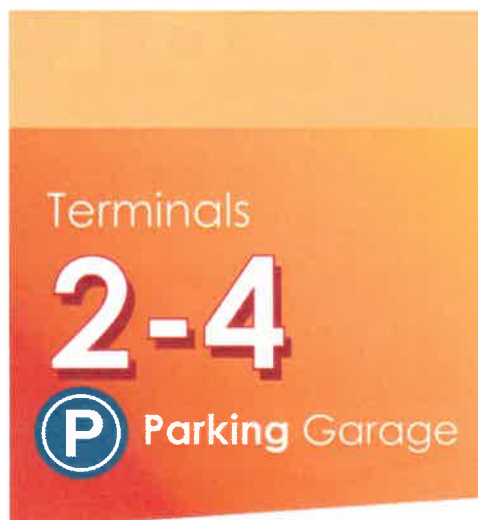

FL-B_06 EXISTING SIGN MODIFICATION (NORTH FACE)

REMOVE HPL's FOR BERTH 29, REPLACE WITH NEW CT-18
SWAP POSITIONS CT-18 ON LEFT SIDE, 19-26 ON RIGHT SIDE





MODS TO BANNER HERON - ADD UP ARROW BOTTOM
LEFT



MODS TO BANNER HERON - ADD UP ARROW BOTTOM
LEFT





MODS TO FL-D_01- ADD UP "P" BOTTOM RIGHT






MODS TO BANNER HERON - ADD UP ARROW BOTTOM
LEFT





MODS TO FL-C_01 - ADD "P" AS SHOWN -
MOVE PANEL TO 3RD POSITION TO THE
RIGHT

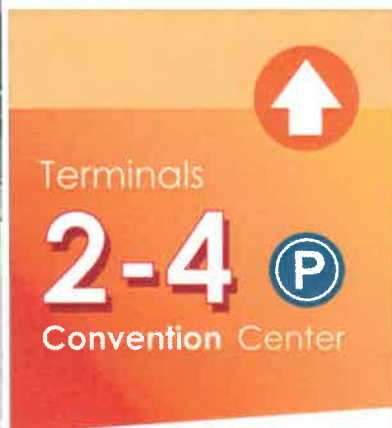



MODS TO BANNER HERON - ADD UP ARROW BOTTOM
LEFT



NEW BANNER HERON - AS SHOWN





Cruise Parking

SUPPLY THIS SIGN, WRONG SIGN WAS PRODUCED, WAS MARKED UP ON SHOP DRAWING No. 2

CORRECTED ON SHOP DRAWINGS No. 5 - FABRICATED WRONG, REPLACE AT NO CHARGE



SIDE A

SIDE B

DIR_05



 422nd Hineswood Center Flat Complex 1901 E. 1st Street Fort Lauderdale, FL 33316	A+	Design: 2-3 Date: 10/10/16 Revision: 10/10/16	UL I-M Companies	Sheet 19c
---	----	---	---------------------	--------------



INSTALL ALREADY FABRICATED DIR PANEL ON
TOP OF BARRIER WALL,
MODIFY SPARE TWO POST MOUNT FOR IT.



mount on barrier





MODS TO FL-C_01 - ADD "P" AS SHOWN





MODS TO BANNER HERON - ADD UP ARROW BOTTOM
LEFT



MODS TO FL-C_02 - ADD "P" AS SHOWN





MODS TO BANNER HERON - ADD RIGHT ARROW BOTTOM
LEFT





MODS TO MON-1 - ADD "P" AS SHOWN BELOW





MODS TO BANNER HERON - ADD UP ARROW BOTTOM
LEFT





MODS TO BANNER HERON - ADD UP ARROW BOTTOM
LEFT





MODS TO BANNER PALM - ADD UP ARROW AND "P" BOTTOM LEFT





MODS TO BANNER HERON - ADD UP ARROW BOTTOM
LEFT





NEW DIR T18 U TURN SIGN ON POSTS

FABRICATE NEW SIGN, INSTALL ON SPARE
DOUBLE POST MOUNT

FABRICATE NEW SIGN, INSTALL ON SPARE
3'-2" wide
4'-4" length
3'-11 3/4" length





MODS TO BANNER PALM - ADD UP ARROW AND "P" BOTTOM LEFT







PANEL CHANGES ON EXISTING SIGN ST008 - REVIEW SHOP DRAWINGS AND FIELD VERIFY DIMENSIONS.



LEFT SIDE NEW PANEL, RE-USE RIGHT HANDED HERON, NEW UP ARROW.

RIGHT SIDE NEW PANEL, RE-USE RIGHT HANDED HERON, RE-USE ARROW.

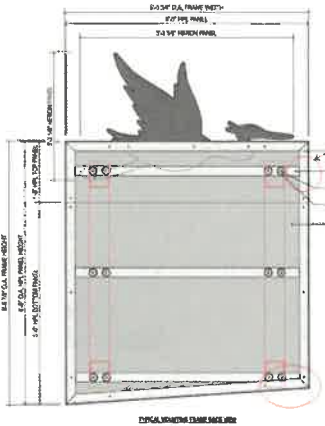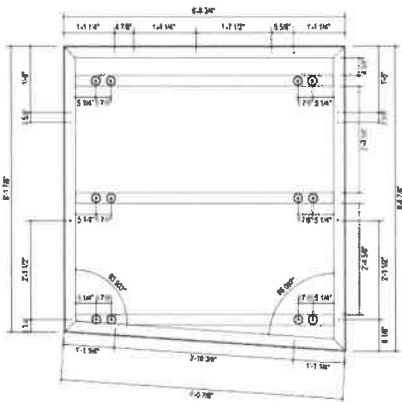

EXISTING SIGN
DIMENSIONS

VERIFY ON THE
FIELD



PANEL FACE CHANGES ON EXISTING SIGN ST008 -
REVIEW SHOP DRAWINGS AND FIELD VERIFY
DIMENSIONS.




LEFT SIDE NEW
PANEL, RE-USE LEFT
HANDED HERON,
RE-USE ARROW.

RIGHT SIDE REMOVE
PANEL -

EXISTING SIGN PANELS (ST010.1) OVER CANOPY HERON GARAGE EXIT
REVIEW SHOP DRAWINGS AND DO THE FOLLOWING CHANGES:

EXISTING SIGN PANELS AND ICONS

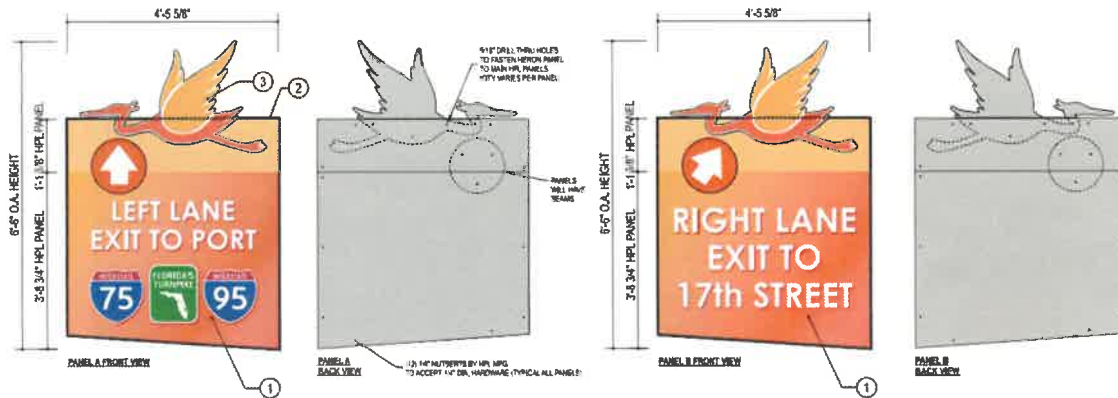

LEFT SIGN PANEL -
COVER I-75 WITH I-595
ADHESIVE SIGN


RIGHT SIGN PANEL - REPLACE
HERON WITH RIGHT SIDED HERON,
RELOCATE ARROW TO THE RIGHT
SIDE OF THE FACE PANEL



14" X 14"

Panel A Heron Detail

Scale: 1/2"=1'-0"

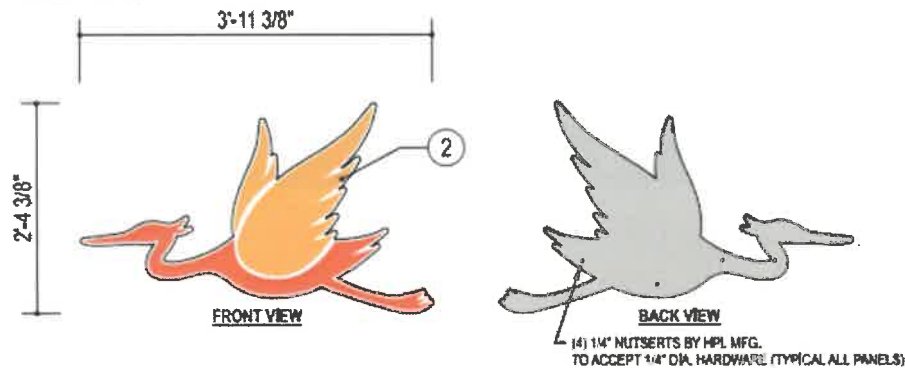

RIGHT HANDED HERON
3'-11 3/8" X 2'-4 3/8"




PANEL CHANGES ON EXISTING SIGN 010 - REVIEW SHOP DRAWINGS AND FIELD VERIFY DIMENSIONS.



Heron Panel Detail

Scale: 3/8"=1'-0"

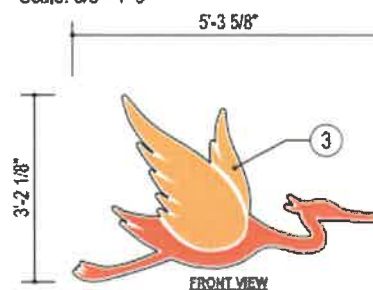

LEFT PANEL,
COVER I-75
WITH I-595
OVERLAY ADHESIVE
SIGN



RIGHT PANEL,
REPLACE HERON,
WITH RIGHT SIDED
RE-LOCATE ARROW
TO RIGHT SIDE OF
PANEL FACE
