

BOARD OF COUNTY COMMISSIONERS, BROWARD COUNTY, FLORIDA

CHANGE ORDER NO: 3
BOARD REGULAR

Project: - Port Everglades Wayfinding Sign Project

Contract: PNC2117560C1 Vend: HORSEPOWER ELECTRIC INC

The following changes are hereby authorized upon approval of the Board and his/her signature below.

Description of Changes, Reasons Therefore, and Cost and/or Time Changes For Each:

Cost Basis: Negotiated Lump Sum, Negotiated Lump Sum, Negotiated Lump Sum, Negotiated Lump Sum, Negotiated Lump Sum

	AMOUNT	TIME
ORIGINAL CONTRACT	\$3,631,302.65	275
PREV APPROVED CHANGE ORDERS	\$63,310.30	280
THIS CHANGE ORDER NO. 3	\$360,889.44	328
REVISED CONTRACT AMOUNT	\$4,055,502.39	883
PENDING CHANGE ORDERS	\$360,889.44	328

	Current	- Apprvd CO	- This CO	= Remaining
Admin Allowance	5.00		1.74	3.26

INCREASE CONTRACT AMOUNT BY \$360,889.44

INCREASE CONTRACT PERIOD BY 328 Days


No Consultant

Accepted By Contractor

Signature:  Date: 8/2/22

Name: MICHAEL MARTINEZ
HORSEPOWER ELECTRIC INC Representative

Recommended By PORT EVERGLADES -SEAPORT ENGINEERING & CONSTRUCTION DIVISION Project Manager

Signature:  Date: 8/3/22
Claude Gentil

Recommended By PORT EVERGLADES -SEAPORT ENGINEERING & CONSTRUCTION DIVISION Contract Administrator

Signature:  Date: 8/6/2022
John Foglesong Division Director

Recommended By Port Everglades Department Director

Signature:  Date: 9-16-22
Jonathan Daniels, Department Director

Approved By Broward County Board Of County Commissioners

Signature: _____ Date: _____
Name: _____
Name: _____

COPY FOR: MINUTES, CONTRACTOR, PURCHASING, CONSULTANT, SUPERVISING AGENCY, BUDGET, DEPARTMENT

8/1/2022

Percentages may not total exactly, due to rounding

Source: ContractsCentral - A Service Of The Purchasing Division

DRAFT DRAFT DRAFT DRAFT

CHANGE ORDER NO: 3

BOARD REGULAR

Project: - Port Everglades Wayfinding Sign Project

Contract: PNC2117560C1 Vend: HORSEPOWER ELECTRIC INC

The following changes are hereby authorized upon approval of the Board and his/her signature below.

Description of Changes, Reasons Therefore, and Cost and/or Time Changes For Each:

Cost Basis: Negotiated Lump Sum, Negotiated Lump Sum, Negotiated Lump Sum, Negotiated Lump Sum, Negotiated Lump Sum

Line Nbr.1	TIME EXTENSION - OWNER REQUESTED CHANGES - Additional Time with Cost	\$0.00	328
Description : Time Extension to implement CO No. 3			
Reason : Additional enhancement were requested by the end user to improve visitors overall experience.			
Cause : User requested scope			
Line Nbr.2	USER REQUESTED ENHANCEMENTS - User Requested Enhancements	\$12,300.00	0
Description : New Item PNC211560C1--01-52 - Fabricate and install adhesive overlays with parking and arrows symbols over existing sign panels. Quantity of forty one (41) at a unit price of \$300.00 for a line item total of \$12,300 increase to the contract.			
Reason : Additional enhancement were requested by the end user to improve visitors overall experience.			
Cause : User requested scope			
Line Nbr.3	USER REQUESTED ENHANCEMENTS - User Requested Enhancements	\$6,000.51	0
Description : New Item PNC211560C1--01-53 - Relocate FL-B_07 sign panel to FL-C_04 side B outer most position. Quantity of one (1) at a unit price of \$6,000.51 and an increase to the contract of \$6,000.51.			
Reason : Additional enhancement were requested by the end user to improve visitors overall experience.			
Cause : User requested scope			
Line Nbr.4	USER REQUESTED ENHANCEMENTS - User Requested Enhancements	\$2,039.20	0
Description : New Item PNC211560C1--01-54 - Furnish and install Banner CT_2 on spare post and new foundation. Quantity of one (1) at a unit price of \$2,039.20 and an increase to the contract amount of \$2,039.20.			
Reason : Additional enhancement were requested by the end user to improve visitors overall experience.			
Cause : User requested scope			

COPY FOR: MINUTES, CONTRACTOR, PURCHASING, CONSULTANT, SUPERVISING AGENCY, BUDGET, DEPARTMENT

8/1/2022

Percentages may not total exactly, due to rounding

Source: ContractsCentral

DRAFT DRAFT DRAFT DRAFT

CHANGE ORDER NO: 3

BOARD REGULAR

Project: - Port Everglades Wayfinding Sign Project

Contract: PNC2117560C1 Vend: HORSEPOWER ELECTRIC INC

The following changes are hereby authorized upon approval of the Board and his/her signature below.

Description of Changes, Reasons Therefore, and Cost and/or Time Changes For Each:

Cost Basis: Negotiated Lump Sum, Negotiated Lump Sum, Negotiated Lump Sum, Negotiated Lump Sum, Negotiated Lump Sum

Line Nbr.5	USER REQUESTED ENHANCEMENTS - User Requested Enhancements	\$4,940.51	0
Description :	New Item PNC211560C1--01-55 - Furnish and install DIR_T18 on spare posts and new foundation. Quantity of one (1) at a unit price of \$4,940.51 and an increase to the contract amount of \$4,940.51.		
Reason :	Additional enhancement were requested by the end user to improve visitors overall experience.		
Cause :	User requested scope		
Line Nbr.6	USER REQUESTED ENHANCEMENTS - User Requested Enhancements	\$221,898.59	0
Description :	New Item PNC211560C1--01-56 - Furnish and install MON_2 Sign, complete with posts and foundations. Quantity of one (1) at a unit price of \$221,898.59 and an increase to the contract amount of \$221,898.59.		
Reason :	Additional enhancement were requested by the end user to improve visitors overall experience.		
Cause :	User requested scope		
Line Nbr.7	USER REQUESTED ENHANCEMENTS - User Requested Enhancements	\$6,657.50	0
Description :	New Item PNC211560C1--01-57 - Furnish and install DIR Snook/Palm on existing post, replacing existing panel. Quantity of three (3) at a unit price of \$2,219.17 resulting on an increase to the contract amount of \$6,657.50.		
Reason :	Additional enhancement were requested by the end user to improve visitors overall experience.		
Cause :	User requested scope		
Line Nbr.8	USER REQUESTED ENHANCEMENTS - User Requested Enhancements	\$6,000.51	0
Description :	New Item PNC211560C1--01-58 - Furnish and install FL-D_04 Snook/Palm in existing frame, re-use arrow, icon and frame. Quantity of one (1) at a unit price of \$6,000.51 resulting on an increase to the contract amount of \$6,000.51		
Reason :	Additional enhancement were requested by the end user to improve visitors overall experience.		
Cause :	User requested scope		

COPY FOR: MINUTES, CONTRACTOR, PURCHASING, CONSULTANT, SUPERVISING AGENCY, BUDGET, DEPARTMENT

8/1/2022

Percentages may not total exactly, due to rounding

Source: ContractsCentral

DRAFT DRAFT DRAFT DRAFT

CHANGE ORDER NO: 3

BOARD REGULAR

Project: - Port Everglades Wayfinding Sign Project

Contract: PNC2117560C1 Vend: HORSEPOWER ELECTRIC INC

The following changes are hereby authorized upon approval of the Board and his/her signature below.

Description of Changes, Reasons Therefore, and Cost and/or Time Changes For Each:

Cost Basis: Negotiated Lump Sum, Negotiated Lump Sum, Negotiated Lump Sum, Negotiated Lump Sum, Negotiated Lump Sum

Line Nbr.9	USER REQUESTED ENHANCEMENTS - User Requested Enhancements	\$4,940.51	0
Description : New Item PNC211560C1--01-59 - Install spare Heron T2-4 Sign on FL-D_06 South Side of sign. Quantity of 1 at a unit price of \$4,940.51 resulting on an increase to contract amount of \$4,940.51.			
Reason : Additional enhancement were requested by the end user to improve visitors overall experience.			
Cause : User requested scope			
Line Nbr.10	USER REQUESTED ENHANCEMENTS - User Requested Enhancements	\$6,000.51	0
Description : New Item PNC211560C1--01-60 Furnish and install Heron T-18 sign panel, complete with new icon, arrow, install on FL-D_06 north side of sign. Quantity of one (1) at a unit price of \$6,000.51 resulting on an increase to contract amount of \$6,000.51.			
Reason : Additional enhancement were requested by the end user to improve visitors overall experience.			
Cause : User requested scope			
Line Nbr.11	USER REQUESTED ENHANCEMENTS - User Requested Enhancements	\$8,603.82	0
Description : New Item PNC211560C1--01-61 - Furnish and install sign panels to replace existing T4-GTA, re-use icons, arrows, and frames. Quantity of three (3) at a unit price of \$2,867.94 resulting on an increase to contract amount of \$8,603.82.			
Reason : Additional enhancement were requested by the end user to improve visitors overall experience.			
Cause : User requested scope			
Line Nbr.12	USER REQUESTED ENHANCEMENTS - User Requested Enhancements	\$4,631.78	0
Description : New Item PNC211560C1--01-62 Furnish and install Heron Icons and adhesive overlays I595 to cover I75 icons for T4 GTA signs. Quantity of 2 at a unit price of \$2,315.89			
Reason : Additional enhancement were requested by the end user to improve visitors overall experience.			
Cause : User requested scope			

COPY FOR: MINUTES, CONTRACTOR, PURCHASING, CONSULTANT, SUPERVISING AGENCY, BUDGET, DEPARTMENT

8/1/2022

Percentages may not total exactly, due to rounding

Source: ContractsCentral

DRAFT DRAFT DRAFT DRAFT

CHANGE ORDER NO: 3

BOARD REGULAR

Project: - Port Everglades Wayfinding Sign Project

Contract: PNC2117560C1 Vend: HORSEPOWER ELECTRIC INC

The following changes are hereby authorized upon approval of the Board and his/her signature below.

Description of Changes, Reasons Therefore, and Cost and/or Time Changes For Each:

Cost Basis: Negotiated Lump Sum, Negotiated Lump Sum, Negotiated Lump Sum, Negotiated Lump Sum, Negotiated Lump Sum

Line Nbr.13	USER REQUESTED ENHANCEMENTS - User Requested Enhancements	\$68,876.00	0
Description : New Item PNC211560C1--01-63 - Install spare DMS sign on building canopy with all necessary structural supports, fiber optic connections, directional boring and electrical supply from existing electrical panel. Quantity of 1 LS at a unit rate of \$68,876.00 resulting on an increase to the contract amount of \$68,876.00			
Reason : Additional enhancement were requested by the end user to improve visitors overall experience.			
Cause : User requested scope			
Line Nbr.14	USER REQUESTED ENHANCEMENTS - User Requested Enhancements	\$8,000.00	0
Description : New Item PNC211560C1--01-64 - Provide engineering drawings for the installation of DMS sign on existing building canopy. Quantity of 1 LS of \$8,000.00 resulting on an increase to the contract in the amount of \$8,000.00			
Reason : Additional enhancement were requested by the end user in proximity of reaching the project's original substantial completion to improve visitors overall experience.			
Cause : User requested scope			

Total Change Order **\$360,889.44** **328**

PURCHASING INFORMATION				
PO : PO SEA2000024		Folder : 0		RX :
Original Award :	Approved Amendments :	Approved COs :	Previous Revised :	
\$3,631,302.65	\$0.00	\$63,310.30	\$3,694,612.95	
275 Days	0 Days	280 Days	555 Days	
This REGULAR Change Order:	INCREASE	\$360,889.44	INCREASE	328 Days
New Revised Contract:		\$4,055,502.39		883 Days

COPY FOR: MINUTES, CONTRACTOR, PURCHASING, CONSULTANT, SUPERVISING AGENCY, BUDGET, DEPARTMENT

8/1/2022


Percentages may not total exactly, due to rounding

Source: ContractsCentral

Proposal					
HORSEPOWER ELECTRIC, INC.					
8105 W. 20th Ave. Hialeah, FL 33014					
(305) 819-4060					
PROPOSAL SUBMITTED TO Part Everglades		PHONE 954-468-0142	DATE 5/25/2022		
STREET 1850 Eller Drive		JOB DESCRIPTION Change Order Request #3			
CITY, STATE AND ZIP CODE Fort Lauderdale, FL 33316		JOB LOCATION Fort Lauderdale			
ARCHITECT/DESIGNER n/a	DATE OF PLANS n/a	ATT: Claude Gentil & Pedro Beltran	FAX -		
Line Item		QTY	Unit	Unit Price	Total
1	Large White Parking Symbol with Blue Background Adhesive Overlay	8	EA	\$ 300.00	\$ 2,400.00
2	Oversized White Parking Symbol with Blue Background Adhesive Overlay	1	EA	\$ 300.00	\$ 300.00
3	White Arrows on Blue Background with Adhesive Overlay	6	EA	\$ 300.00	\$ 1,800.00
4	Small white Parking Symbol with Blue Background on Adhesive Overlay	8	EA	\$ 300.00	\$ 2,400.00
5	White Arrows on Green Background on Adhesive Overlay	7	EA	\$ 300.00	\$ 2,100.00
6	White Arrows on Orange Background on Adhesive Overlay	11	EA	\$ 300.00	\$ 3,300.00
7	Heron Sign Mount on FL-B-07, Relocate exit to Back of FL-C_04, Outside 3rd Position	1	EA	\$ 6,000.51	\$ 6,000.51
8	Banner CT-2 with Right Arrow (pending availability of spare post)	1	EA	\$ 2,039.20	\$ 2,039.20
9	Dir-5small T18 U Turn (on spare support post)	1	EA	\$ 4,940.51	\$ 4,940.51
10	MON-2 Sign, New Complete, SE Corner of Eller and SE 19th Avenue	1	EA	\$ 221,898.59	\$ 221,898.59
11	Dir Snook/Palm (reuse arrow, icon, and mount)	3	EA	\$ 2,219.17	\$ 6,657.50
12	FL-D_04 Snook Panel (reuse arrow, icon, and frame)	1	EA	\$ 6,000.51	\$ 6,000.51
13	Install Spare Heron T2-4 Sign, add to FL-D_06 South Face	1	EA	\$ 4,940.51	\$ 4,940.51
14	Heron T-18 Panel, Icon, and Arrow, add to FL-D_06 North Face	1	EA	\$ 6,000.51	\$ 6,000.51
15	New Sign Panels for Existing T4-GTA (reuse icons, arrows, and frames)	3	EA	\$ 2,867.94	\$ 8,603.81
16	Muds to Existing Signs Over Canopy T4-GTA Incl. (2) 1595 adhesive signs to cover 175 Signs T4-GTA Area	2	EA	\$ 2,315.89	\$ 4,631.78
17	Installation of DMS Sign on Wall of Building	1	EA	\$ 68,876.00	\$ 68,876.00
18	Engineering for Installation of DMS	1	EA	\$ 8,000.00	\$ 8,000.00
<p>Days - Due to longer than usual supply lead times, we need 180 days to complete the project.</p>					
<p>Note: MOT, CONCRETE APRONS AND RESTORATION, MONITOR EXISTING STRUCTURES- INSPECTION, SETTLEMENT AND VIBRATION MONITORING IS NOT INCLUDED.</p>					<p>Total \$ 360,889.44</p>
<p><small>We warrant to guarantee to be as specified. All work to be completed in a workmanlike manner according to standard practice. Any alteration or deviation from above specifications involving extra work will be executed only upon written orders, and will become an extra charge over and above the contract. All agreements contingent upon written orders. Payment of money before approval. Owners carry the, license and other necessary insurance. Our workers are fully covered by workers' compensation insurance.</small></p>					
<p>Acceptance of proposal - The above prices, specifications and conditions are satisfactory and are hereby accepted. You are authorized to do work as specified. Payment will be made as outlined above.</p>					
DATE OF ACCEPTANCE: _____			SIGNATURE _____		

SCOPE

- EIGHT (8) LARGE WHITE Ps WITH BLUE BACKGROUND ADHESIVE OVERLAY.
 - ONE (1) OVERSIZED WHITH P WITH BLUE BACKGROUND ADHESIVE OVERLAY.
 - FIVE (5) WHITE ARROWS ON BLUE BACKGROUND ADHESIVE OVERLAY.
 - SEVEN (7) SMALL WHITE Ps WITH BLUE BACKGROUND ADHESIVE OVERLAY.
 - SEVEN (7) WHITE ARROW ON GREEN BACKGROUND ADHESIVE OVERLAY.
 - ELEVEN (11) WHITE ARROW ON ORANGE BACKGROUND ADHESIVE OVERLAY.
 - ONE (1) COMPLETE HERON SIGN MOUNT ON FL-B-07 RELOCATE EXIT TO BACK OF FL-C_04 OUTSIDE 3RD POSITION
 - ONE (1) BANNER CT-2 WITH RIGHT ARROW (VERIFY WE HAVE SPARE POST).
 - ONE (1) DIR-SMALL T18 U TURN (ON SPARE SUPPORT POSTS).
 - MON-2 SIGN -NEW COMPLETE, SE CORNER OF ELLER AND SE 19TH AVE.
 - THREE (3) NEW DIR SNOOK/PALM (REUSE ARROW AND ICON, MOUNT.)
 - ONE (1) FL-D_04 SNOOK PANEL (REUSE ARROW AND ICON, FRAME.)
 - ONE (1) INSTALL SPARE HERON T2-4 SIGN, ADD TO FL-D_06 SOUTH FACE
 - ONE (1) HERON T-18 PANEL, ICON, ARROW, ADD TO FL-D_06 NORTH FACE
 - THREE (3) NEW SIGN PANELS FOR EXISTING T4-GTA (RE-USE ICONS, ARROWS, FRAMES)
 - TWO MODS TO EXISTING SIGNS OVER CANOPY T4-GTA, INCLUDES
 - TWO (2) I-595 ADHESIVE SIGNS TO COVER I-75 SIGNS T4-GTA AREA
- INSTALL SPARE DMS SIGN ON T21 FASCIA WALL - FIELD COORDINATION AND DESIGN REQUIRED,

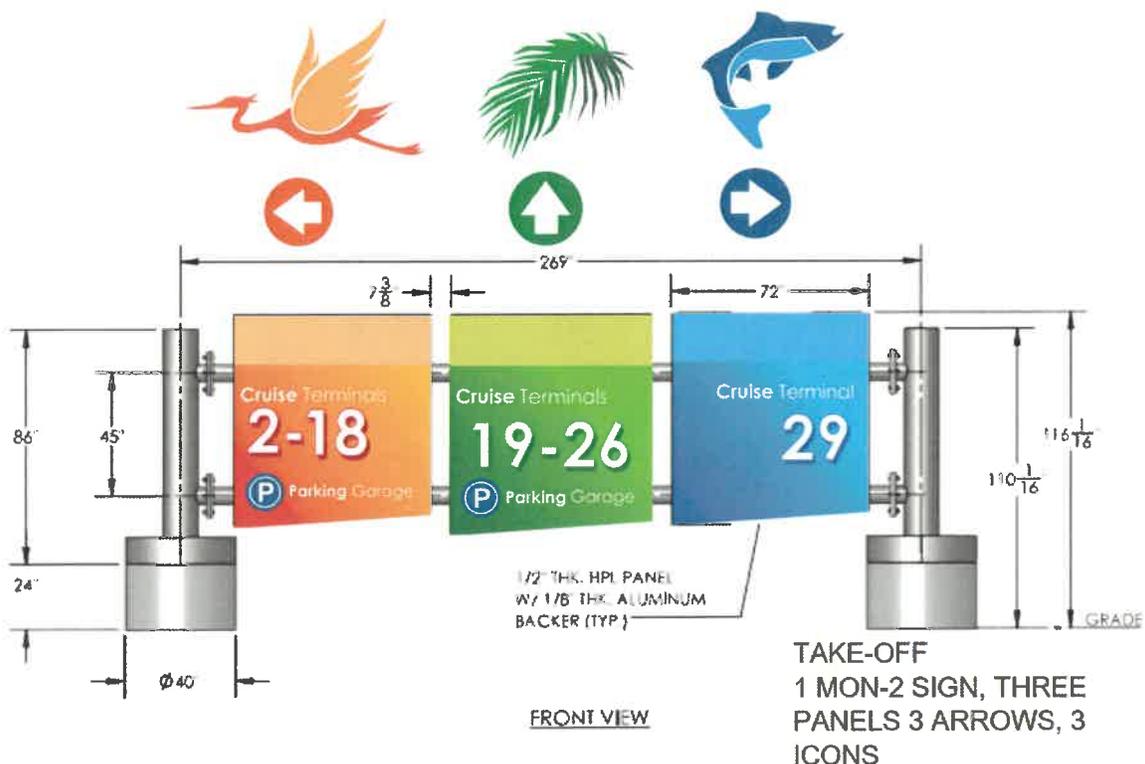




MODS TO FL-C_04 HERON - ADD "P" TOP RIGHT






MODS TO BANNER SNOOK - ADD "P" BOTTOM LEFT



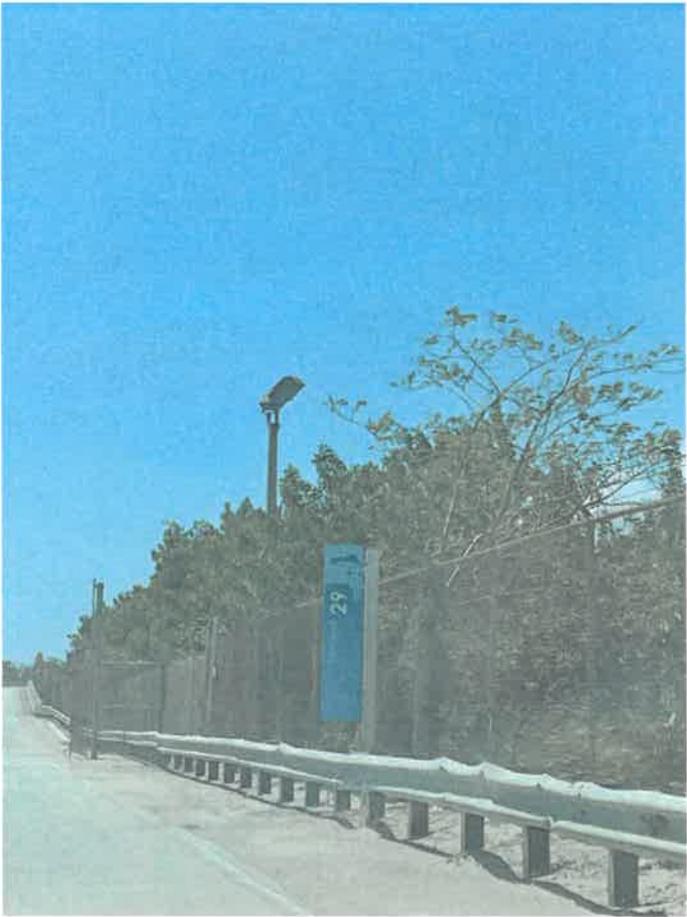


MODS TO BANNER SNOOK - ADD "P" BOTTOM LEFT





MODS TO BANNER SNOOK - ADD "P" BOTTOM LEFT





MODS TO BANNER SNOOK - ADD "P" BOTTOM LEFT





MODS TO BANNER SNOOK - ADD "P" BOTTOM LEFT





DIR_16, 17, 18 NEW PANELS - REUSE ARROW AND ICON

3'-2" x 3'-7" SAME AS ORIGINAL





DIR_16, 17, 18 NEW PANELS - REUSE ARROW AND ICON

3'-2" x 3'-7" SAME AS ORIGINAL





FL-D_04 NEW FACE PANELS, REUSE ICON AND ARROW



6'-0" x 6'-6" SAME AS ORIGINAL





DIR_16, 17, 18 NEW PANELS - REUSE ARROW AND ICON

3'-2" x 3'-7" SAME AS ORIGINAL





BANNER 19- 26 - ADD "P" AND UP ARROW





BANNER 19- 26 - ADD "P" AND UP ARROW





BANNER 21- 25 - ADD "P" AND UP ARROW





BANNER 21- 25 - ADD "P" AND UP ARROW



BANNER 19 - ADD UP ARROW





BANNER 21 - ADD UP ARROW (COVER





FL-B_07
- MOVE EXIT SIGN TO BACK OF FL-C_04
- INSTALL HERON 2 -18 FABRICATE NEW
RIGHT HAND HERON, RIGHT ARROW





MODS TO BANNER HERON - ADD UP ARROW BOTTOM LEFT



MODS TO FL-E_01 - ADD UP "P" TOP RIGHT





MODS TO FL-D_02 - ADD UP "P" BOTTOM RIGHT CORNER
"P" IS OVERSIZED TO COVER ORANGE ARROW IN WHITE
CIRCLE





MODS TO BANNER HERON - ADD UP ARROW BOTTOM LEFT







MODS TO FL-B_06: ADD FROM SPARE PANEL ON FRAME,
UP ARROW AND RIGHT HANDED HERON, MOUNT ON
OUTSIDE



FL-B_06 EXISTING SIGN MODIFICATION (NORTH FACE)

REMOVE HPL's FOR BERTH 29, REPLACE WITH NEW CT-18
SWAP POSITIONS CT-18 ON LEFT SIDE, 19-26 ON RIGHT SIDE

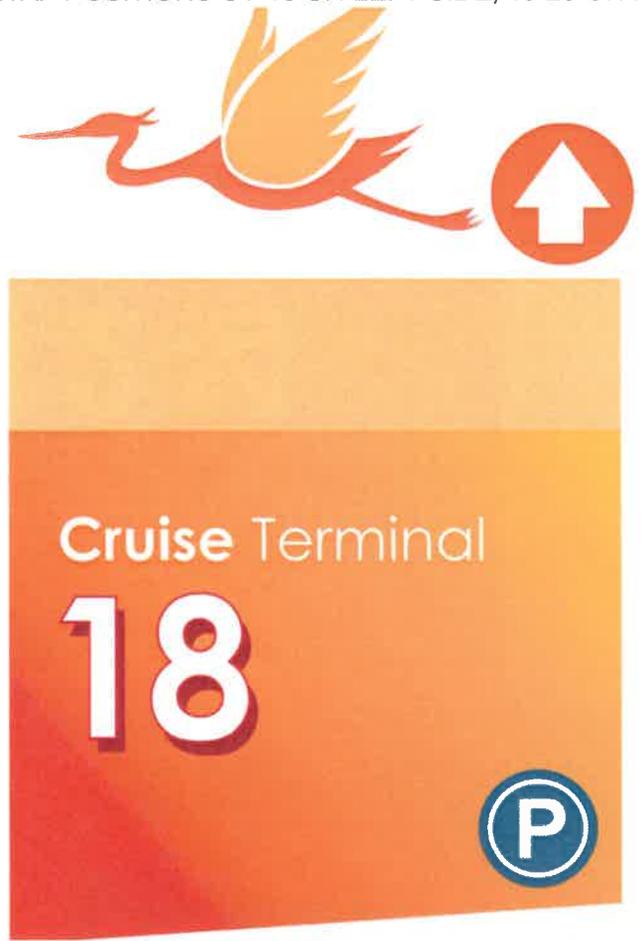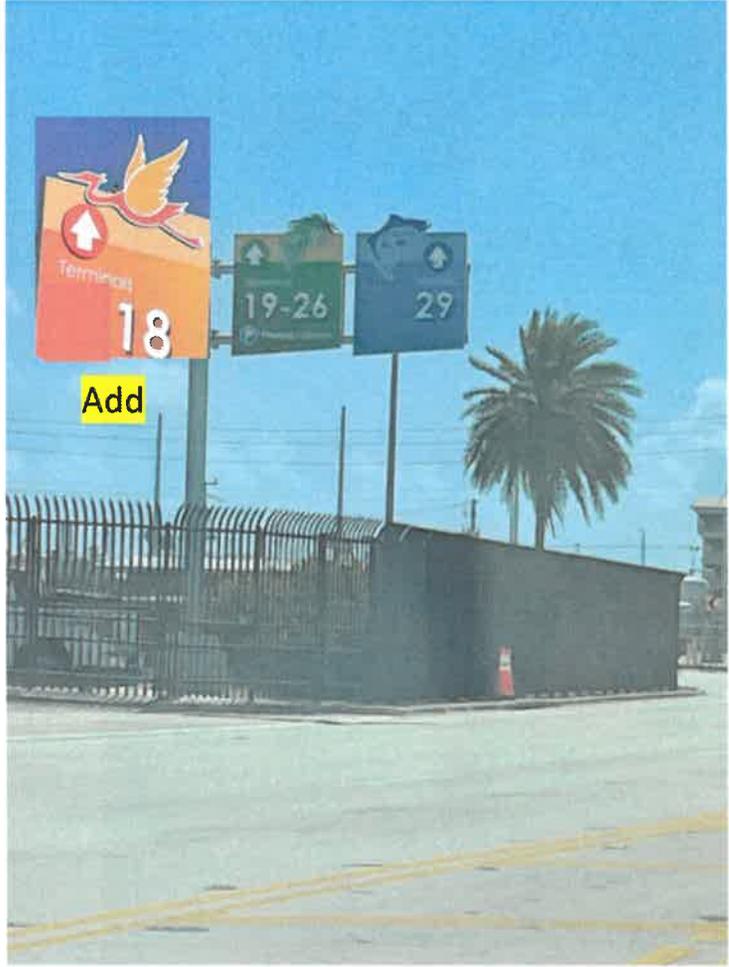



MODS TO BANNER HERON - ADD UP ARROW BOTTOM LEFT




MODS TO BANNER HERON - ADD UP ARROW BOTTOM LEFT





MODS TO FL-D_01- ADD UP "P" BOTTOM RIGHT

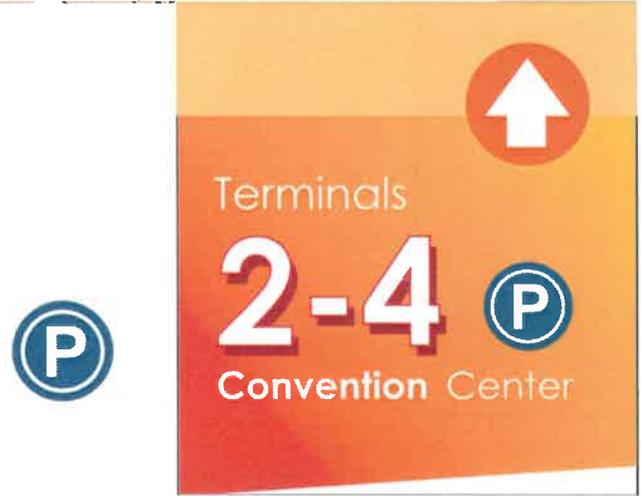



MODS TO BANNER HERON - ADD UP ARROW BOTTOM LEFT



MODS TO FL-C_01 - ADD "P" AS SHOWN -
MOVE PANEL TO 3RD POSITION TO THE
RIGHT



MODS TO BANNER HERON - ADD UP ARROW BOTTOM
LEFT



NEW BANNER HERON - AS SHOWN





Cruise Parking

SUPPLY THIS SIGN, WRONG SIGN WAS PRODUCED, WAS MARKED UP ON SHOP DRAWING No. 2

CORRECTED ON SHOP DRAWINGS No. 5 - FABRICATED WRONG, REPLACE AT NO CHARGE



SIDE A SIDE B

DIR_05



	12266 Homeowner Details Flat Complex	A+	Design - 3	Title - 4 7/8 2018				Sheet 19c
	3901 E. Bay Street Fort Lauderdale, FL 33319							



INSTALL ALREADY FABRICATED DIR PANEL ON TOP OF BARRIER WALL, MODIFY SPARE TWO POST MOUNT FOR IT.



mount on barrier



MODS TO FL-C_01 - ADD "P" AS SHOWN





MODS TO BANNER HERON - ADD UP ARROW BOTTOM LEFT



MODS TO FL-C_02 - ADD "P" AS SHOWN





MODS TO BANNER HERON - ADD RIGHT ARROW BOTTOM LEFT





MODS TO MON-1 - ADD "P" AS SHOWN BELOW





MODS TO BANNER HERON - ADD UP ARROW BOTTOM LEFT





MODS TO BANNER HERON - ADD UP ARROW BOTTOM LEFT





MODS TO BANNER PALM - ADD UP ARROW AND "P" BOTTOM LEFT





MODS TO BANNER HERON - ADD UP ARROW BOTTOM LEFT





NEW DIR T18 U TURN SIGN ON POSTS

FABRICATE NEW SIGN, INSTALL ON SPARE
DOUBLE POST MOUNT


FABRICATE NEW SIGN, INSTALL ON SPARE
3'-2" wide
4'-4" length
3'-11 3/4" length





MODS TO BANNER PALM - ADD UP ARROW AND "P" BOTTOM LEFT




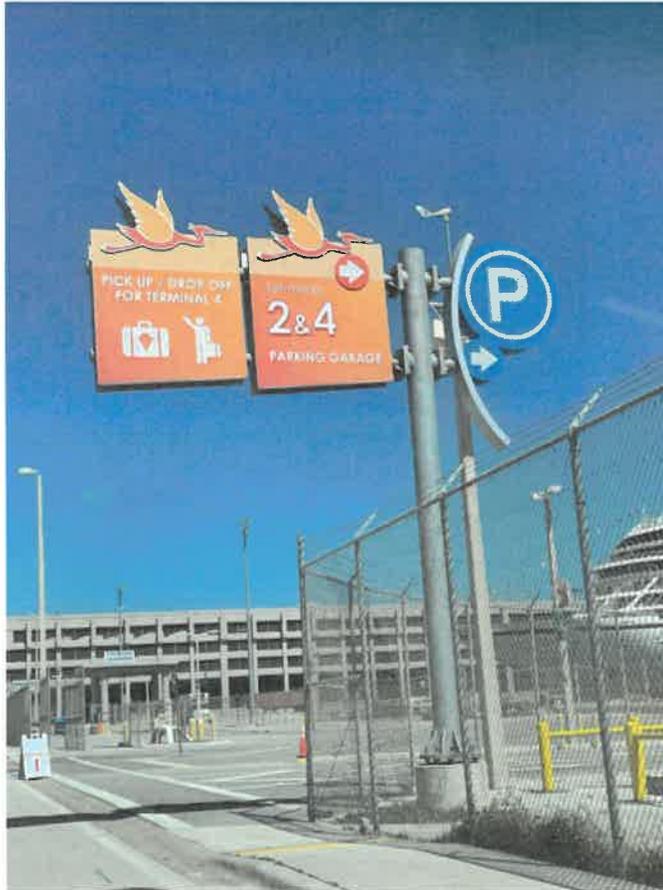


PANEL CHANGES ON EXISTING SIGN ST008 - REVIEW SHOP DRAWINGS AND FIELD VERIFY DIMENSIONS.



LEFT SIDE NEW PANEL, RE-USE RIGHT HANDED HERON, NEW UP ARROW.

RIGHT SIDE NEW PANEL, RE-USE RIGHT HANDED HERON, RE-USE ARROW.

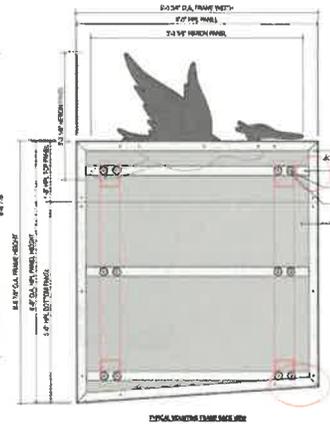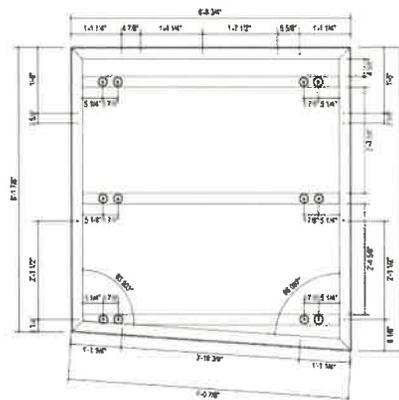

EXISTING SIGN DIMENSIONS
VERIFY ON THE FIELD



PANEL FACE CHANGES ON EXISTING SIGN ST008 -
REVIEW SHOP DRAWINGS AND FIELD VERIFY
DIMENSIONS.




LEFT SIDE NEW
PANEL, RE-USE LEFT
HANDED HERON,
RE-USE ARROW.

RIGHT SIDE REMOVE
PANEL -

EXISTING SIGN PANELS (ST010.1) OVER CANOPY HERON GARAGE EXIT
REVIEW SHOP DRAWINGS AND DO THE FOLLOWING CHANGES:

EXISTING SIGN PANELS AND ICONS

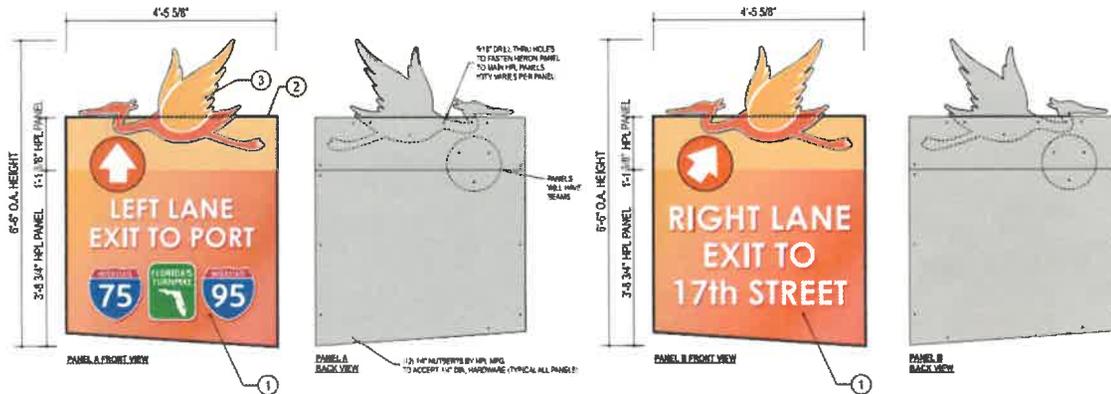

LEFT SIGN PANEL -
COVER I-75 WITH I-595
ADHESIVE SIGN


RIGHT SIGN PANEL - REPLACE
HERON WITH RIGHT SIDED HERON,
RELOCATE ARROW TO THE RIGHT
SIDE OF THE FACE PANEL



14" X 14"

Panel A Heron Detail

Scale: 1/2"=1'-0"

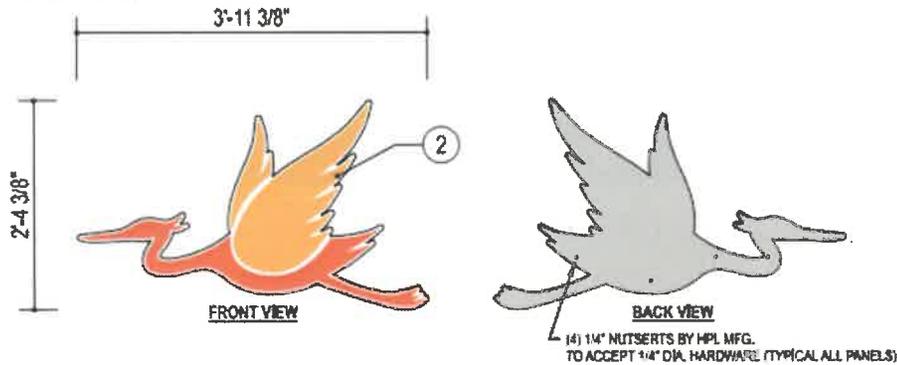

RIGHT HANDED HERON
3'-11 3/8" X 2'-4 3/8"






PANEL CHANGES ON EXISTING SIGN 010 - REVIEW SHOP DRAWINGS AND FIELD VERIFY DIMENSIONS.



Heron Panel Detail

Scale: 3/8"=1'-0"

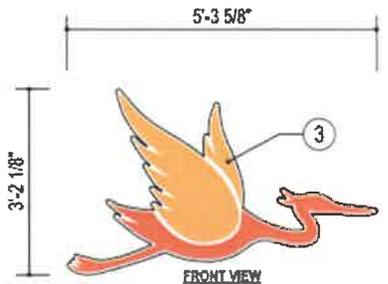

(4) 1/4" NUTSERTS BY HPI, MFG. TO ACCEPT 1/4" DIA. HARDWARE

LEFT PANEL,
COVER I-75
WITH I-595
OVERLAY ADHESIVE
SIGN

RIGHT PANEL,
REPLACE HERON,
WITH RIGHT SIDED
RE-LOCATE ARROW
TO RIGHT SIDE OF
PANEL FACE
