

BOARD OF COUNTY COMMISSIONERS, BROWARD COUNTY, FLORIDA

CHANGE ORDER NO: 5

BOARD REGULAR

Project: - Port Everglades Wayfinding Sign Project

Contract: PNC2117560C1 Vend: HORSEPOWER ELECTRIC INC

The following changes are hereby authorized upon approval of the Board and his/her signature below.

Description of Changes, Reasons Therefore, and Cost and/or Time Changes For Each:

Cost Basis: Negotiated Lump Sum

	<u>AMOUNT</u>	<u>TIME</u>
ORIGINAL CONTRACT	\$3,631,302.65	275
PREV APPROVED CHANGE ORDERS	\$532,199.74	973
THIS CHANGE ORDER NO. 5	\$259,555.27	0
REVISED CONTRACT AMOUNT	\$4,423,057.66	1248
PENDING CHANGE ORDERS	\$259,555.27	0

	<u>Current</u>	<u>- Apprvd CO</u>	<u>- This CO</u>	<u>= Remaining</u>
Admin Allowance	5.00	4.72		0.28
Board Allowance	17.09	9.94	7.15	0.00
Total Allowance	22.09	21.80	7.15	0.28

INCREASE CONTRACT AMOUNT BY \$259,555.27

NO CHANGE IN CONTRACT PERIOD

COPY FOR: MINUTES, CONTRACTOR, PURCHASING, CONSULTANT, SUPERVISING AGENCY, BUDGET, DEPARTMENT

2/13/2024

Percentages may not total exactly, due to rounding

Source: ContractsCentral - A Service Of The Purchasing Division

BOARD OF COUNTY COMMISSIONERS, BROWARD COUNTY, FLORIDA
CHANGE ORDER NO: 5
BOARD REGULAR

Project: - Port Everglades Wayfinding Sign Project
Contract: PNC2117560C1 Vend: HORSEPOWER ELECTRIC INC

The following changes are hereby authorized upon approval of the Board and his/her signature below.
Description of Changes, Reasons Therefore, and Cost and/or Time Changes for each:
Cost Basis: Negotiated Lump Sum

Line Nbr.1	USER REQUESTED ENHANCEMENTS	\$6,080.00	0
Description : New Item PNC211560C1--01-65 - Provide all labor, equipment and material to relocate Snook sign from FL-B_06 to FL-B_01. Quantity of one (1) at a unit price of \$6,080.000 each, for a line item total of 6,080.00 increase to the contract. Reason : Additional enhancements were requested by the end user to improve visitors overall experience. Cause : User requested scope			
Line Nbr.2	USER REQUESTED ENHANCEMENTS	\$68,781.84	0
Description : New Item PNC211560C1--01-66 - Furnish and install DIG 1 Heron 8 feet wide icons on HPL. Quantity of three (3) at a unit price of \$22,927.28 each, for a line item total of \$68,781.84 increase to the contract. Reason : Additional enhancements were requested by the end user to improve visitors overall experience. Cause : User requested scope			
Line Nbr.3	USER REQUESTED ENHANCEMENTS	\$35,070.24	0
Description : New Item PNC211560C1--01-67 - Furnish and install DIG 1 Palm 6 feet wide icons on HPL. Quantity of two (2) at a unit price of \$17,535.12 each, for a line item total of \$35,070.24 increase to the contract Reason : Additional enhancements were requested by the end user to improve visitors overall experience. Cause : User requested scope			
Line Nbr.4	USER REQUESTED ENHANCEMENTS	\$13,760.00	0
Description : New Item PNC211560C1--01-68 - Furnish and install FL-C_04 2-18 Heron Sign HPL panel on Eller Drive. Quantity of one (1) at a unit price of \$13,760.00 each, and an increase to the contract amount of \$13,760.00. Reason : Additional enhancements were requested by the end user to improve visitors overall experience. Cause : User requested scope			
Line Nbr.5	USER REQUESTED ENHANCEMENTS	\$13,760.00	0
Description : New Item PNC211560C1--01-69 - Furnish and install FL-C_06 2-4 Heron Sign HPL panel on Eisenhower. Quantity of one (1) at a unit price of \$13,760 each, and an increase to the contract amount of \$13,760.00 Reason : Additional enhancements were requested by the end user to improve visitors overall experience. Cause : User requested scope			

COPY FOR: MINUTES, CONTRACTOR, PURCHASING, CONSULTANT, SUPERVISING AGENCY, BUDGET, DEPARTMENT

2/28/2024

Percentages may not total exactly, due to rounding

Source: ContractsCentral

BOARD OF COUNTY COMMISSIONERS, BROWARD COUNTY, FLORIDA

CHANGE ORDER NO: 5

BOARD REGULAR

Project: - Port Everglades Wayfinding Sign Project

Contract: PNC2117560C1 Vend: HORSEPOWER ELECTRIC INC

The following changes are hereby authorized upon approval of the Board and his/her signature below.

Description of Changes, Reasons Therefore, and Cost and/or Time Changes for each:

Cost Basis: Negotiated Lump Sum

Line Nbr.6	USER REQUESTED ENHANCEMENTS	\$17,604.54	0
Description : New Item PNC211560C1--01-71 - Furnish and install DIR type Parking lot A double sided signs on Eller Drive. Quantity of one (1) at a unit price of \$17,760.54 each, and an increase to the contract amount of \$17,604.54 Reason : Additional enhancements were requested by the end user to improve visitors overall experience. Cause : User requested scope			
Line Nbr.7	USER REQUESTED ENHANCEMENTS	\$17,604.54	0
Description : New Item PNC211560C1--01-72 - Furnish and install DIR type Parking lot B and C single sided signs on SE 19th Avenue and on Terminal 18 respectively. Quantity of two (2) at a unit price of \$8,802.27 each, and an increase to the contract amount of \$17,604.54 Reason : Additional enhancements were requested by the end user to improve visitors overall experience. Cause : User requested scope			
Line Nbr.8	USER REQUESTED ENHANCEMENTS	\$9,542.11	0
Description : New Item PNC211560C1--01-73 - Furnish and install DIR type Parking lot B 52" x 38" single sided sign on SE 19th Avenue. Quantity of one (1) at a unit price of \$9,542.11 each, and an increase to the contract amount of \$9,542.11 Reason : Additional enhancements were requested by the end user to improve visitors overall experience. Cause : User requested scope			
Line Nbr.9	USER REQUESTED ENHANCEMENTS	\$19,672.00	0
Description : New Item PNC211560C1--01-74 - Furnish and install FL-B_06 Metal Frame, left orientation. Quantity of one (1) at a unit price of \$19,672 each, and an increase to the contract amount of \$19,672.00 Reason : Additional enhancements were requested by the end user to improve visitors overall experience. Cause : User requested scope			

BOARD OF COUNTY COMMISSIONERS, BROWARD COUNTY, FLORIDA

CHANGE ORDER NO: 5

BOARD REGULAR

Project: - Port Everglades Wayfinding Sign Project

Contract: PNC2117560C1 Vend: HORSEPOWER ELECTRIC INC

The following changes are hereby authorized upon approval of the Board and his/her signature below.

Description of Changes, Reasons Therefore, and Cost and/or Time Changes for each:

Cost Basis: Negotiated Lump Sum

Line Nbr.10	USER REQUESTED ENHANCEMENTS	\$7,680.00	0
Description : New Item PNC211560C1--01-75 - Furnish and install Modifications to Sign Metal Frame to enable double sided installation. Quantity of two (2) at a unit price of \$3,840.00 each, and an increase to the contract amount of \$7,680.00 Reason : Additional enhancements were requested by the end user to improve visitors overall experience. Cause : User requested scope			
Line Nbr.11	USER REQUESTED ENHANCEMENTS	\$50,000.00	0
Description : New Item PNC211560C1-01-76- Furnish and install necessary labor and materials when directed by Port, repair damaged signs, or in case of replacement; replace in kind based on project specifications. Allowance item in the sum of \$50,000 and increase to the contract amount of \$50,000. Reason : Signs have been hit by vehicular traffic prompting repairs or replacement. Cause : User requested scope.			
Total Change Order		\$259,555.27	0

PURCHASING INFORMATION			
PO : PO SEA2400004			
Original Award :	Approved Amendments :	Approved COs :	Previous Revised :
\$3,631,302.65	\$0.00	\$532,199.74	\$4,163,502.39
275 Days	0 Days	973 Days	1248 Days
This REGULAR Change Order: INCREASE \$259,555.27 NO TIME CHANGE			
New Revised Contract: \$4,423,057.66 1248 Days			

COPY FOR: MINUTES, CONTRACTOR, PURCHASING, CONSULTANT, SUPERVISING AGENCY, BUDGET, DEPARTMENT

2/28/2024

Percentages may not total exactly, due to rounding

Source: ContractsCentral



BOARD OF COUNTY COMMISSIONERS, BROWARD COUNTY, FLORIDA
CHANGE ORDER NO: 5
BOARD REGULAR


Project: - Port Everglades Wayfinding Sign Project
Contract: PNC2117560C1 Vend: HORSEPOWER ELECTRIC INC


The following changes are hereby authorized upon approval of the Board and his/her signature below.

Description of Changes, Reasons Therefore, and Cost and/or Time Changes For Each:

Cost Basis: Negotiated Lump Sum

<u>No Consultant</u>	
Signature: 	<u>Accepted By Contractor</u>
Name: Michael Martinez	Date: 02/19/2024
HORSEPOWER ELECTRIC INC Representative	
<u>Recommended By PORT EVERGLADES -SEAPORT ENGINEERING & CONSTRUCTION DIVISION Project Manager</u>	
Signature: 	Date: 2/20/2024
Claude Gentil	

<u>Recommended By PORT EVERGLADES -SEAPORT ENGINEERING & CONSTRUCTION DIVISION Contract Administrator</u>	
Signature: 	Date: 2/28/2024
John Foglesong Division Director	

<u>Recommended By Port Everglades Department Director</u>	
Signature: 	Date: 2/28/2024
Jonathan Daniels, Department Director GLENN A WILTSHIRE , ACTING DERECTOR	

<u>Approved By Broward County Board Of County Commissioners</u>	
Signature:	Date:
Name:	
Name:	

COPY FOR: MINUTES, CONTRACTOR, PURCHASING, CONSULTANT, SUPERVISING AGENCY, BUDGET, DEPARTMENT

2/13/2024

Percentages may not total exactly, due to rounding

Source: ContractsCentral - A Service Of The Purchasing Division

Horsepower Electric, Inc. 8105 W 20 Avenue 305-819-4060					
Job Description Wayfinding Job Location Port Everglades Client: Port Everglades					Date 12/14/2023
Please accept our proposal to provide labor, material & equipment for the following work descriptions.					
Item No.	Description	Unit	Qty	Unit Price	Total
1	Relocation of FL-B 06 Snook T29 to New Location (Left Orientation)	EA	1	\$ 6,080.00	\$ 6,080.00
2	Fabrication of FL-B 06 Metals (Left Orientation)	EA	1	\$ 19,672.00	\$ 19,672.00
3	DIG 1 Heron Icons F&I	EA	3	\$ 22,927.28	\$ 68,781.84
4	DIG 1 Palm Icons F&I	EA	2	\$ 17,535.12	\$ 35,070.24
5	FL-C 04 F&I 2-18 Heron Sign Panel only at Eller Drive (Left Orientation)	EA	1	\$ 13,760.00	\$ 13,760.00
6	FL-B 06 F&I Heron Panels Only at Eisenhower (Right Orientation)	EA	1	\$ 13,760.00	\$ 13,760.00
7	Parking Lot A F&I Complete Palm Themed Double Sided Sign 42X34 - Eller	EA	1	\$ 17,604.54	\$ 17,604.54
8	Parking Lot B F&I Complete Palm Themed Single Sided Sign 42X34 - SE 19 Ave	EA	1	\$ 8,802.27	\$ 8,802.27
9	Parking Lot B F&I Complete Palm Themed Single Sided Sign 52x38 on Back of Existing	EA	1	\$ 9,542.11	\$ 9,542.11
10	Parking Lot C F&I Complete Heron Themed Single Sided Sign 42X34 installation in sidewalk	EA	1	\$ 8,802.27	\$ 8,802.27
11	Modification of Existing Structures to Accommodate Double Signs	EA	2	\$ 3,840.00	\$ 7,680.00
				Subtotal	\$ 209,555.28
Terms and Conditions					
Price Includes Furnish and installation of sign panels					
				Total	\$ 209,555.28
All material is guaranteed to be as specified. All work to be completed in a workmanlike manner according to standard practice. Any alteration or derivation from above specifications involving extra costs will be executed only upon written orders, and will become an extra charge over and above the estimate. All agreements contingents upon strikes, accidents or delays beyond our control. Owner to carry fire, tornado and other necessary insurance. Our workers are fully covered by Workmen's Compensation insurance.				AUTHORIZED SIGNATURE Note: This proposal may be withdrawn by us if not accepted within 30 days.	
Acceptance of proposal - The above prices, specifications and conditions are satisfactory and are hereby accepted. You are authorized to do work as specified. Payment will be made as outlined above. Service agreement terms to follow.					
DATE OF ACCEPTANCE:					

CHANGE ORDER NO. 5 WORK ITEMS



Port Everglades

Wayfinding Design Intent Document

rev. June 19, 2018

COORDINATED
WITH OTHER
PROJECTS AND SITE
CONDITIONS
8.21.2020




FINAL LOCATION PLANS



Change Order No. 5 Pay Items

Item 2, PNC211560C1-01-66 - Furnish and install DIG 1 Heron 8 feet wide icons on high pressure laminate (HPL)
Qty 2 this page mount on Heron Garage top of Stair Case.

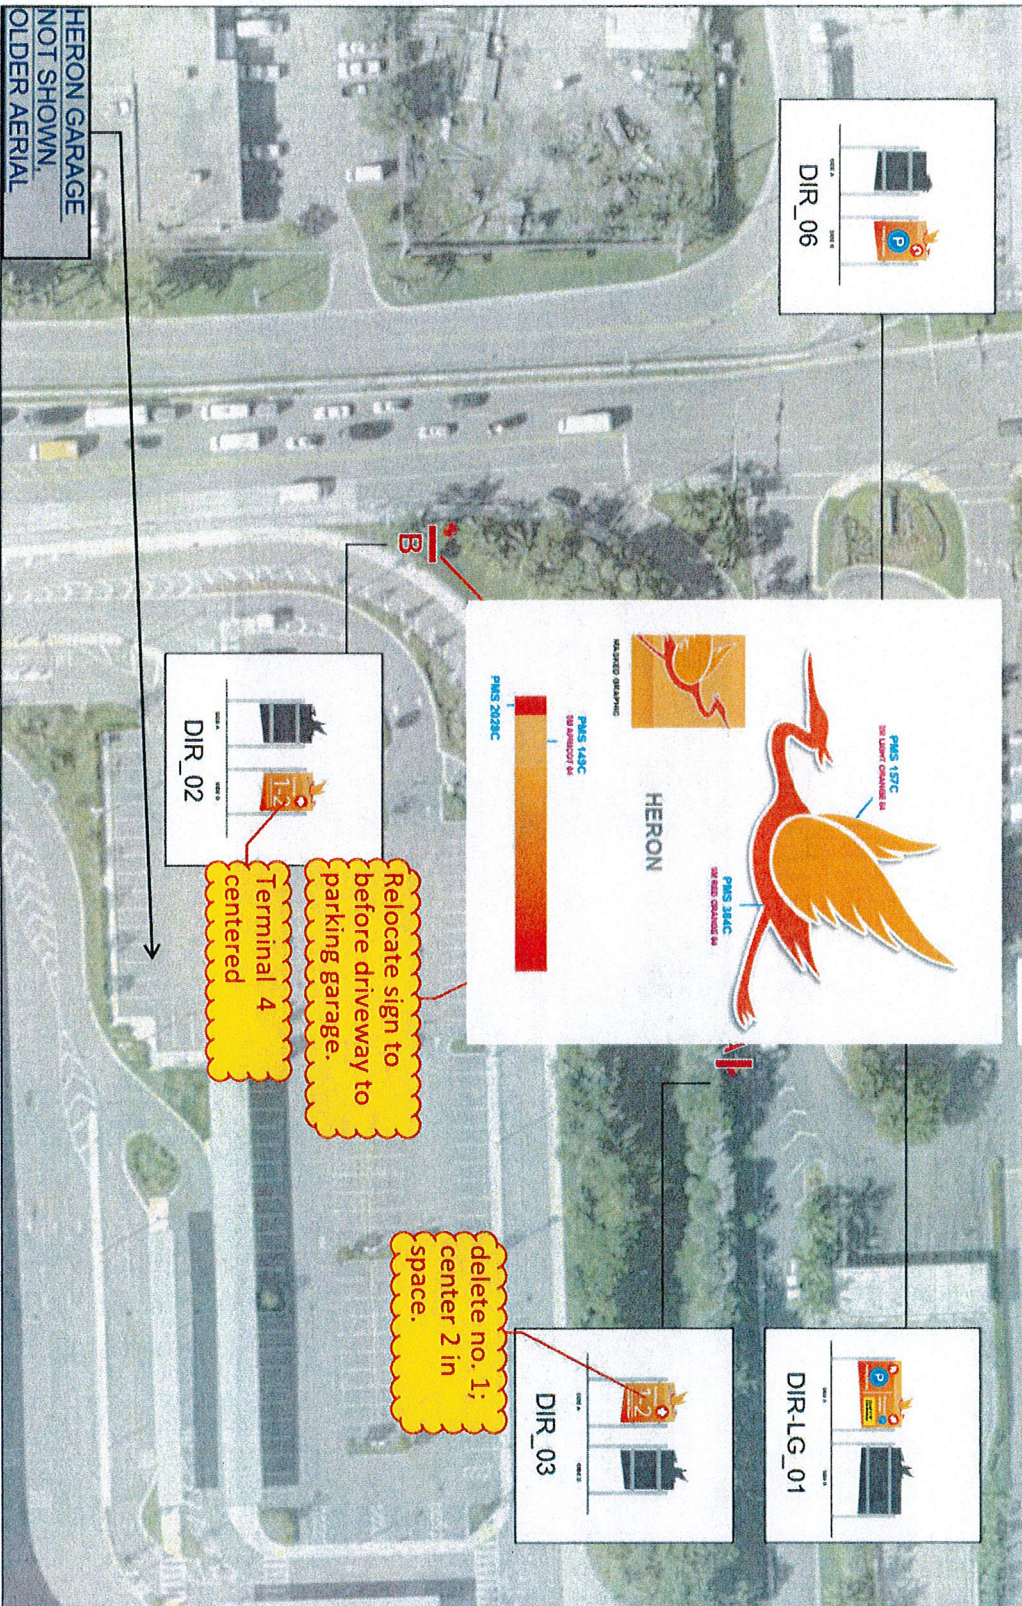


Change Order No. 5 Pay Items

Item 1 PNC211560C1--01-65 Relocate Snook Sign from FL-B_06 To FL-B_01 -Damaged Sign. QTY 1

Item 9 PNC211560C1--01-74 Furnish new metal frame and backing panel to enable relocation -Damaged Sign. QTY 1

Item 5 PNC211560C1--01-69 - Furnish and install FL-C_06 2-4 Heron Sign HPL panel on Eisenhower, QTY 1

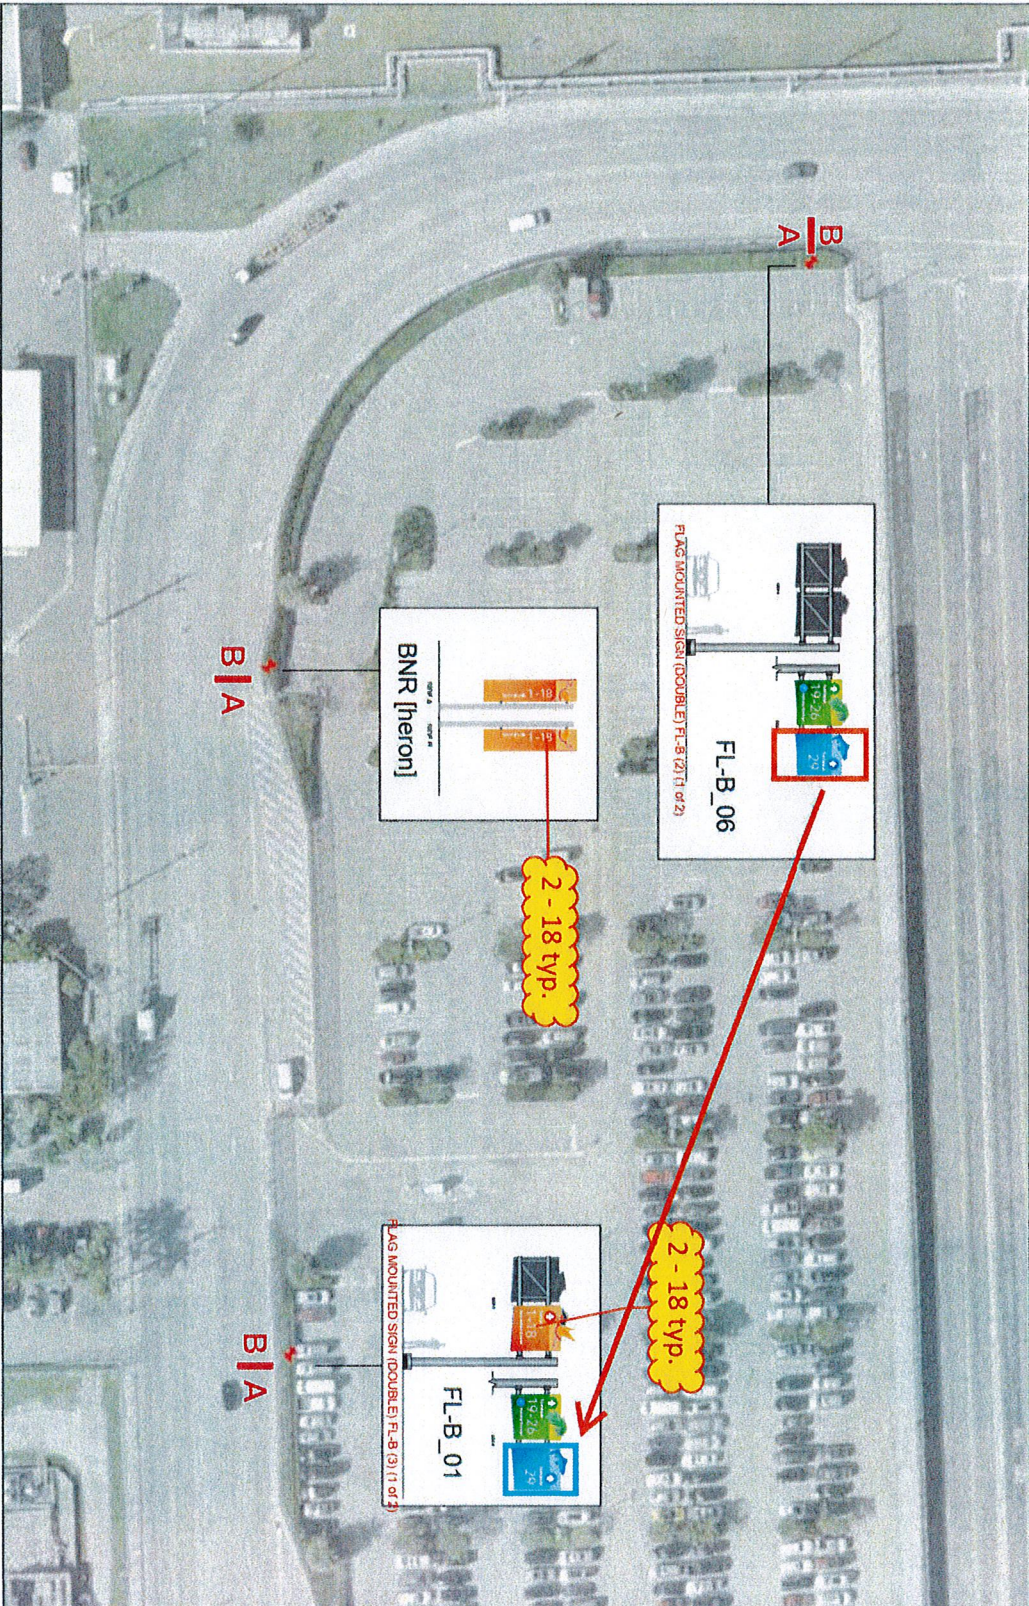

HOLLYWOOD

Change Order No. 5 Pay Items
Item 7 Furnish and install DIR type Parking lot B and C single sided signs on SE 19th Avenue and on Terminal 18 respectively QTY 1, this page.



Item 8 PNC211560C1--01-73 - Furnish and install DIR type Parking lot B 52" x 38" single sided sign on SE 19th Avenue. Qty of one (1)

Item 10 PNC211560C1--01-75 - Furnish and install Modifications to Sign Metal Frame to enable double sided installation. Qty of one (1) this page.




Change Order No. 5 Pay Items

- Item 6, PNC211560C1--01-71 - Furnish and install DIR type Parking lot A double sided signs on Eller Drive. Qty of one (1)
- Item 10 PNC211560C1--01-75 - Furnish and install Modifications to Sign Metal Frame to enable double sided installation. Qty of one (1) this page.



Change Order No. 5 Pay Items


Item 3, Item PNC211560C1-01-67 - Furnish and install DIG 1 Palm 6 feet wide icons on HPL City of two (2) this page mount on Palm Garage South Fascia Corners.

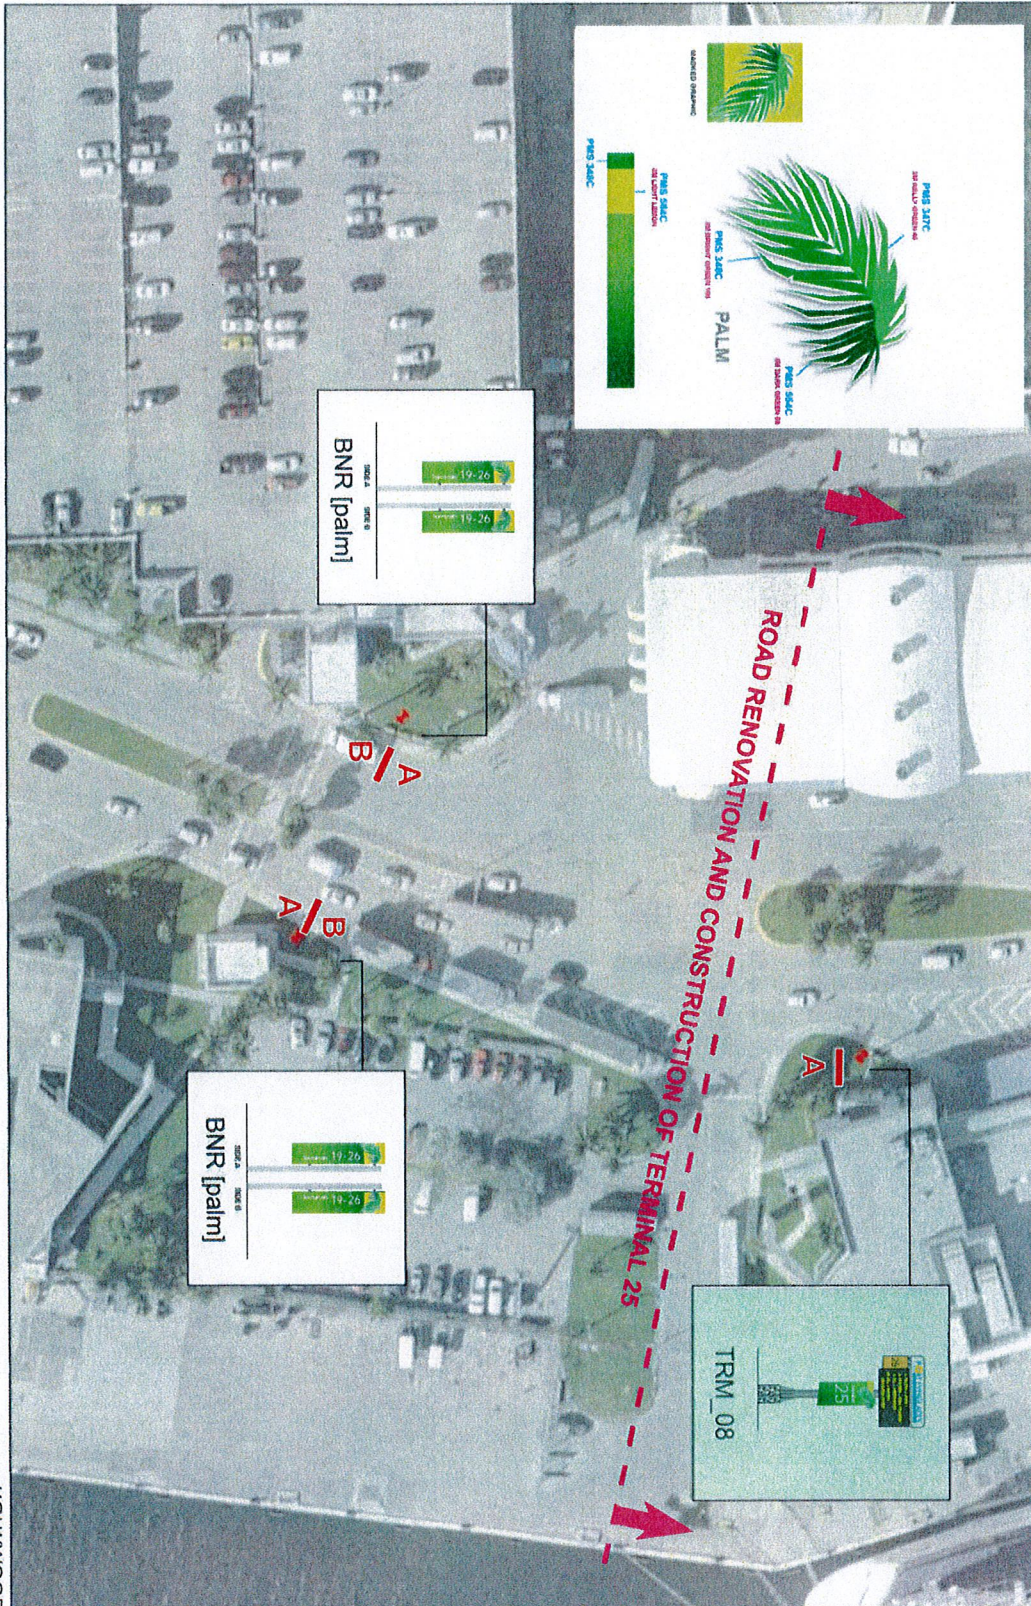

Change Order No. 5 Pay Items

Item 2, PNC211560C1--01-66 - Furnish and install DIG 1 Heron 8 feet wide icons on high pressure laminate (HPL) - Qty of one (1) this page mount on Heron sign DIG_01.

Item 4, PNC211560C1--01-68 - Furnish and install FL-C_04 2-18 Heron Sign HPL panel on Eller Drive. - Qty of one (1) this page mount on existing FL-C_04 structure.
Damaged sign.

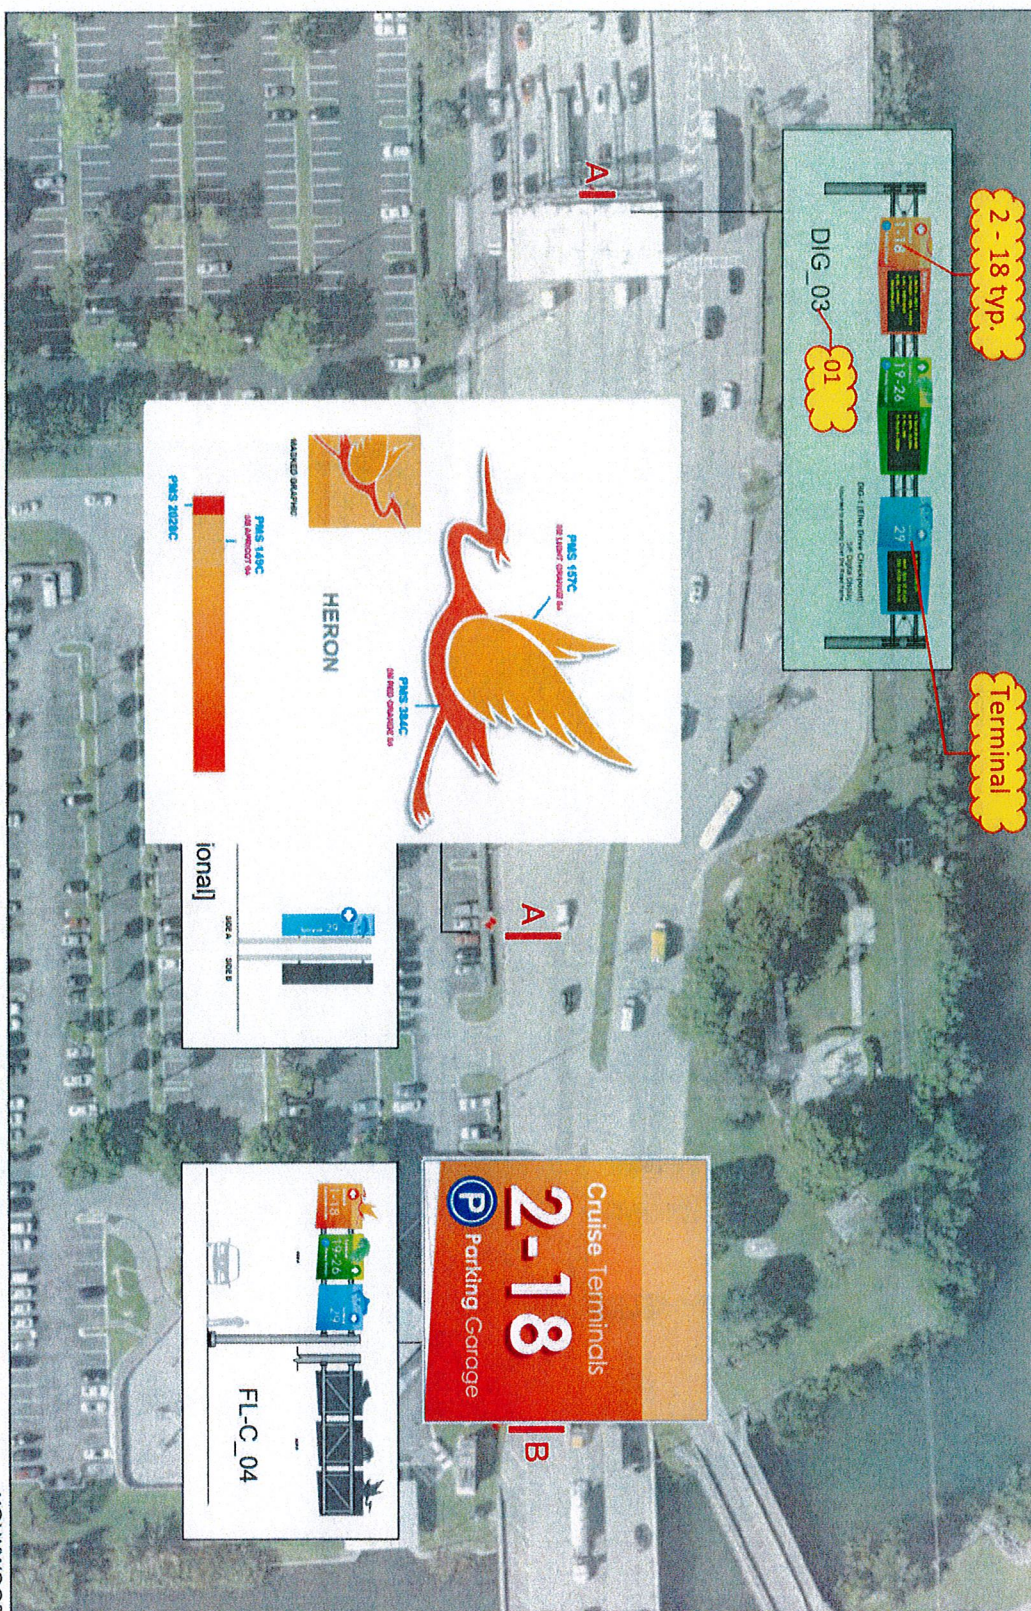

ELLER DRIVE CHECKPOINT - SECTION 20

PORT EVERGLADES : DESIGN INTENT DOCUMENT FINAL 06.19.18
