

BOARD OF COUNTY COMMISSIONERS, BROWARD COUNTY, FLORIDA

CHANGE ORDER NO: 5

BOARD REGULAR

Project: - Port Everglades Wayfinding Sign Project

Contract: PNC2117560C1 Vend: HORSEPOWER ELECTRIC INC

The following changes are hereby authorized upon approval of the Board and his/her signature below.

Description of Changes, Reasons Therefore, and Cost and/or Time Changes For Each:

Cost Basis: Negotiated Lump Sum

	<u>AMOUNT</u>	<u>TIME</u>
ORIGINAL CONTRACT	\$3,631,302.65	275
PREV APPROVED CHANGE ORDERS	\$532,199.74	973
THIS CHANGE ORDER NO. 5	\$259,555.27	0
REVISED CONTRACT AMOUNT	\$4,423,057.66	1248
PENDING CHANGE ORDERS	\$259,555.27	0

	<u>Current</u>	<u>- Apprvd CO</u>	<u>- This CO</u>	<u>= Remaining</u>
Admin Allowance	5.00	4.72		0.28
Board Allowance	17.09	9.94	7.15	0.00
Total Allowance	22.09	21.80	7.15	0.28

INCREASE CONTRACT AMOUNT BY \$259,555.27

NO CHANGE IN CONTRACT PERIOD

COPY FOR: MINUTES, CONTRACTOR, PURCHASING, CONSULTANT, SUPERVISING AGENCY, BUDGET, DEPARTMENT

2/13/2024

Percentages may not total exactly, due to rounding

Source: ContractsCentral - A Service Of The Purchasing Division

BOARD OF COUNTY COMMISSIONERS, BROWARD COUNTY, FLORIDA
CHANGE ORDER NO: 5
BOARD REGULAR

Project: - Port Everglades Wayfinding Sign Project
Contract: PNC2117560C1 Vend: HORSEPOWER ELECTRIC INC

The following changes are hereby authorized upon approval of the Board and his/her signature below.
 Description of Changes, Reasons Therefore, and Cost and/or Time Changes for each:
 Cost Basis: Negotiated Lump Sum

Line Nbr.1	USER REQUESTED ENHANCEMENTS	\$6,080.00	0
Description :	New Item PNC211560C1--01-65 - Provide all labor, equipment and material to relocate Snook sign from FL-B_06 to FL-B_01. Quantity of one (1) at a unit price of \$6,080.000 each, for a line item total of 6,080.00 increase to the contract.		
Reason :	Additional enhancements were requested by the end user to improve visitors overall experience.		
Cause :	User requested scope		
Line Nbr.2	USER REQUESTED ENHANCEMENTS	\$68,781.84	0
Description :	New Item PNC211560C1--01-66 - Furnish and install DIG 1 Heron 8 feet wide icons on HPL. Quantity of three (3) at a unit price of \$22,927.28 each, for a line item total of \$68,781.84 increase to the contract.		
Reason :	Additional enhancements were requested by the end user to improve visitors overall experience.		
Cause :	User requested scope		
Line Nbr.3	USER REQUESTED ENHANCEMENTS	\$35,070.24	0
Description :	New Item PNC211560C1--01-67 - Furnish and install DIG 1 Palm 6 feet wide icons on HPL. Quantity of two (2) at a unit price of \$17,535.12 each, for a line item total of \$35,070.24 increase to the contract		
Reason :	Additional enhancements were requested by the end user to improve visitors overall experience.		
Cause :	User requested scope		
Line Nbr.4	USER REQUESTED ENHANCEMENTS	\$13,760.00	0
Description :	New Item PNC211560C1--01-68 - Furnish and install FL-C_04 2-18 Heron Sign HPL panel on Eller Drive. Quantity of one (1) at a unit price of \$13,760.00 each, and an increase to the contract amount of \$13,760.00.		
Reason :	Additional enhancements were requested by the end user to improve visitors overall experience.		
Cause :	User requested scope		
Line Nbr.5	USER REQUESTED ENHANCEMENTS	\$13,760.00	0
Description :	New Item PNC211560C1--01-69 - Furnish and install FL-C_06 2-4 Heron Sign HPL panel on Eisenhower. Quantity of one (1) at a unit price of \$13,760 each, and an increase to the contract amount of \$13,760.00		
Reason :	Additional enhancements were requested by the end user to improve visitors overall experience.		
Cause :	User requested scope		

COPY FOR: MINUTES, CONTRACTOR, PURCHASING, CONSULTANT, SUPERVISING AGENCY, BUDGET, DEPARTMENT

2/28/2024

Percentages may not total exactly, due to rounding

Source: ContractsCentral

BOARD OF COUNTY COMMISSIONERS, BROWARD COUNTY, FLORIDA
CHANGE ORDER NO: 5
BOARD REGULAR

Project: - Port Everglades Wayfinding Sign Project
Contract: PNC2117560C1 Vend: HORSEPOWER ELECTRIC INC

The following changes are hereby authorized upon approval of the Board and his/her signature below.
Description of Changes, Reasons Therefore, and Cost and/or Time Changes for each:
Cost Basis: Negotiated Lump Sum

Line Nbr.6	USER REQUESTED ENHANCEMENTS	\$17,604.54	0
Description :	New Item PNC211560C1--01-71 - Furnish and install DIR type Parking lot A double sided signs on Eller Drive. Quantity of one (1) at a unit price of \$17,760.54 each, and an increase to the contract amount of \$17,604.54		
Reason :	Additional enhancements were requested by the end user to improve visitors overall experience.		
Cause :	User requested scope		
Line Nbr.7	USER REQUESTED ENHANCEMENTS	\$17,604.54	0
Description :	New Item PNC211560C1--01-72 - Furnish and install DIR type Parking lot B and C single sided signs on SE 19th Avenue and on Terminal 18 respectively. Quantity of two (2) at a unit price of \$8,802.27 each, and an increase to the contract amount of \$17,604.54		
Reason :	Additional enhancements were requested by the end user to improve visitors overall experience.		
Cause :	User requested scope		
Line Nbr.8	USER REQUESTED ENHANCEMENTS	\$9,542.11	0
Description :	New Item PNC211560C1--01-73 - Furnish and install DIR type Parking lot B 52" x 38" single sided sign on SE 19th Avenue. Quantity of one (1) at a unit price of \$9,542.11 each, and an increase to the contract amount of \$9,542.11		
Reason :	Additional enhancements were requested by the end user to improve visitors overall experience.		
Cause :	User requested scope		
Line Nbr.9	USER REQUESTED ENHANCEMENTS	\$19,672.00	0
Description :	New Item PNC211560C1--01-74 - Furnish and install FL-B_06 Metal Frame, left orientation. Quantity of one (1) at a unit price of \$19,672 each, and an increase to the contract amount of \$19,672.00		
Reason :	Additional enhancements were requested by the end user to improve visitors overall experience.		
Cause :	User requested scope		

BOARD OF COUNTY COMMISSIONERS, BROWARD COUNTY, FLORIDA
CHANGE ORDER NO: 5
BOARD REGULAR

Project: - Port Everglades Wayfinding Sign Project
Contract: PNC2117560C1 Vend: HORSEPOWER ELECTRIC INC

The following changes are hereby authorized upon approval of the Board and his/her signature below.
Description of Changes, Reasons Therefore, and Cost and/or Time Changes for each:
Cost Basis: Negotiated Lump Sum





Line Nbr.10	USER REQUESTED ENHANCEMENTS	\$7,680.00	0
Description : New Item PNC211560C1--01-75 - Furnish and install Modifications to Sign Metal Frame to enable double sided installation. Quantity of two (2) at a unit price of \$3,840.00 each, and an increase to the contract amount of \$7,680.00			
Reason : Additional enhancements were requested by the end user to improve visitors overall experience.			
Cause : User requested scope			
Line Nbr.11	USER REQUESTED ENHANCEMENTS	\$50,000.00	0
Description : New Item PNC211560C1-01-76- Furnish and install necessary labor and materials when directed by Port, repair damaged signs, or in case of replacement; replace in kind based on project specifications. Allowance item in the sum of \$50,000 and increase to the contract amount of \$50,000.			
Reason : Signs have been hit by vehicular traffic prompting repairs or replacement.			
Cause : User requested scope.			
Total Change Order		\$259,555.27	0

PURCHASING INFORMATION			
PO : PO SEA2400004			
Original Award :	Approved Amendments :	Approved COs :	Previous Revised :
\$3,631,302.65	0	4	\$4,163,502.39
275 Days	0 Days	973 Days	1248 Days
This REGULAR Change Order:	INCREASE	\$259,555.27	NO TIME CHANGE
New Revised Contract:		\$4,423,057.66	1248 Days

BOARD OF COUNTY COMMISSIONERS, BROWARD COUNTY, FLORIDA
CHANGE ORDER NO: 5
BOARD REGULAR

Project: - Port Everglades Wayfinding Sign Project
Contract: PNC2117560C1 Vend: HORSEPOWER ELECTRIC INC

The following changes are hereby authorized upon approval of the Board and his/her signature below.
Description of Changes, Reasons Therefore, and Cost and/or Time Changes For Each:
Cost Basis: Negotiated Lump Sum

<u>No Consultant</u>	
<u>Accepted By Contractor</u>	
Signature: 	Date: 02/19/2024
Name: Michael Martinez	
HORSEPOWER ELECTRIC INC Representative	
<u>Recommended By PORT EVERGLADES -SEAPORT ENGINEERING & CONSTRUCTION DIVISION Project Manager</u>	
Signature: 	Date: 2/20/2024
Claude Gentil	
<u>Recommended By PORT EVERGLADES -SEAPORT ENGINEERING & CONSTRUCTION DIVISION Contract Administrator</u>	
Signature: 	Date: 2/28/2024
John Foglesong Division Director	
<u>Recommended By Port Everglades Department Director</u>	
Signature: 	Date: 2/28/2024
Jonathan Daniels, Department Director GLENN A WILTSHIRE , ACTING DIRECTOR	
<u>Approved By Broward County Board Of County Commissioners</u>	
Signature:	Date:
Name:	
Name:	

2-26-24



Port Everglades

Wayfinding Design Intent Document

rev. June 19, 2018

COORDINATED
WITH OTHER
PROJECTS AND SITE
CONDITIONS
8.21.2020




FINAL LOCATION PLANS



Change Order No. 5 Pay Items

Item 2, PNC211560C1-01-66 - Furnish and install DIG 1 Heron 8 feet wide icons on high pressure laminate (HPL)
Qty 2 this page mount on Heron Garage top of Stair Case.

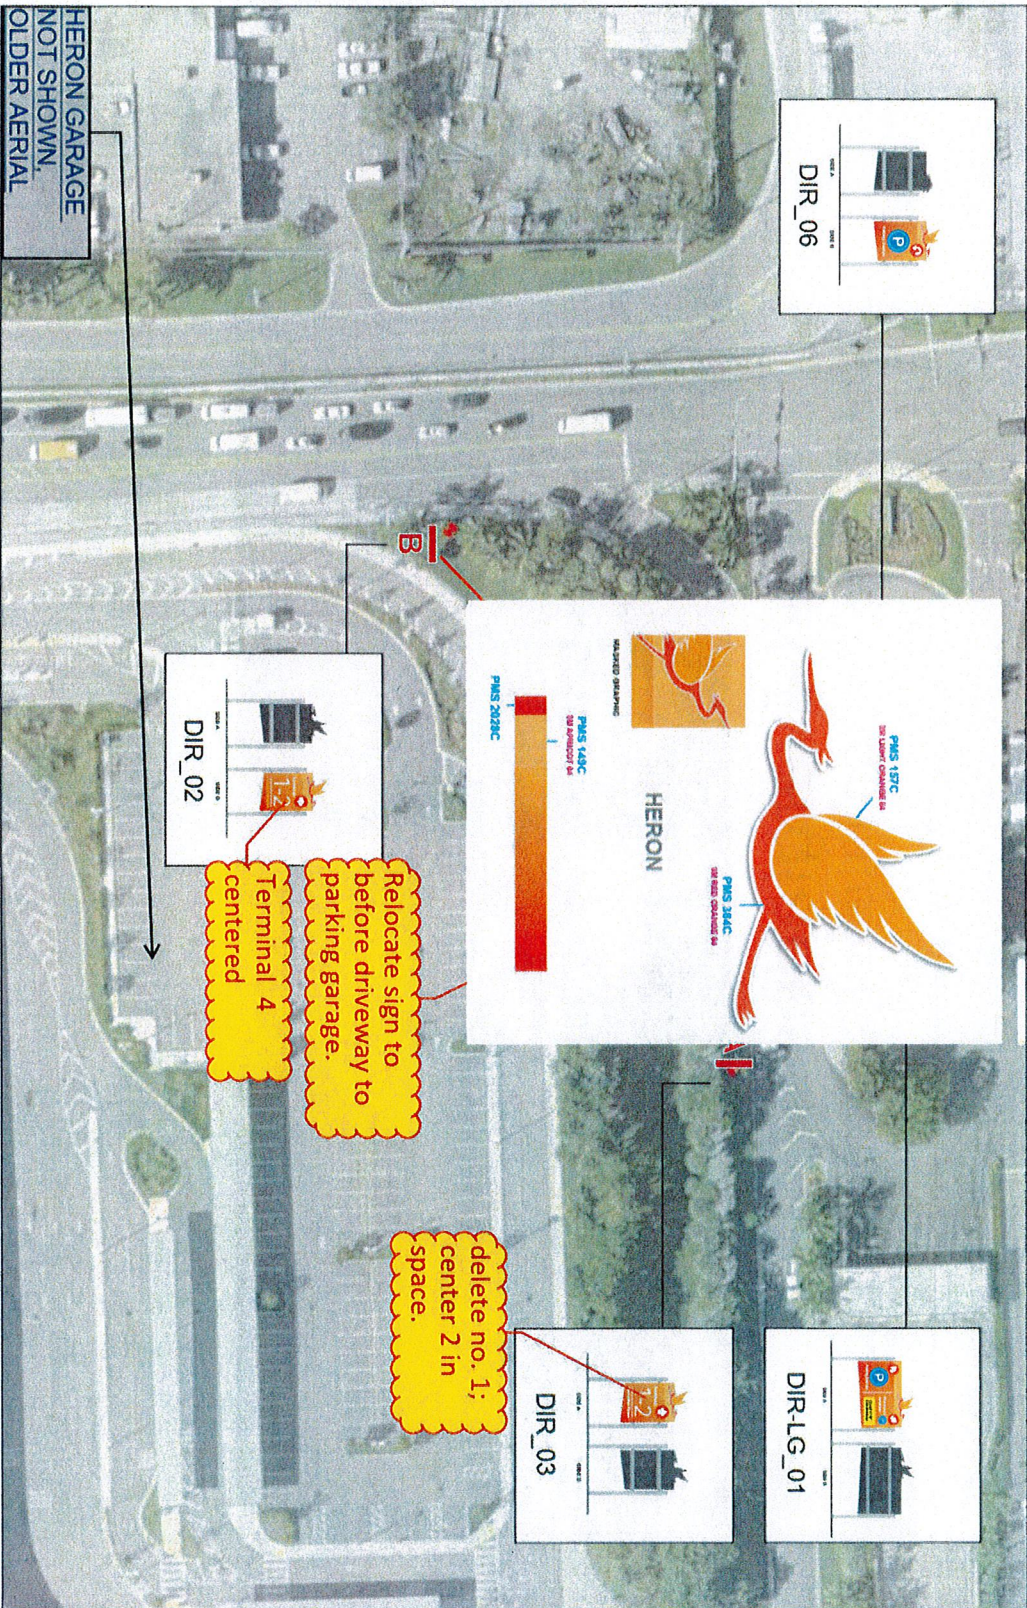

NORTHPORT - SECTION 2


PORT EVERGLADES DESIGN INTENT DOCUMENT FINAL 09.19.18



FT. LAUDERDALE



- Change Order No. 5 Pay Items
- Item 1 PNC211560C1--01-65 Relocate Snook Sign from FL-B_06 To FL-B_01 -Damaged Sign. QTY 1
- Item 9 PNC211560C1--01-74 Furnish new metal frame and backing panel to enable relocation -Damaged Sign. QTY 1
- Item 5 PNC211560C1--01-69 - Furnish and install FL-C_06 2-4 Heron Sign HPL panel on Eisenhower, QTY 1

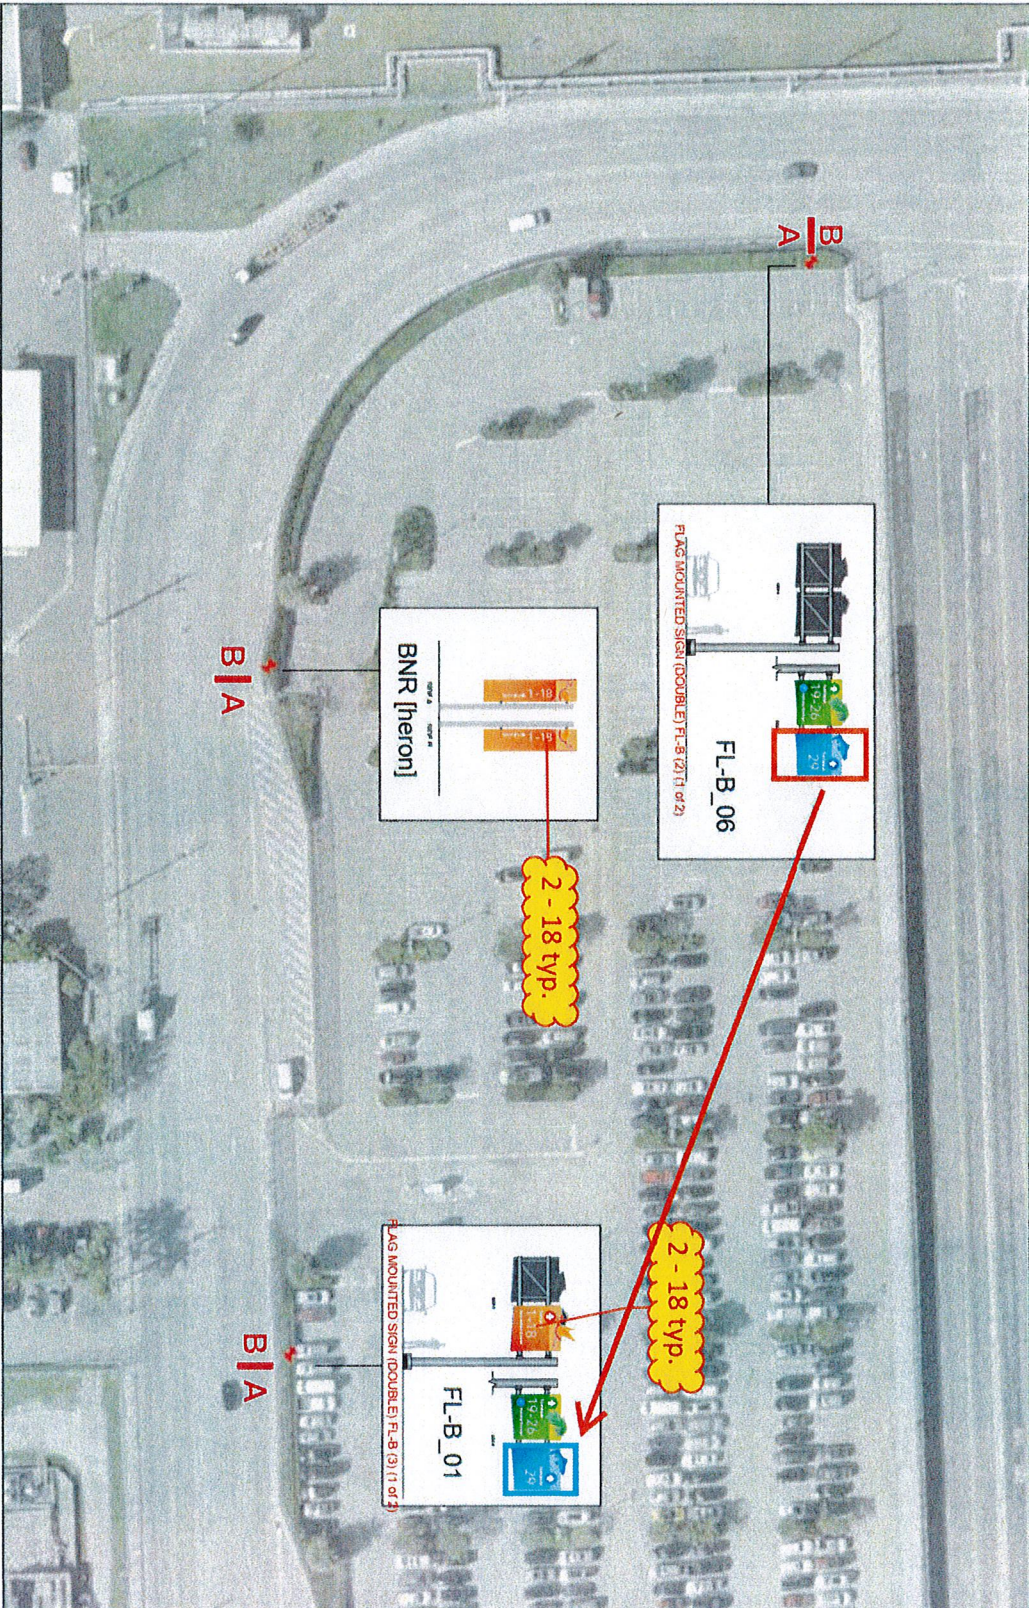


NORTHPORT - SECTION 9

PORT EVERGLADES : DESIGN INTENT DOCUMENT FINAL 06.19.18



Change Order No. 5 Pay Items
Item 7 Furnish and install DIR type Parking lot B and C single sided signs on SE 19th Avenue and on Terminal 18 respectively QTY 1, this page.

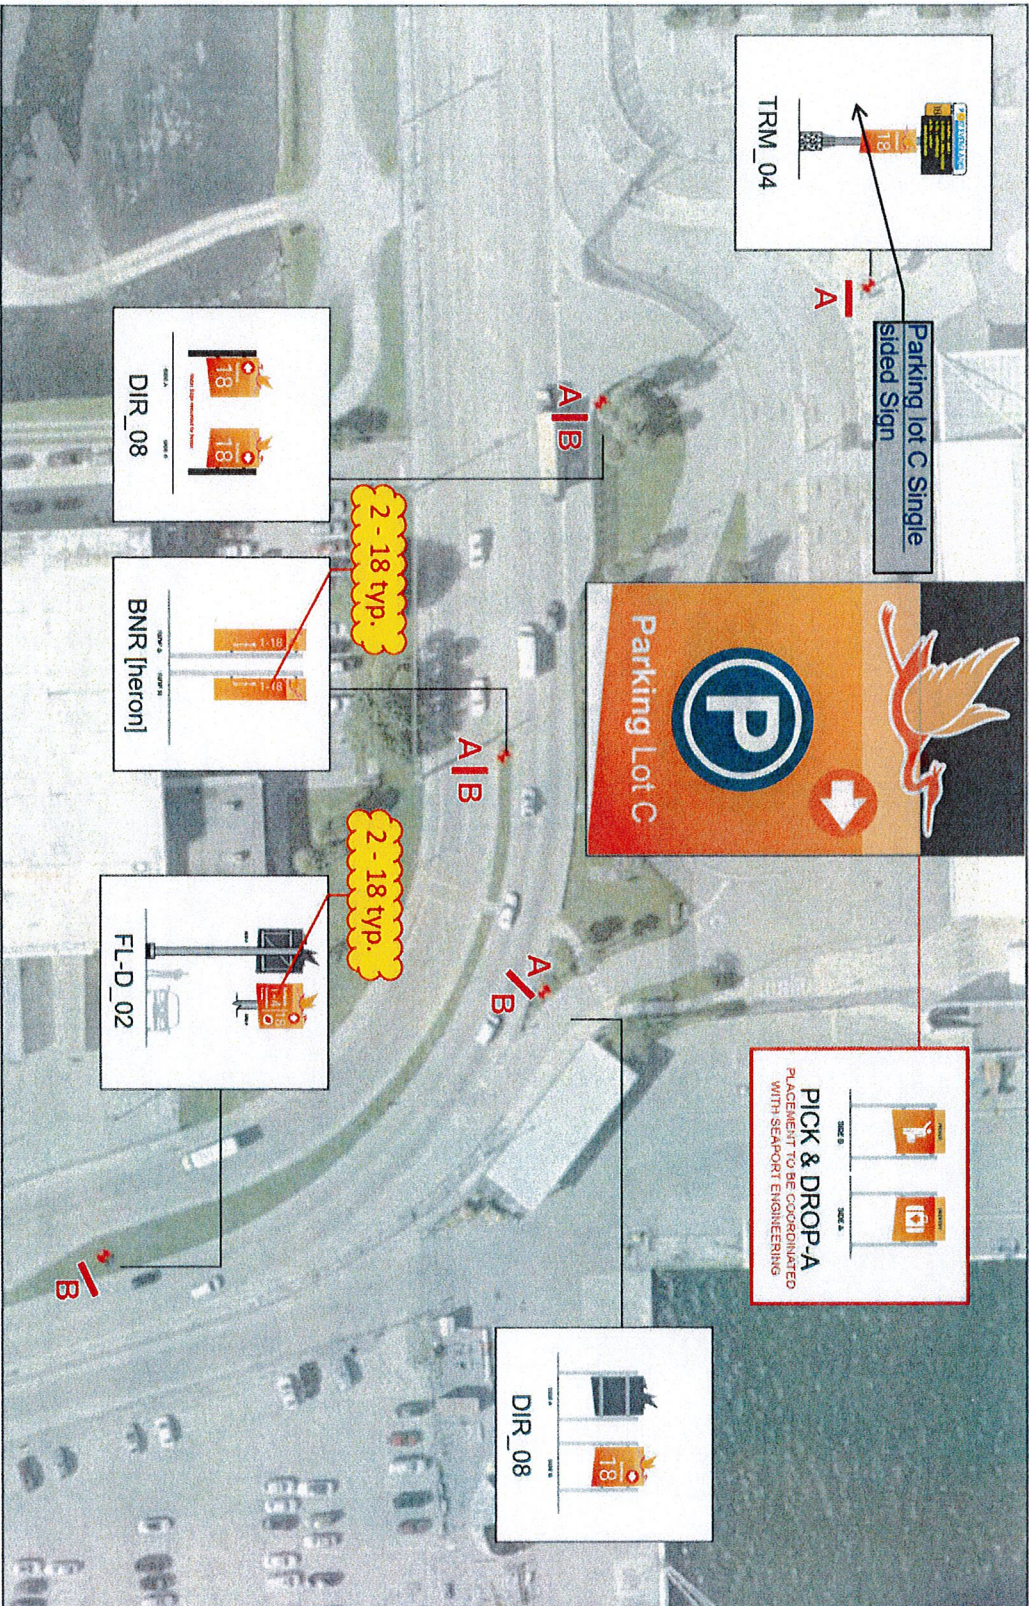

NORTHPORT - SECTION 10



PORT EVERGLADES : DESIGN INTENT DOCUMENT FINAL 08.19.18



Change Order No. 5 Pay Items

- Item 6, PNC211560C1-01-71 - Furnish and install DIR type Parking lot A double sided signs on Eller Drive. Qty of one (1)
- Item 10 PNC211560C1-01-75 - Furnish and install Modifications to Sign Metal Frame to enable double sided installation. Qty of one (1) this page.




MIDPORT - SECTION 16
PORT EVERGLADES DESIGN INTENT DOCUMENT FINAL 08.19.18



Change Order No. 5 Pay Items


Item 3. Item PNC211560C1-01-67 - Furnish and Install DIG 1 Palm 6 feet wide icons on HPL Qty of two (2) this page mount on Palm Garage South Fascia Corners.

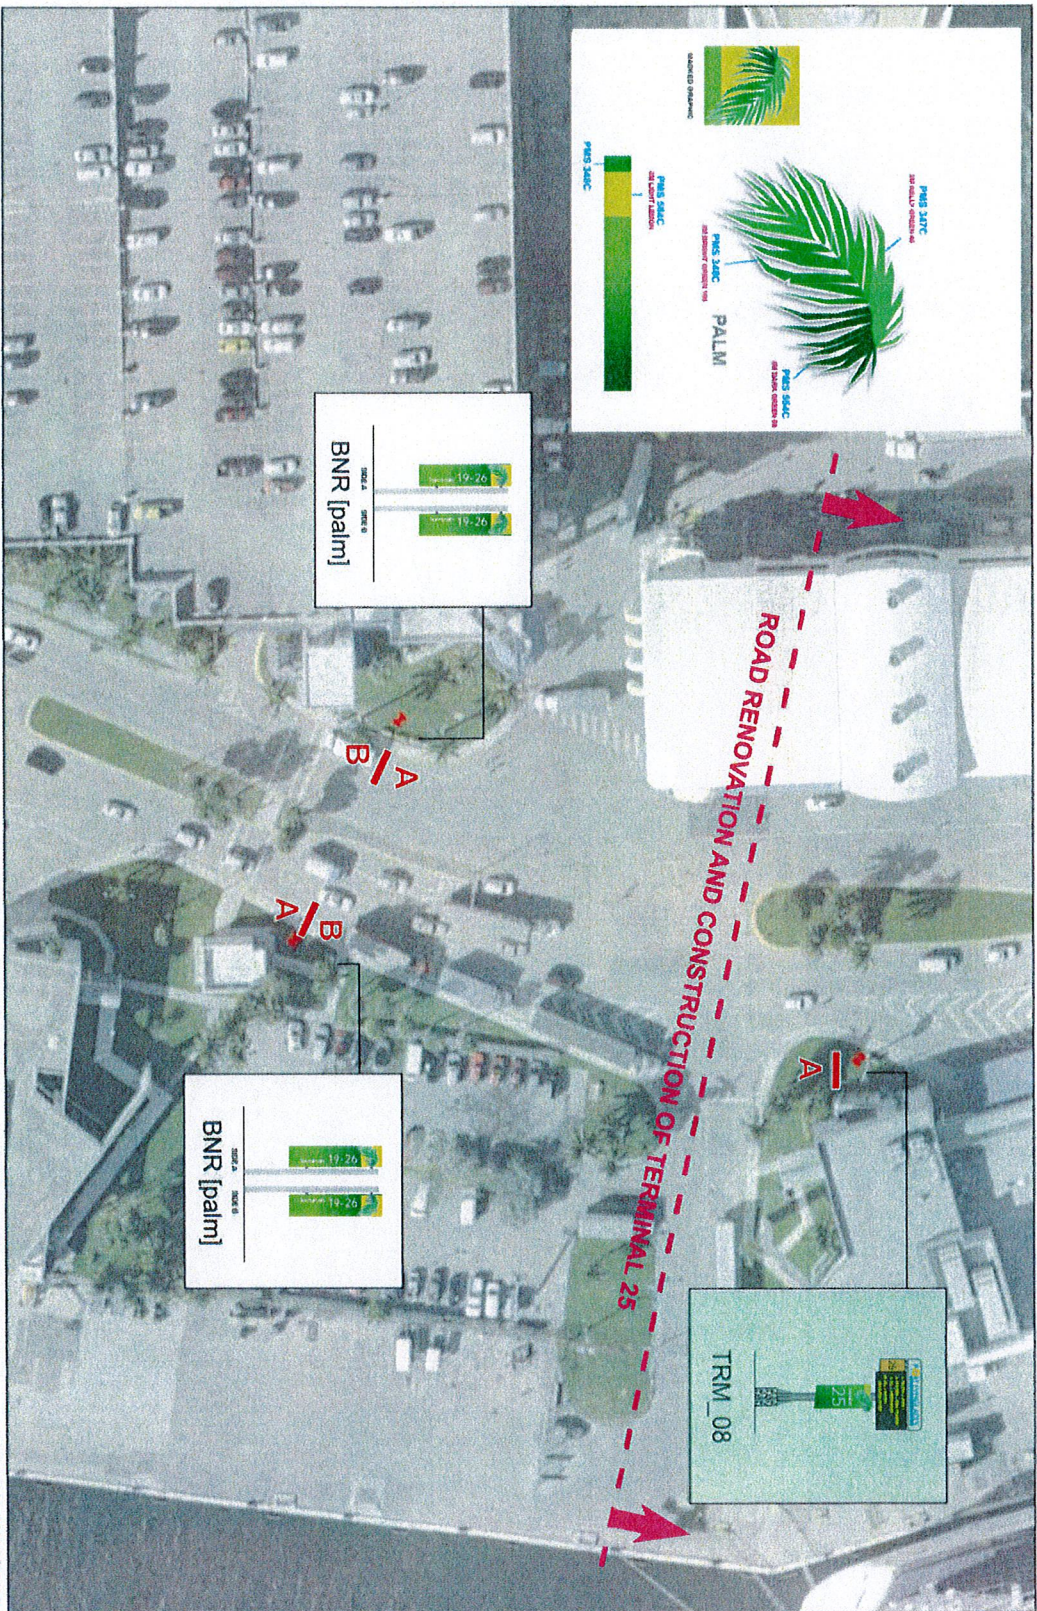

Change Order No. 5 Pay Items

Item 2, PNC211560C1--01-66 - Furnish and install DIG 1 Heron 8 feet wide icons on high pressure laminate (HPL) - Qty of one (1) this page mount on Heron sign DIG_01.

Item 4, PNC211560C1--01-68 - Furnish and install FL-C_04 2-18 Heron Sign HPL panel on Eller Drive. - Qty of one (1) this page mount on existing FL-C_04 structure.
Damaged sign.

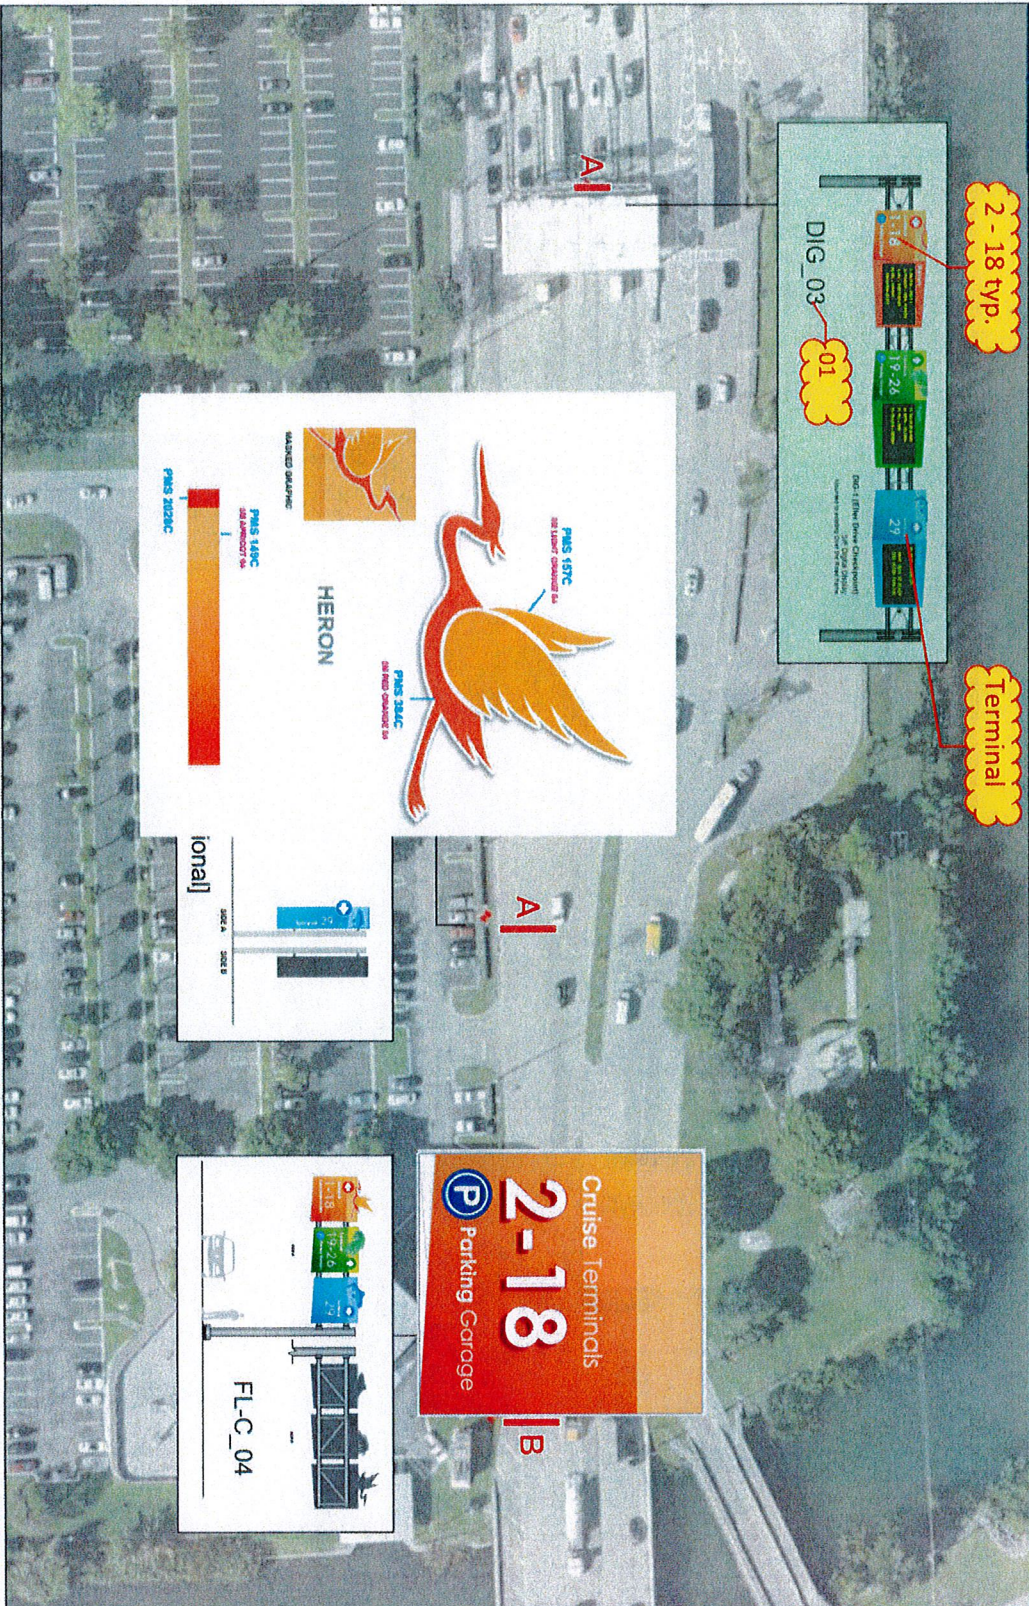

ELLER DRIVE CHECKPOINT - SECTION 2.0

PORT EVERGLADES : DESIGN INTENT DOCUMENT FINAL 06.19.18



HOLLYWOOD
