WORK AUTHORIZATION PURSUANT TO THE SYSTEM AND SERVICES AGREEMENT BETWEEN BROWARD COUNTY AND KEYLITE POWER AND LIGHTING CORP.

Contract Number: R1426611P1

Work Authorization No. 02-25 FSA Infrastructure Equipment Life Cycle Replacement

This Work Authorization is between Broward County and Keylite Power and Lighting Corp. ("Provider" or "Keylite") pursuant to the System and Services Agreement, dated October 10, 2017 (as amended, the "Agreement"). In the event of any inconsistency between this Work Authorization and the Agreement, the provisions of the Agreement shall govern and control unless otherwise expressly stated herein.

The time period for all work required under this Work Authorization (i.e., Project 1, Project 2, and Project 3) will be from the date of complete execution by the parties until one hundred eighty (180) days after County's Notice to Proceed for Project 1, unless otherwise extended or terminated in writing by the Contract Administrator. Each individual project shall commence only upon County's issuance of a Notice to Proceed for that project.

Services to be provided:

Provider shall provide services for three (3) projects under this Work Authorization.

The projects are as follows:

Exhibit A, Project 1: Fire Alerting Infrastructure Life Cycle Equipment Replacement

Exhibit B, Project 2: EMS-Sunrise Site Changeout of Frequency 6 GHz to 11 GHZ

Exhibit C, Project 3: Markham Park – Davie Antenna Replacement

See the applicable Statement of Work for additional details.

Fee Determination: Payment for services under this Work Authorization is as follows:

Project 1 – Fire Alerting Infrastructure Life Cycle Equipment Replacement

Equipment & Materials: \$172,158.26
Professional Services: \$175,728.30
Project 1 Total Cost \$347,886.56

Recurring Fees for Support and Maintenance Services for Project 1 Equipment

Recurring Support and Maintenance Services fees for all Equipment in Project 1 shall be invoiced quarterly in arrears in the amount of \$1,030.09 (\$4,120.36 annually), in accordance with the

existing invoicing schedule for Support and Maintenance Services under the Agreement (with the first and last invoice pro rata to the extent applicable), beginning one year after the date of Final Acceptance of Project 1. These amounts shall be allocated to the Support and Maintenance Services not-to-exceed amounts under the Agreement and are stated here for informational purposes only.

Project 2 – EMS Sunrise Site Changeout of Frequency 6 GHz to 11 GHz*

Professional Services:	\$20,322.94				
Project 2 Total Cost \$38,926.07					
Project 3 – Markham Park – Davie Antenna	Replacement*				
Equipment & Materials:	\$14,528.96				
Professional Services:	\$19,810.64				
i i diessional sel vices.	Ψ=5/0=0.0.				

^{*} Provider will provide Support and Maintenance Services for the Equipment in Project 2 and Project 3 for the duration of and in accordance with the terms of the Agreement at no additional cost to County.

The foregoing amounts shall be invoiced by Provider in accordance with the Payment Terms as stated in the applicable Exhibit for that project. Final payment for each project shall be made only upon written acceptance by the County of all goods and services provided under the applicable project (i.e., Final Acceptance as defined in each project).

(Reminder of Page Left Intentionally Blank)

IN WITNESS WHEREOF, the Parties hereto have made and executed this Work Authorization No. 02-25, effective as of the date the last party signs this Work Authorization No. 02-25.

County

Broward County, by and through Its Board of County Commissioners	Contract Administrator
	Ву:
By:	Project Manager
Mayor	Ву:
day of, 202	Бу
Approved as to form by	
Andrew J. Meyers Broward County Attorney	
115 South Andrews Avenue, Suite 423	
Fort Lauderdale, Florida 33301	
Telephone: (954) 357-7600	
Sara Cohen Reason: Approved as to form Location: Broward County Attorney's Office Date: 2025.05.19 11:57:34 -0400'	
Sara F. Cohen (Date)	
Assistant County Attorney	
Rene D. Harrod cn=Rene D. Harrod, ou=Broward County Altorney's Office, email-marrod Berroward.org, c=US Approved as to form 2025.05.19 12:03:18-0-4100'	
René D. Harrod (Date)	
Chief Deputy County Attorney	
Contractor Angel E Digitally signed by Angel	
By: Munoz Date: 2025.05.16 09:09:01 -04'00'	
Authorized Signer	
Angel Munoz	
Print Name and Title	
day of, 20	

(Date)

(Date)

Exhibit A

Project 1: Fire Alerting Infrastructure Life Cycle Equipment Replacement

Executive Summary

The Broward County Fire Station Alerting system ("BFSA System") provides countywide fire alerting services to all stations in Broward County. The BFSA System handles over 300,000 calls for service annually, with a 99.999% uptime goal that has been successfully maintained since commissioning.

Pursuant to the Agreement, Provider maintains the BFSA System as part of the annual maintenance services, conducts an annual site audit of all Equipment, and reports End of Life (EOL) status of the Equipment to County.

EOL determination is made by each manufacturer separately, and EOL definitions vary in form. Provider's annual BFSA System review considers three EOL conditions:

- 1. End of Manufacturing
- 2. End of Sale
- 3. End of Support

Th purpose of this project is to replace critical Equipment that is in EOL status. The equipment and services described in this SOW are required to accomplish EOL updates as specified herein.

1. Equipment

Provider shall provide the replacement equipment as stated in Attachment 1, Project 1 Fire Alerting Infrastructure Lifecycle Equipment Replacement.

2. Project Timeline

Provider shall adhere to the following project timeline unless otherwise agreed to by County. All timeframes stated in this Project 1, SOW shall begin upon County's issuance of the Notice to Proceed ("NTP") for Project 1 (e.g., the detailed design must commence within 8-12 weeks after County's issuance of the NTP for Project 1).

Item	Description	Project Week	Fiscal Week
1	Work Authorization	0	FY25-25
2	Purchase Order	0	
3	Payment 1	6	
4	Orders 1	7	
5	Commence Detailed Design	8-12	
6	Receive Orders 1	10	
7	Prototype & Lab Testing	10-13	
8	Dispatch Upgrades	14-15	
9	Pilot Testing	17-21	
10	Remedial Work	22	
11	Orders 2	23-35	
12	Install and Cutover	36-40	
13	Punchlist & Asbuilts	41	
14	Final Acceptance	42	

3. Responsibilities

For the duration of the project, the parties will be responsible for the following tasks as indicated below:

TASKS	REPSONSIBILE							
	Broward County	Keylite	MobileCom	Cambium	Other Suppliers			
Work Authorization	x							
County Purchase Order	x							
Initial Deposit	x							
Project Management	x	x						
System Design		x	х	x	x			
Materials Orders		x	х		х			
Materials Managment			х					
Staging, Bench testing	observe	x	х					
Pilot Field Testing	approve	x	х					
Field Installation	access, approve	x	х					
Acceptance Testing	approve	x	х					
Warranty		x	х					
Documentation		x	х					
Final Acceptance	x							
Progress Payments	x							

Keylite, individually and/or through its approved subcontractors, will perform the following:

- Provide detailed design of BFSA System (e.g., network and equipment topology)
- Provide all replacement components/equipment

- Perform installation of components/equipment
- Perform system configuration and testing
- Coordinate with County staff
- Submit Change Management Requests (CMRs) as needed during the project
- Record all Moves, Adds, and Changes to BFSA As built drawings
- Provide County staff with an updated BFSA equipment list and updated As Built drawings

County will perform the following:

- Collaborate with Keylite team during the project
- Coordinate any meeting needed with stakeholders
- Provide Keylite team with access and/or accompany team members where needed
- Review, approve, process CMRs
- Witness Acceptance Testing Procedures performed by Keylite and provide approval of Acceptance Testing
- Provide Final Acceptance, which shall not be unreasonably withheld

4. Technical Approach

After the issuance of the NTP by the Contract Administrator, Provider shall provide the services in three phases. At the discretion of County and with approval by Provider, phases may proceed simultaneously or be reordered.

Phase 1 – Project Launch and System Design:

4.1 Project Launch

Within ten (10) business days after County's issuance of the NTP for Project 1, Keylite will schedule a kickoff meeting. This meeting will include County stakeholders, as designated by County, Keylite engineering and project management team members, and subcontractors and vendors as necessary.

The kickoff meeting will outline the goals, major steps, timelines, and requests and expectations of the project from all teams.

Upon project launch (i.e., the issuance of the NTP for Project 1), Keylite will conduct Project Planning, inclusive of the following steps:

a. BFSA System Design – Revise and Review. In consultation with suppliers, the BFSA System design will be revised and detailed with final Bills of Materials, supplier orders, and high-level configuration review. Any required changes to the BFSA System design will be escalated to County. Provider will notify County of any expected price increase due to tariffs or otherwise within ten (10) business days after becoming aware of any price

increase; any changes that increase the cost of this Work Authorization will require an amendment to this Work Authorization.

- b. Schedule Creation and Updates A project schedule will be created by Provider prior to the kickoff meeting and presented to the project team during the kickoff meeting. The project schedule will be revised and updated at least three (3) days prior to any bi-weekly meetings with the project team.
- c. For the duration of Project 1, Provider shall conduct bi-weekly progress meetings with County. Resource planning, CMR scheduled events, and related project items will be maintained on a 3-week lookahead basis.

4.2 Detail Design

Within 15 business days after the NTP, Provider will provide County detailed design drawings and support information that will embody the complete BFSA System design. Installation drawings will be of like kind and quality to the existing BFSA System drawing package. Installation drawings will be marked up in the field and revised as necessary. Installation drawings will be included in the final As-Built drawing package that must be provided to County prior to Final Acceptance.

Phase 2 Installation, Configuration, and Testing:

4.3. Project Orders

Within 20 business days after the NTP, Provider will place and inventory material orders at Mobilecom. Provider shall be liable for any equipment inventoried and stored at MobileCom. Incoming material receipt reports, inventory database updates, incoming QA materials inspections, and project-specified unit-test procedures will be conducted and documented upon arrival of shipments and processing.

4.4 Equipment Staging and Bench Testing

All active equipment (i.e., equipment that uses AC or DC power) will be bench tested by Provider and burned in for a minimum of 120 hours before field installation.

Provider will assemble, install, and test all equipment. Provider will test all configurations, and protocols will be exercised. Provider will simulate and manually induce error conditions and measure the effects. Errors will be rectified in isolation to exercise failure mode effect and critically analyzed. Keylite will develop and conduct such tests as are necessary and appropriate to exercise equipment and software functionality (i.e., server operating system; Windows 2022 (Standard)) in a simulated isolated network environment. Ancillary tasks required by Provider include staging software upgrades, remote access and support procedures, and maintenance procedure development. A detailed Acceptance Test Plan ("ATP") will be developed by Provider and reviewed with County prior to being rehearsed on the lab equipment. Provider shall incorporate any County-requested edits into the ATP and Provider shall resubmit the ATP for

County approval prior to commencing ATP. Pilot Testing (as defined in Section 4.8 below) will be completed by Provider at the conclusion of this stage.

4.5 Configuration Development

Provider will develop "bare metal" configurations for network components. Existing configuration management tools will be modified or mothballed. Configurations will be created in isolation and version controlled. Updated procedures for field and lab deployment will be developed and rehearsed/released in parallel.

4.6 Network Routers and Switch Upgrades

The core switches and routers will be swapped by Provider with new Cisco 3560 routers independently. This will be conducted before Pilot Testing to ensure the target environment is complete. Site routers at each of the four (4) UHF sites, plus Sunrise and Coconut Creek dispatch site routers will also be swapped by Provider under the CMR process.

4.7 Unit Replication and Testing

When configurations are created and tested by Provider, Provider must replicate and propagate the configurations to the field. This may involve a series of transitional configurations as network changes are designated for incremental deployment.

4.8 Acceptance Testing

Provider will develop and rehearse functional tests during the Equipment Staging and Bench Testing stage. As stated in Section 4.4, a detailed ATP will be developed in concert with County and will be comprises of two phases: Pilot Testing and System Deployment Testing.

4.8.1. <u>Pilot Test</u>: The goal of Pilot Testing is to demonstrate the stability of the pilot equipment installation and its suitability for system-wide deployment. Tests will exercise the basic site unit functionalities for startup, failure, recovery, error reporting, stability, and related operational states. The successful passing of these tests will signify the system is ready for full production deployment, and that field installation can continue.

Keylite will run a field pilot test for a minimum of seven (7) and maximum of thirty (30) calendar days for the Point to Multi-Point (PMP) site upgrades. The Pilot Test is planned to be run on the northern microwave segment between Sunrise Dispatch, and the two (2) Tamarac and Coconut Creek Radio Frequency (RF) sites. A written test plan will be created for County review and approval no less than 10 business days in advance of the Pilot Test's start date. Data will be collected during the Pilot Test period, and all recorded errors will be traced to root cause.

A Pilot Test report will be created by Keylite within ten (10) business days after the conclusion of the Pilot Test. The Pilot Test report will detail all test findings and make recommendations for deployment or remedial work, as necessary and appropriate.

All equipment configurations will be archived before Provider commences with any changes because of Pilot Testing. If there are unsolvable errors, any equipment removed or reconfigured will be restored to its original condition, and Keylite will revert the PMP test sites to their former working states. In this event, Keylite will present a remedial plan to County to upgrade the site within thirty (30) days after the reversion to the former working state. Any remedial actions required will be recorded by Provider on a project action item register.

4.8.2 <u>Field Deployment Acceptance Testing</u>: Field Deployment Acceptance Testing will be conducted by Provider after Pilot Testing for each site as it is installed. The goal of Field Deployment Acceptance Testing is to validate that the equipment is installed and programmed properly to ensure that the equipment operates correctly on all network connections, and that the equipment reports problem-errors as designed. Provider will conduct intrusive testing to implement link failures and recoveries, and other such invasive procedures as are recommended by Provider and approved by County.

4.9 Field Deployment

Based on results of the Pilot Testing, field deployment installation will be performed throughout the network. Each site will be installed and cut over to production under the County's established CMR process. Field Deployment Acceptance Testing will be completed by Provider at the conclusion of this stage.

Phase 3 Final Acceptance Testing:

4.10 Final Acceptance

After all sites are installed, a thirty (30) day field burn-in period will commence. After the burn-in period, a final report will be generated by Provider and As Built documentation will be created by Provider and provided to County for approval. Prior to commencing Final Acceptance testing, County and Provider will collaboratively prepare a punch list. Any punch list items with a designation of Severe, Major, or Minor (as defined in the Agreement) will be resolved or scheduled for resolution, as agreed by the parties at the time of punch list creation.

Upon completion of the thirty (30) days burn-in period and all punch list items with a Severe, Major, or Minor designation have been resolved to County's satisfaction, County will issue written notice of Final Acceptance. Upon County's written notice of Final Acceptance, the equipment will be deemed "Equipment" under the Agreement.

4.11 Maintenance

The Equipment will be warranted for one year after the date of Final Acceptance ("Warranty Period"). After the Warranty Period, the Equipment will be transitioned from warranty support to Support and Maintenance Services as defined in the Agreement.

5. Security/Access

Provider will always comply with all applicable County access and security standards, as well as any other or additional restrictions or standards for which County provides written notice to Provider. Provider will provide any and all information that County may request to determine appropriate security and network access restrictions and verify Provider's compliance with County security standards. If at any point in time County, in the sole discretion of its Chief Information Officer or written designee, determines that Provider's access to any aspect of the County's network presents an unacceptable security risk, County may immediately suspend or terminate Provider's access and, if the risk is not promptly resolved to the reasonable satisfaction of the County's Chief Information Officer or written designee, may terminate this Work Authorization upon ten (10) business days' notice (including, without limitation, without restoring any access to the County network to Provider). County is solely responsible for the physical security of its network infrastructure.

6. Payment Terms:

All fees for the equipment are included in the amounts below. All equipment and services under this Work Authorization shall be invoiced as follows:

Payment Milestone	Invoicing	Amount	
Equipment	Upon receipt of Purchase Order	\$86,079.15	
Equipment & Installation	Per site upon County's written	\$9,958.67 per site	
per site (Site Acceptance	acceptance of the applicable site.	(\$129,462.71 total for all 13	
Testing)		sites)	
Phase 1 Project Launch and	Upon County's written acceptance	\$53,767.83	
System Design	of Phase 1		
Phase 2 Installation,	Upon County's written acceptance	\$43,788.23	
Configuration, and Testing	of Phase 2		
Phase 3 Final Acceptance	Upon County's written notice of	\$34,788.64	
Testing	Final Acceptance		
TOTAL		\$347,886.56	

(Remainder of Page Left Intentionally Blank)

Exhibit B

Project 2: Microwave System Repair: EMS-Sunrise Site Changeout of 6 GHz to 11 GHz

Executive Summary

Keylite conducts continuous diagnostic reviews on all reported alarms and errors. In (1Q) 2023 Keylite detected anomalous errors on the microwave link between the EMS site and the Sunrise Dispatch site. These errors were traced to a root cause of interference caused by residential 6 GHz Wi-Fi operations in the immediate vicinity of the EMS site. County escalated the interference to the Federal Communications Commission (FCC), and County, Keylite, and FCC engineers tracked the source to local Comcast customer(s).

Due to the recent FCC licensing of the 6 GHz band for Wi-Fi applications, County determined that the best course of action is to replace the microwave link with radio and dishes in the 11 GHz band. This will abate the immediate problem and will protect the link from future 6 GHz interference.

This project is to procure and install the new 11 GHz microwave radios, utilizing the new 11GH frequency licenses provided by the County for the microwave path, and configure and optimize the equipment at both site locations.

1. Equipment

Provider shall provide the replacement equipment as stated in Attachment 2, Project 2 - EMS-Sunrise Site Project Equipment.

2. Project Timeline

Provider shall adhere to the following project timeline unless otherwise agreed to in writing by County. All timeframes shall begin upon County's issuance of the Notice to Proceed ("NTP") for Project 2 (e.g., the bench burn in must commence within 11-15 weeks after County's issuance of the NTP).

Item	Description	Project Week	Fiscal Week
1	Work Authorization	0	FY25-25
2	Purchase Order	0	
3	Payment 1	6	
4	Orders 1	7	
5	Receive Orders 1	10	
6	Bench Burn In	11-15	
6	Install and Cutover	16	
7	Punchlist & Asbuilts	17	
8	Final Acceptance	20	

3. Responsibilities

For the duration of the project, the parties will be responsible for the following tasks as indicated below:

TASKS	REPSONSIBILE							
	Broward County	Keylite	MobileCom	Cambium	Other Suppliers			
Work Authorization	х							
County Purchase Order	х							
Initial Deposit	х							
Project Management	х	x						
Structural Analysis	х							
System Design		x	x	x	x			
Materials Orders		x	x		x			
Materials Managment			x					
Staging, Bench testing	observe	x	x					
Field Installation	access, approve	x	x					
Acceptance Testing	approve	x	x					
Warranty		x	x					
Documentation		x	x					
Final Acceptance	х							
Progress Payments	х							

Keylite, individually and/or through its subcontractors, will perform the following:

- Provide technical specifications
- Provide intermodulation study and confirm no interferences on existing equipment located at each site
- Provide all replacement components/equipment in Attachment 2
- Perform installation of components/equipment
- Perform system configuration and testing
- Coordinate with County staff
- Submit CMRs as needed during the project
- Record all Moves, Adds, and Changes to BFSA System As built drawings
- Provide County staff with updated equipment list and updated As Built drawings

County will perform the following:

- Frequency coordination
- Structural analysis
- Collaborate with Keylite team during the project
- Coordinate any meeting needed with stakeholders
- Provide Keylite team with access and/or accompany team members when needed
- Review, approve, process CMRs.

4. Technical Approach

After the issuance of the NTP for Project 2 by the Contract Administrator, Provider shall perform the services in three phases. At the discretion of County and with approval by Provider, phases may proceed simultaneously or be reordered.

Phase 1 – Project Launch and System Design

4.1 Project Launch

Within ten (10) business days after County's issuance of the NTP for Project 2, Keylite will schedule a kickoff meeting. This meeting will include County stakeholders as designated by County, Keylite engineering staff, project management team members, and subcontractors and vendors as necessary.

The kickoff meeting will outline the goals, major steps, timelines, and requests and expectations of the project from all teams.

Upon project launch (i.e., the issuance of the NTP for Project 2), Keylite will conduct Project Planning, inclusive of the following steps:

- a. BFSA System Design Revise and Review. In consultation with suppliers, the design will be revised and detailed with final Bills of Materials, supplier orders, and high-level configuration review. Any required BFSA System design changes will be escalated to County at this time.
- b. Schedule Creation and Updates A project schedule will be created by Provider prior to the kick-off meeting and presented to the project team during the kickoff meeting. The project schedule will be revised and updated at least three (3) days prior to any bi-weekly meetings with the project team. Resource planning, CMR scheduled events and related project items will be maintained by Provider on a 3-week lookahead basis.
- c. For the duration of Project 2, Provider shall conduct bi-weekly progress meetings with County. Resource planning, CMR scheduled events, and related project items will be maintained on a 3-week lookahead basis.

4.2 Detailed Design

Within fifteen (15) business days after the NTP, Provider will provide County detailed design drawings and support information that will embody the complete BFSA System design. Installation drawings will be of like kind and quality to the existing BFSA System drawing package. Installation drawings will be marked up in the field and revised as necessary. Installation drawings will be included in the final As-Built drawing package that must be provided to County prior to Final Acceptance.

4.3 Structural Analysis

County will have a structural analysis performed on the towers to determine if the towers can support the proposed equipment. County will provide Keylite with the results of the structural analysis; however, Keylite acknowledges the deadlines stated in this Exhibit B are not contingent or dependent upon County providing the structural analysis to Keylite. The structural analysis shall become a part of this Exhibit B and the BFSA System Technical Design Folder.

Phase 2— Installation, Configuration, and Testing

4.4 Project Orders

Within twenty (20) business days after the NTP, Provider will place and inventory material orders at Mobile Communications (MobileCom). Provider shall be liable for any equipment inventoried at MobileCom. Incoming material receipt reports, inventory database updates, incoming QA materials inspections, and project-specified unit-test procedures will be conducted and documented upon arrival of shipments and processing.

4.5 Equipment Staging and Bench Testing

All active equipment (i.e., equipment that uses AC or DC power) will be bench tested by Provider and burned in for a minimum of 72 hours before field installation.

4.6 Configuration Development

Provider will develop "bare metal" configurations for microwave radios and related network components. Configurations will be created in isolation and version controlled. Update procedures for field and lab deployment will be developed and rehearsed/released in parallel.

4.7 Installation

Keylite through its subcontractors will perform all necessary work associated with the installation, configuration, and testing of equipment identified in Attachment 2. All equipment will be installed and cut over to production in accordance with the County's CMR process.

4.8 Acceptance Testing

Acceptance Test Procedures (ATP) replicate the original project ATP steps for this link and are attached as Attachment 3.

ATP testing will be conducted by Provider for each site as it is installed. The goal of ATP is to validate that the equipment is installed and programmed properly, and that the equipment operates correctly on all network connections, and reports problem-errors as designed. Provider will perform intrusive tests to implement link failures and recoveries, and other such invasive procedures as are recommended by Provider and approved in writing by County.

Phase 3— Final Acceptance Testing

4.9 Final Acceptance

Prior to commencing Final Acceptance, County and Provider will collaboratively prepare a punch list. Any punch list items with a designation of Severe, Major, or Minor (as defined in the Agreement) will be resolved or scheduled for resolution, as agreed by the Parties at the time of punch list creation.

Once all punch list items with a Severe, Major, or Minor designations have been resolved to County's satisfaction, County will issue written notice of Final Acceptance.

Upon County's written notice of Final Acceptance, the equipment shall be deemed "Equipment" under the Agreement.

5. Security/Access

Provider will always comply with all applicable County access and security standards, as well as any other or additional restrictions or standards for which County provides written notice to Provider. Provider will provide any and all information that County may reasonably request in order to determine appropriate security and network access restrictions and verify Provider's compliance with County security standards. If at any point in time County, in the sole discretion of its Chief Information Officer or written designee, determines that Provider's access to any aspect of the County's network presents an unacceptable security risk, County may immediately suspend or terminate Provider's access and, if the risk is not promptly resolved to the reasonable satisfaction of the County's Chief Information Officer or written designee, may terminate this Work Authorization upon ten (10) business days' notice (including, without limitation, without restoring any access to the County network to Provider). County is solely responsible for the security of its physical network infrastructure.

6. Payment Terms:

All fees for the equipment are included in the amounts below. All equipment and services under this Work Authorization shall be invoiced as follows:

Payment Milestone	Invoicing	Amount
Equipment Receipt	Upon receipt of equipment inventory and	\$9,301.56
	packing slip	
Phase 2: Installation, System	Upon County's written acceptance of Phase 2	\$21,839.30
Configuration & Testing		
Final Acceptance Testing	Upon County's written notice of Final	\$7,785.21
	Acceptance	
TOTAL		\$38,926.07

7. Support and Maintenance Services

The equipment will be warranted (break/fix) for one year after the date of Final Acceptance ("Warranty Period"). After the Warranty Period, the equipment will be transitioned from warranty support to Support and Maintenance Services as defined in the Agreement.

(Remainder of Page Left Intentionally Blank)

Exhibit C

Project 3: Microwave System Repair: Markham Park - Davie Antenna Replacement

Executive Summary

As part of the annual maintenance services, Keylite conducts continuous diagnostic reviews of all reported alarms and errors. In (1Q) 2023 Keylite detected anomalous errors on the microwave link between the Markham Park and site and the Davie RF sites.

These errors could not be traced to a direct root cause. After reviewing test plans and data, County elected to have the antennas replaced to higher gain and directionally shield antennas. This project is to install replacement antennas between the cited RF sites and measure the results to determine if the problem is resolved.

1. Equipment

Provider shall provide the replacement equipment as stated in Attachment 4, Project 3 - Markham Park – Davie Antenna Replacement and Services Costs

2. Project Schedule

Provider shall adhere to the following project schedule unless otherwise agreed to by County. All timeframes shall begin upon County's issuance of the Notice to Proceed ("NTP") for Project 3 (e.g., install and cutover must commence within 13 weeks after County's issuance of the NTP).

Item	Description	Project Week	Fiscal Week
1	Work Authorization	0	FY25-25
2	Purchase Order	0	
3	Payment 1	6	
4	Orders 1	7	
5	Receive Orders 1	10	
6	Install and Cutover	13	
7	Punchlist & Asbuilts	14	
8	Final Acceptance	15	

3. Responsibilities

For the duration of the project, the parties will be responsible for the following tasks as shown below:

TASKS	REPSONSIBILE							
	Broward County	Keylite	MobileCom	Cambium	Other Suppliers			
Work Authorization	х							
County Purchase Order	x							
Initial Deposit	x							
Project Management	x	x						
Structural Analysis	x							
System Design		x	x	x	x			
Materials Orders		x	x		x			
Materials Managment			X					
Acceptance Testing	approve	x	x					
Warranty		x	X					
Documentation		x	X					
Final Acceptance	x							
Progress Payments	x	-						

Keylite, individually and/or through its subcontractors, will perform the following:

- Provide technical specifications
- Provide all replacement components/equipment in Attachment 4
- Perform installation of components/equipment
- Perform system configuration and testing
- Coordinate with County staff
- Submit CMRs as needed during the project
- Record all Moves, Adds, and Changes to BFSA As built drawings
- Provide County staff with updated equipment list and As Built drawing updates

County will provide the following:

- Frequency coordination
- Structural analysis
- Collaborate with Keylite team during the project
- Coordinate any meeting needed with stakeholders
- Provide Keylite team with access and/or accompany team members when needed
- Review, approve, process CMRs

4. Technical Approach

After the issuance of the NTP for Project 3 by the Contract Administrator, Provider shall perform the services in three phases. At the discretion of County and with approval by Provider, phases may proceed simultaneously or be reordered.

Phase 1— Project Launch and System Design

4.1 Project Launch

Within ten (10) business days after County's issuance of the NTP for Project 3, Keylite will schedule a kickoff meeting. This meeting will include County stakeholders as designated by

County, Keylite engineering staff, project management team members, and subcontractors and vendors as necessary.

The kickoff meeting will outline the goals, major steps, timelines, and requests and expectations of the project from all teams.

Upon project launch (i.e., the issuance of the NTP for Project 3), Keylite will conduct Project Planning, inclusive of the following steps:

- a. BFSA System Design Revise and Review. In consultation with suppliers, the design will be revised and detailed with final Bills of Materials, supplier orders, and high-level configuration review. Any required BFSA System design changes will be escalated to County at this time.
- b. Schedule Creation and Updates A project schedule will be created by Provider prior to the kickoff meeting and presented to the project team during the kickoff meeting. The project schedule will be revised and updated at least three (3) days prior to any monthly meeting.
- c. For the duration of Project 3, Provider shall conduct monthly progress meetings with County. Resource planning, CMR scheduled events and related project items will be maintained on a 3-week lookahead basis.

4.2 Detailed Design

Within fifteen (15) business days after the NTP, Provider will provide County detailed design drawings and support information that will embody the complete BFSA System design. Installation drawings will be of like kind and quality to the existing BFSA System drawing package. Installation drawings will be marked up in the field and revised as necessary. Installation drawings will be included in the final As-Built drawing package that must be provided to County prior to Final Acceptance.

4.3 Structural Analysis

County will have a structural analysis performed on the towers to determine if the towers can support the proposed equipment. County will provide Keylite with the result of the structural analysis; however, Keylite acknowledges the deadlines stated in this Exhibit C are not contingent or dependent upon County providing the structural analysis to Keylite. The structural analysis shall become a part of this Exhibit C and the BFSA System Technical Design Folder.

Phase 2— Installation, Configuration, and Testing

4.4 Project Orders

Within twenty (20) business days after the NTP, Provider will place and inventory material orders at Mobilecom. Provider shall be liable for any equipment inventoried and stored at MobileCom. Incoming material receipt reports, inventory database updates, incoming QA materials

inspections, and project-specified unit-test procedures will be conducted and documented upon arrival of shipments and processing.

4.5 Equipment Staging and Bench Testing

All active equipment (i.e., equipment that uses AC or DC power) will be bench tested by Provider and burned in for a minimum of 72 hours before field installation.

4.6 Configuration Development

Provider will develop "bare metal" configurations for microwave radios and related network components. Configurations will be created in isolation and version controlled. Update procedures for field and lab deployment will be developed and rehearsed/released in parallel.

4.7 Installation

Keylite, directly and/or through its subcontractors, will perform all necessary work associated with the installation, configuration, and testing of equipment identified in Attachment 4. All equipment will be installed and cut over to production in accordance with the County's CMR process.

4.8 Acceptance Testing

Acceptance Test Procedures (ATP) replicate the original project ATP steps for this link and are attached as Attachment 3.

ATP testing will be conducted by Provider for each site as it is installed. The goal of ATP is to validate that the equipment is installed and programmed properly to ensure that the equipment operates correctly on all network connections, and reports problem-errors as designed. Provider will conduct intrusive tests to implement link failures and recoveries, and other such invasive procedures as are recommended by Provider and approved in writing by County.

Phase 3— Final Acceptance Testing

4.9 Final Acceptance

Prior to commencing Final Acceptance, County and Provider will collaboratively prepare a punch list. Any punch list items with a designation of Severe, Major, or Minor (as defined in the Agreement) will be resolved or scheduled for resolution, as agreed by the Parties at the time of punch list creation.

Once all punch list items with a Severe, Major, or Minor designations have been resolved to County's satisfaction, County will issue written notice of Final Acceptance.

Upon County's written notice of Final Acceptance, the equipment shall be deemed "Equipment" under the Agreement.

5. Security/Access

Provider will comply at all times with all applicable County access and security standards, as well as any other or additional restrictions or standards for which County provides written notice to Provider. Provider will provide any and all information that County may reasonably request to determine appropriate security and network access restrictions and verify Provider's compliance with County security standards. If at any point in time County, in the sole discretion of its Chief Information Officer or written designee, determines that Provider's access to any aspect of the County's network presents an unacceptable security risk, County may immediately suspend or terminate Provider's access and, if the risk is not promptly resolved to the reasonable satisfaction of the County's Chief Information Officer or written designee, may terminate this Work Authorization upon ten (10) business days' notice (including, without limitation, without restoring any access to the County network to Provider). County is solely responsible for the physical security of its network infrastructure.

6. Payment Terms:

All fees for the equipment are included in the amounts below. All equipment and services under this Work Authorization shall be invoiced as follows:

Payment Milestone	Invoicing	Amount
Equipment	Upon receipt of equipment inventory and packing slip	\$7,264.48
Phase 2: Installation, Configuration & Testing	Upon County's written acceptance of Phase 2	\$20,207.20
Phase 3: Final Acceptance	Upon County's written notice of Final Acceptance	\$6,867.92
TOTAL		\$34,339.60

7. Support and Maintenance Services:

The equipment will be warranted (break/fix) for one year after the date of Final Acceptance ("Warranty Period"). After the Warranty Period, the equipment will be transitioned from warranty support to Support and Maintenance Services as defined in the Agreement.

Attachment 1 Project 1-Fire Alerting Infrastructure Lifecycle Equipment Replacement

ttachment 1			BFSA EOL Q	uotation 10-	5-2024				KEYLITE POWER & LIGHTING CORP Sent Sonny - Pinick Sonny
em	Item ID	Description	Mfg	List	List -10%	Unit Sell	Qty	Extended Sell	Maint. Scope/Comments
	DISPATCH	•							
	4221 Replace	WS-C3560CX-12	Cisco	CONTRACT		\$1,971.39	6	\$11,828.32	Replace 4221
	3650 Replace	WS-C3560CX-12	Cisco	CONTRACT		\$1,971.39	4		Replace 3650
	HP360	Dell Poweredge R350, configured	Dell			\$10,205.23	2		Replace H360
	USDD GaRI	Honeywell GaRI2	Honeywell	CONTRACT		\$2,535.75	2	\$5,071.50	
	Fortigate	Fortigate FG-81F-BDL-950-36	Fortigate			\$5,351.99	2		Replace FG-60, UTP
						¥-/		\$55,899.80	
	CREEK RF 17533	TX2020R-P	Cambium	\$2.989.00	\$2,690.10	\$2,690.10	1	\$2,690.10	Replace CMM5
	17543	ADVRP-5		\$792.00	\$712.80	\$712.80	1		'
			Cambium					\$712.80	Replace CMM5
	3859	930 watt supply	Cambium	\$766.32	\$689.69	\$689.69	2	\$1,379.38	New
	59251	GPS (CN pulse)	Cambium	\$336.93	\$303.24	\$303.24	1	\$303.24	New
	47431	GPS-TMG-HR-26N-100	PC-Tel	\$326.29	\$293.66	\$293.66	1	\$293.66	Replace existing
	69355	GPS-LMR/SMA-100-RA	Mobilecomm	\$245.72	\$221.15	\$221.15	1	\$221.15	Replace existing
	69357	GPS cable-CAT5-C	Mobilecomm	\$65.00	\$58.50	\$58.50	1	\$58.50	Replace existing
	17373	GPS mount	Cambuim	\$38.65	\$34.79	\$34.79	1	\$34.79	Replace existing
	59733	SPF10GSR modules	Cambuim	\$153.99	\$138.59	\$138.59	4	\$554.36	New
	6406	Fiber jumpers-LC	Misc	\$27.56	\$24.80	\$24.80	2	\$49.61	New
	61541	Surger protector-CAT5	Misc	\$58.59	\$52.73	\$52.73	1	\$52.73	New
	61543	Surge protector-GPS	Misc	\$195.99	\$176.39	\$176.39	1	\$176.39	New
	11612	Shop supplies	Misc	\$125.00	\$112.50	\$112.50	1	\$112.50	New
214	9996	Misc. Risk	Misc	\$0.00	\$0.00	\$0.00	1	\$0.00	Temp1
								\$0,033.20	
300	SUNRISE RF								
	17533	TX2020R-P	Cambium	\$2,989.00	\$2,690.10	\$2,690.10	1	\$2,690.10	Replace CMM5
	17543	ADVRP-5	Cambium	\$792.00	\$712.80	\$712.80	1	\$712.80	Replace CMM5
	3859	930 watt supply	Cambium	\$766.32	\$689.69	\$689.69	2	\$1,379.38	New
	59251	GPS (CN pulse)	Cambium	\$336.93	\$303.24	\$303.24	1	\$303.24	New
	47431	GPS-TMG-HR-26N-100	PC-Tel	\$326.29	\$293.66	\$293.66	1	\$293.66	Replace existing
	69355	GPS-IMG-RR-26N-100 GPS-LMR/SMA-100-RA	Mobilecomm	\$245.72	\$293.00		1	\$293.00	
				,	-	\$221.15			Replace existing
	69357	GPS cable-CAT5-C	Mobilecomm	\$65.00	\$58.50	\$58.50	1	\$58.50	Replace existing
	17373	GPS mount	Cambuim	\$38.65	\$34.79	\$34.79	1	\$34.79	Replace existing
	59733	SPF10GSR modules	Cambuim	\$153.99	\$138.59	\$138.59	4	\$554.36	New
	6406	Fiber jumpers-LC	Misc	\$27.56	\$24.80	\$24.80	2	\$49.61	New
	61541	Surger protector-CAT5	Misc	\$58.59	\$52.73	\$52.73	1	\$52.73	New
	61543	Surge protector-GPS	Misc	\$195.99	\$176.39	\$176.39	1	\$176.39	New
	11612	Shop supplies	Misc	\$125.00	\$112.50	\$112.50	1	\$112.50	New
314	9996	Misc. Risk	Misc	\$0.00	\$0.00	\$0.00	1	\$0.00	Temp1
								,	
	DAVIE	1							
	17533	TX2020R-P	Cambium	\$2,989.00	\$2,690.10	\$2,690.10	1	\$2,690.10	Replace CMM5
402	17543	ADVRP-5	Cambium	\$792.00	\$712.80	\$712.80	1	\$712.80	Replace CMM5
403	3859	930 watt supply	Cambium	\$766.32	\$689.69	\$689.69	2	\$1,379.38	New
	59251	GPS (CN pulse)	Cambium	\$336.93	\$303.24	\$303.24	1	\$303.24	New
	47431	GPS-TMG-HR-26N-100	PC-Tel	\$326.29	\$293.66	\$293.66	1	\$293.66	Replace existing
	69355	GPS-LMR/SMA-100-RA	Mobilecomm	\$245.72	\$233.00	\$221.15	1	\$221.15	Replace existing
				-	-		1		-
	69357	GPS cable-CAT5-C	Mobilecomm	\$65.00	\$58.50	\$58.50	_	\$58.50	Replace existing
	17373	GPS mount	Cambuim	\$38.65	\$34.79	\$34.79	1	\$34.79	Replace existing
	59733	SPF10GSR modules	Cambuim	\$153.99	\$138.59	\$138.59	4	\$554.36	New
	6406	Fiber jumpers-LC	Misc	\$27.56	\$24.80	\$24.80	2	\$49.61	New
411	61541	Surger protector-CAT5	Misc	\$58.59	\$52.73	\$52.73	1	\$52.73	New
	61543	Surge protector-GPS	Misc	\$195.99	\$176.39	\$176.39	1	\$176.39	New
	11612	Shop supplies	Misc	\$125.00	\$112.50	\$112.50	1	\$112.50	New
	9996	Misc. Risk	Misc	\$0.00	\$0.00	\$0.00	1	\$0.00	Temp1
414									
414								\$6,639.20	

tachment 1			BFSA EOL Q	BFSA EOL Quotation 10-5-2024					KEYLITE POWER & LIGHTING CORP Soret Storag - Fluid Storag
m	Item ID	Description	Mfg	List	List -10%	Unit Sell	Qty	Extended Sell \$6,639.	Maint. Scope/Comments
F00	CH2								
	17533	TX2020R-P	Cambium	\$2,989.00	\$2.690.10	\$2,690.10	1	\$2,690.10	Replace CMM5
	17543	ADVRP-5	Cambium	\$792.00	\$712.80	\$712.80	1	\$712.80	Replace CMM5
	3859	930 watt supply	Cambium	\$766.32	\$689.69	\$689.69	2	\$1,379.38	New New
	59251	GPS (CN pulse)	Cambium	\$336.93	\$303.24	\$303.24	1	\$303.24	New
	47431	GPS-TMG-HR-26N-100	PC-Tel	\$326.29	\$293.66	\$293.66	1	\$293.66	Replace existing
	69355	GPS-LMR/SMA-100-RA	Mobilecomm	\$245.72	\$221.15	\$221.15	1	\$221.15	Replace existing
	69357	GPS cable-CAT5-C	Mobilecomm	\$65.00	\$58.50	\$58.50	1	\$58.50	Replace existing
	17373	GPS mount	Cambuim	\$38.65	\$34.79	\$34.79	1	\$34.79	Replace existing
	59733	SPF10GSR modules	Cambuim	\$153.99	\$138.59	\$138.59	4	\$554.36	New
510	6406	Fiber jumpers-LC	Misc	\$27.56	\$24.80	\$24.80	2	\$49.61	New
511	61541	Surger protector-CAT5	Misc	\$58.59	\$52.73	\$52.73	1	\$52.73	New
512	61543	Surge protector-GPS	Misc	\$195.99	\$176.39	\$176.39	1	\$176.39	New
513	11612	Shop supplies	Misc	\$125.00	\$112.50	\$112.50	1	\$112.50	New
514	9996	Misc. Risk	Misc	\$0.00	\$0.00	\$0.00	1	\$0.00	Temp1
								\$6,639.	20
	EMS			1.				T.	
	17533	TX2020R-P	Cambium	\$2,989.00	\$2,690.10	\$2,690.10	1	\$2,690.10	Replace CMM5
	17543	ADVRP-5	Cambium	\$792.00	\$712.80	\$712.80	1	\$712.80	Replace CMM5
	3859	930 watt supply	Cambium	\$766.32	\$689.69	\$689.69	2	\$1,379.38	New
	59251	GPS (CN pulse)	Cambium	\$336.93	\$303.24	\$303.24	1	\$303.24	New Sealers suisting
	47431	GPS-TMG-HR-26N-100	PC-Tel	\$326.29	\$293.66	\$293.66	1	\$293.66	Replace existing
	69355	GPS-LMR/SMA-100-RA GPS cable-CAT5-C	Mobilecomm Mobilecomm	\$245.72	\$221.15 \$58.50	\$221.15 \$58.50	1	\$221.15	Replace existing
	69357 17373	GPS mount	Cambuim	\$65.00 \$38.65	\$34.79	\$34.79	1	\$58.50 \$34.79	Replace existing Replace existing
	59733	SPF10GSR modules	Cambuim	\$153.99	\$138.59	\$138.59	4	\$554.36	New New
	6406	Fiber jumpers-LC	Misc	\$27.56	\$24.80	\$24.80	2	\$49.61	New
	61541	Surger protector-CAT5	Misc	\$58.59	\$52.73	\$52.73	1	\$52.73	New
	61543	Surge protector-GPS	Misc	\$195.99	\$176.39	\$176.39	1	\$176.39	New
	11612	Shop supplies	Misc	\$125.00	\$112.50	\$112.50	1	\$112.50	New
	9996	Misc. Risk	Misc	\$0.00	\$0.00	\$0.00	1	\$0.00	Temp1
								\$6,639.	
tachment 1			BFSA EOL Q	uotation 10-	5-2024				KEYLITE BONES IL-O'HING COSE SONE SAMP.
tachment 1	Item ID	Description	BFSA EOL Q	uotation 10-	-5-2024 List -10%	Unit Sell	Qty	Extended Sell	KEYLITE ONE & Licrosic Code State Study - Fluid Desay State Study - Study Maint. Scope/Comments
	Item ID	Description				Unit Sell	Qty	Extended Sell	POWER & LIGHTING CORP. Souri Strang - Parcel Strang Stay Strang
m		Description				Unit Sell	Qty	Extended Sell	POWER & LIGHTING CORP. Souri Strang - Parcel Strang Stay Strang
m 700	Item ID MIRAMAR 17533	Description TX2020R-P				Unit Sell	Qty	Extended Sell	POWER & LIGHTING CORP. Souri Strang - Parcel Strang Stay Strang
700	MIRAMAR		Mfg	List	List -10%				Maint. Scope/Comments
700 701 702 703	MIRAMAR 17533 17543 3859	TX2020R-P	Mfg	\$2,989.00 \$792.00 \$766.32	\$2,690.10 \$712.80 \$689.69	\$2,690.10 \$712.80 \$689.69	1	\$2,690.10 \$712.80 \$1,379.38	Maint. Scope/Comments Replace CMM5 Replace CMM5 New
700 701 702 703 704	MIRAMAR 17533 17543 3859 59251	TX2020R-P ADVRP-5 930 watt supply GPS (CM pulse)	Mfg Cambium Cambium Cambium Cambium	\$2,989.00 \$792.00 \$766.32 \$336.93	\$2,690.10 \$712.80 \$689.69 \$303.24	\$2,690.10 \$712.80 \$689.69 \$303.24	1 1	\$2,690.10 \$712.80 \$1,379.38 \$303.24	Maint. Scope/Comments Replace CMM5 Replace CMM5
700 701 702 703 704 705	MIRAMAR 17533 17543 3859 59251 47431	TX2020R-P ADVRP-5 930 watt supply GPS (CN pulse) GPS-TMG-HR-26N-100	Cambium Cambium Cambium Cambium PC-Tel	\$2,989.00 \$792.00 \$766.32 \$336.93 \$326.29	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66	1 1 2 1	\$2,690.10 \$712.80 \$1,379.38 \$303.24 \$293.66	Maint. Scope/Comments Replace CMM5 Replace CMM5 New New Replace existing
700 701 702 703 704 705 706 707 707 708 709	MIRAMAR 17533 17543 3859 59251 47431 69355	TX2020R-P ADVRP-5 930 watt supply GPS (CN pulse) GPS-TMG-HR-26N-100 GPS-TMR/SMA-100-RA	Cambium Cambium Cambium Cambium Cambium Mobilecomm	\$2,989.00 \$792.00 \$766.32 \$336.93 \$326.29 \$245.72	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15	1 1 2 1 1	\$2,690.10 \$712.80 \$1,379.38 \$303.24 \$293.66 \$221.15	Maint. Scope/Comments Replace CMM5 Replace CMM5 New New Replace existing Replace existing Replace existing
700 701 702 703 704 705 706 707	MIRAMAR 17533 17543 3859 59251 47431 69355 69357	TX2020R-P ADVRP-5 930 wast supply GPS (CN pulse) GPS-TMG-HR-26N-100 GPS-LMR/SMA-100-RA GPS-cable-CATS-C	Cambium Cambium Cambium Cambium Cambium PC-Tel Mobilecomm Mobilecomm	\$2,989.00 \$792.00 \$766.32 \$336.93 \$326.29 \$245.72 \$65.00	\$2,690.10 \$712.80 \$689.69 \$303.24 \$221.15 \$58.50	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50	1 1 2 1 1 1	\$2,690.10 \$712.80 \$1,379.38 \$303.24 \$293.66 \$221.15 \$58.50	Replace CMM5 Replace CMM5 Replace Existing Replace existing Replace existing Replace existing Replace existing
700 701 702 703 704 705 706 707 708	MIRAMAR 17533 17543 3859 59251 47431 69355 69357 17373	TX2020R-P ADVRP-5 930 wett supply GPS (CM pulse) GPS-TMG-HR-26M-100 GPS-LMR/SMM-100-RA GPS-Cable-CATS-C GPS mount	Cambium Cambium Cambium Cambium Cambium PC-Tel Mobilecomm Mobilecomm Cambum	\$2,989.00 \$792.00 \$766.32 \$336.93 \$326.29 \$245.72 \$65.00 \$38.65	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79	1 1 2 1 1 1 1	\$2,690.10 \$712.80 \$1,379.38 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79	Maint. Scope/Comments Replace CMM5 Replace CMM5 New New Replace existing Replace existing Replace existing Replace existing Replace existing
700 701 702 703 704 705 706 707 708	MIRAMAR 17533 17543 3859 59251 47431 69355 69357 17373 59733	TX2020R-P ADVRP-5 990 watt supply GPS (CN pulse) GPS-TMG-HR-26N-100 GPS-TMR/SMA-100-RA GPS cable-CATS-C GPS mount SPF10GSR modules	Cambium Cambium Cambium Cambium Cambium Cambium Mobilecomm Cambium Cambuim	\$2,989.00 \$792.00 \$796.32 \$336.93 \$326.29 \$245.72 \$65.00 \$38.65 \$153.99	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59	1 1 2 1 1 1 1 1 4	\$2,690.10 \$712.80 \$1,379.38 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$554.36	Maint. Scope/Comments Replace CMM5 Replace CMM5 New New Replace existing New New
700 701 702 703 704 705 706 707 708 709 710	MIRAMAR 17533 17543 3859 59251 47431 69355 69357 17373 59733 6406	TX2020R-P ADVRP-5 930 watt supply GPS (CN pulse) GPS-TMG-HR-26N-100 GPS-LMR/SMA-100-RA GPS-cable-CATS-C GPS mount SPF10GSR modules Fiber jumpers-LC	Mfg Cambium Cambium Cambium Cambium Cambium PC-Tel Mobilecomm Mobilecomm Cambuim Cambuim Cambuim Missc	\$2,989.00 \$792.00 \$766.32 \$336.93 \$326.29 \$245.72 \$65.00 \$38.65 \$153.99 \$27.56	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$24.80	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80	1 1 2 1 1 1 1 1 1 4	\$2,690.10 \$712.80 \$1,379.38 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$554.36 \$49.61	Replace CMM5 Replace CMM5 Replace CMM5 Replace EMIS Replace EMIS New Replace existing Replace New
700 701 702 703 704 705 706 707 708 709 710	MIRAMAR 17533 17543 3859 59251 47431 69355 69357 17373 59733 6406 61541	TX2020R-P ADVRP-5 930 wett supply GPS (CM pulse) GPS-TMG-HR-26M-100 GPS-TMG-HR-26M-100 GPS-LMR/SMA-100-RA GPS cable-CATS-C GPS mount SPF1JOSSR modules Fiber jumpers-LC Surger protector-CATS	Mfg Cambium Cambium Cambium Cambium PC-Tel Mobilecomm Mobilecomm Cambuim Cambuim Mobilecomm Mobilecomm Mobilecomm Misc	\$2,989.00 \$792.00 \$796.32 \$336.93 \$326.29 \$245.72 \$65.00 \$38.65 \$153.99 \$27.56 \$58.59	\$2,690.10 \$712.80 \$689.69 \$303.24 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73	1 1 2 1 1 1 1 1 4 2	\$2,690.10 \$712.80 \$1,379.38 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$554.36 \$49.61 \$52.73	Replace CMM5 Replace CMM5 Replace CMM5 New New Replace existing Replace with the third
700 701 701 702 703 704 705 706 707 708 709 711 711	MIRAMAR 17533 17543 3859 59251 47431 69355 69357 17373 59733 6406 61541 61543	TX2020R-P ADVRP-5 990 watt supply GPS (CN pulse) GPS-TMG-HR-26N-100 GPS-TMR/SMA-100-RA GPS cable-CAT5-C GPS mount SPF10GSR modules Fiber jumpers-LC Surger protector-CAT5 Surge protector-GPS	Cambium Cambium Cambium Cambium Cambium Cambium Cambium Cambium Mobilecomm Mobilecomm Cambuim Cambuim Cambuim Misc Misc Misc	\$2,989.00 \$792.00 \$766.32 \$336.93 \$326.29 \$245.72 \$65.00 \$38.65 \$153.99 \$27.56 \$58.59 \$195.99	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73 \$176.39	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73 \$176.39	1 1 2 1 1 1 1 1 4 2 1 1	\$2,690.10 \$712.80 \$1,379.38 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$554.36 \$49.61 \$55.73 \$176.39	Replace CMM5 Replace existing Replace wisting New New New New New New
700 701 702 703 704 705 706 707 708 709 710 711 711 712	MIRAMAR 17533 17543 3859 59251 47431 69355 69357 17373 59733 6406 61541	TX2020R-P ADVRP-5 930 wett supply GPS (CM pulse) GPS-TMG-HR-26M-100 GPS-TMG-HR-26M-100 GPS-LMR/SMA-100-RA GPS cable-CATS-C GPS mount SPF1JOSSR modules Fiber jumpers-LC Surger protector-CATS	Mfg Cambium Cambium Cambium Cambium PC-Tel Mobilecomm Mobilecomm Cambuim Cambuim Mobilecomm Mobilecomm Mobilecomm Misc	\$2,989.00 \$792.00 \$796.32 \$336.93 \$326.29 \$245.72 \$65.00 \$38.65 \$153.99 \$27.56 \$58.59	\$2,690.10 \$712.80 \$689.69 \$303.24 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73	1 1 2 1 1 1 1 1 4 2	\$2,690.10 \$712.80 \$1,379.38 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$554.36 \$49.61 \$52.73	Replace CMM5 Replace CMM5 Replace CMM5 New New Replace existing Replace with the third
700 701 702 703 704 705 706 707 708 709 710 711 711 712	MIRAMAR 17533 17543 3859 59251 47431 69355 69357 17373 59733 6406 61541 61543 11612	TX2020R-P ADVRP-5 930 watt supply GPS (CN pulse) GPS-TMG-HR-26N-100 GPS-LMR/SMM-100-RA GPS-CATS-C GPS mount SPF10GSR modules Fiber jumpers-LC Surger protector-CATS Surge protector-GPS Shops supplies	Cambium Cambium Cambium Cambium Cambium PC-Tel Mobilecomm Cambuim Cambuim Cambuim Cambuim Cambuim Misc Misc Misc Misc	\$2,989.00 \$792.00 \$766.32 \$336.99 \$245.72 \$65.00 \$38.65 \$153.99 \$27.56 \$58.59 \$195.99 \$125.00	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50	1 1 2 1 1 1 1 1 1 4 2 1 1	\$2,690.10 \$712.80 \$1,379.38 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$554.36 \$49.61 \$52.73 \$112.50	Maint. Scope/Comments Replace CMM5 Replace CMM5 Replace CMM5 New New New Replace existing Replace existing Replace existing Replace existing New
700 701 702 703 704 705 706 707 708 709 710 711 711 712	MIRAMAR 17533 17543 3859 59251 47431 69355 69357 17373 59733 6406 61541 61543 11612	TX2020R-P ADVRP-5 930 watt supply GPS (CN pulse) GPS-TMG-HR-26N-100 GPS-LMR/SMM-100-RA GPS-CATS-C GPS mount SPF10GSR modules Fiber jumpers-LC Surger protector-CATS Surge protector-GPS Shops supplies	Cambium Cambium Cambium Cambium Cambium PC-Tel Mobilecomm Cambuim Cambuim Cambuim Cambuim Cambuim Misc Misc Misc Misc	\$2,989.00 \$792.00 \$766.32 \$336.99 \$245.72 \$65.00 \$38.65 \$153.99 \$27.56 \$58.59 \$195.99 \$125.00	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50	1 1 2 1 1 1 1 1 1 4 2 1 1	\$2,690.10 \$712.80 \$1,379.38 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$554.36 \$49.61 \$52.73 \$116.39 \$112.50 \$50.00	Maint. Scope/Comments Replace CMM5 Replace CMM5 Replace CMM5 New New New Replace existing Replace existing Replace existing Replace existing New
700 701 702 703 704 705 706 707 708 709 711 712 713 714	MIRAMAR 17533 17543 3859 59251 47431 69355 69355 69357 17373 59733 6406 61541 61543 11612 9996	TX2020R-P ADVRP-S 930 watt supply GPS (CN pulse) GPS-TMG-HR-26N-100 GPS-MMR/SMA-100-RA GPS cable-CATS-C GPS mount SPF10GSR modules Fiber jumpers-LC Surger protector-CATS Surge protector-GPS Shop supplies Misc. Risk	Cambium Cambium Cambium Cambium Cambium PC-Tel Mobilecomm Cambuim Cambuim Cambuim Cambuim Cambuim Misc Misc Misc Misc	\$2,989.00 \$792.00 \$766.32 \$336.99 \$245.72 \$65.00 \$38.65 \$153.99 \$27.56 \$58.59 \$195.99 \$125.00	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50	1 1 2 1 1 1 1 1 1 4 2 1 1	\$2,690.10 \$712.80 \$1,379.38 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$554.36 \$49.61 \$52.73 \$116.39 \$112.50 \$50.00	Maint. Scope/Comments Replace CMM5 Replace CMM5 Replace CMM5 New New New Replace existing Replace existing Replace existing Replace existing New
700 701 701 702 703 704 705 706 707 708 709 711 712 713 714	MIRAMAR 17533 17543 3859 59251 47431 69355 69357 17373 59733 6406 61541 61543 11612 9996	TX2020R-P ADVRP-5 930 watt supply GPS (CN pulse) GPS-TMG-HR-26N-100 GPS-TMR/SMA-100-RA GPS cable-CATS-C GPS mount SPF10GSR modules Fiber jumpers-LC Surger protector-CATS Surge protector-CPS Shop supplies Misc. Risk	Mfg Cambium Cambium Cambium Cambium PC-Tel Mobilecomm Cambuim Cambuim Cambuim Mobilecomm Cambuim Misc Misc Misc Misc Misc	\$2,989.00 \$792.00 \$766.32 \$336.93 \$326.29 \$245.72 \$555.00 \$38.65 \$153.99 \$27.56 \$58.59 \$195.90 \$125.00 \$0.00	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50 \$0.00	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73 \$1176.39 \$112.50 \$0.00	1 1 2 1 1 1 1 1 4 2 1 1 1 1 1 1 1 1 1 1	\$2,690.10 \$712.80 \$1,379.38 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$554.36 \$49.61 \$52.73 \$176.39 \$112.50 \$0.00	Replace CMM5 Replace CMM5 Replace CMM5 Replace CMM5 Replace EMISING Replace existing New New New New New Temp1
700 701 702 703 704 705 706 707 708 709 710 711 712 713 714	MIRAMAR 17533 17543 3859 59251 47431 69355 69357 17373 59733 6406 61541 61543 11612 9996	TX2020R-P ADVRP-5 930 watt supply GPS (CM pulse) GPS-TMG-HR-26M-100 GPS-TMG-HR-26M-100 GPS-TMG-HR-26M-100 GPS-DHR/SMA-100-RA GPS cable-CATS-C GPS mount SPF100SR modules Fiber jumpers-LC Surger protector-CATS Surge protector-GPS Shop supplies Misc. Risk	Mfg Cambium Cambium Cambium Cambium PC-Tel Mobilecomm Cambuim Cambuim Cambuim Mobilecomm Cambuim Cambuim Cambuim Misc Misc Misc Misc Misc Cambium Cambium Misc Misc Misc Misc Misc Misc Misc Misc	\$2,989.00 \$792.00 \$766.32 \$336.93 \$326.29 \$245.72 \$65.00 \$38.65 \$153.99 \$27.56 \$58.59 \$195.99 \$195.99 \$195.90 \$0.00	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50 \$0.00	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50 \$0.00	1 1 2 1 1 1 1 1 4 2 2 1 1 1 1 1 1 1 1 1	\$2,690.10 \$712.80 \$1,379.38 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$554.36 \$49.61 \$52.73 \$176.39 \$112.50 \$0.00 \$6,639.	Replace CMM5 Replace CMM5 Replace CMM5 Replace CMM5 Replace CMM5 Replace existing Replace wisting Replace wisting Replace Existing Replace Existing Replace Existing Replace Existing Replace Existing New New New New New New Replace CMM5
700 701 702 703 704 705 706 707 708 709 711 712 713 714 800 801	MIRAMAR 17533 17543 3859 59251 47431 69355 69357 17373 59733 6406 61541 61543 11612 9996 MARKHAM F 17533 17543	TX2020R-P ADVRP-S 930 watt supply GPS (CN pulse) GPS-TMG-HR-26N-100 GPS-MMR/SMA-100-RA GPS cable-CATS-C GPS mount SPF10GSR modules Fiber jumpers-LC Surger protector-CATS Surge protector-CATS Surge protector-GPS Shop supplies Misc. Risk	Mfg Cambium Cambium Cambium Cambium PC-Tel Mobilecomm Mobilecomm Cambuim Misc Misc Misc Misc Misc Misc Cambium Cambuim Cambuim Cambuim Cambuim Misc Misc	\$2,989.00 \$792.00 \$766.32 \$336.93 \$326.29 \$245.72 \$65.00 \$38.65 \$153.99 \$27.56 \$58.59 \$125.00 \$0.00	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73 \$112.50 \$0.00	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$88.50 \$34.79 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50 \$0.00	1 1 2 1 1 1 1 1 4 2 2 1 1 1 1 1 1 1 1 1	\$2,690.10 \$1,379.38 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$554.36 \$49.61 \$52.73 \$176.39 \$112.50 \$0.00 \$6,639.	Replace CMM5 Replace existing Replace EX
700 701 702 703 704 705 706 707 708 709 711 711 711 712 713 714 800 801	MIRAMAR 17533 17543 3859 59251 47431 69355 69357 17373 59733 6406 61541 61543 11612 9996 MARKHAM F 17533 17543	TX2020R-P ADVRP-5 930 watt supply GPS (CN pulse) GPS-TMG-HR-26N-100 GPS-TMG-MA-100-RA GPS cable-CATS-C GPS mount SPF10GSR modules Fiber jumpers-LC Surger protector-CATS Surge protector-CPS Shop supplies Misc. Risk TX2020R-P ADVRP-5 930 watt supply	Mfg Cambium Cambium Cambium Cambium PC-Tel Mobilecomm Cambuim Cambuim Cambuim Mobilecomm Cambuim	\$2,989.00 \$792.00 \$766.32 \$336.93 \$326.29 \$245.72 \$565.00 \$38.65 \$153.99 \$27.56 \$58.59 \$195.99 \$195.90 \$0.00	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50 \$0.00	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73 \$112.50 \$0.00	1 1 2 2 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1	\$2,690.10 \$712.80 \$1,379.38 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$554.36 \$49.61 \$52.73 \$112.50 \$0.00 \$6,639.	Replace CMM5 Replace existing New New New New New New Replace CMM5
700 701 702 703 704 705 706 707 708 709 710 711 711 711 714 800 801 802 803	MIRAMAR 17533 17543 3859 59251 47431 69355 69357 17373 59733 6406 61541 61543 11612 9996 MARKHAM F 17533 17543 3859	TX2020R-P ADVRP-5 930 wett supply GPS (CM pulse) GPS-TMG-HR-26H-100 GPS-TMG-HR-26H-100 GPS-TMG-HR-26H-100 GPS-TMG-HR-26H-100 GPS-TMG-HR-26H-100 GPS-TMG-HR-26H-100 GPS-TMG-HR-26H-100 GPS-TMG-HR-26H-100 SPF10GSR modules Fiber jumpers-LC Surger protector-CATS Surge protector-CATS Surge protector-CFS Shop supplies Misc. Risk TX2020R-P ADVRP-5 930 watt supply GPS (CM pulse)	Mfg Cambium Cambium Cambium Cambium PC-Tel Mobilecomm Cambuim Cambium	\$2,989.00 \$792.00 \$766.32 \$336.93 \$326.29 \$245.72 \$65.00 \$38.65 \$153.99 \$27.56 \$5153.99 \$27.56 \$5153.99 \$27.56 \$5153.99 \$27.56 \$5153.99 \$27.56 \$5153.99 \$27.56 \$5153.99 \$27.56 \$5153.99 \$27.56 \$5153.99 \$27.56 \$5153.99 \$27.56 \$5153.99 \$27.56 \$	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50 \$0.00	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50 \$0.00	1 1 1 2 2 1 1 1 1 1 4 2 1 1 1 1 1 1 1 1	\$2,690.10 \$712.80 \$1,379.38 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$554.36 \$49.61 \$52.73 \$176.39 \$112.50 \$0.00 \$6,639.	Replace CMM5 Replace CMM5 Replace CMM5 Replace CMM5 Replace existing New
700 701 702 703 704 705 706 707 708 709 711 712 713 714 800 801 802 803 804	MIRAMAR 17533 17543 3859 59251 47431 69355 69355 69357 17373 59733 6406 61541 61543 11612 9996 MARKHAM F 17533 17543 3859	TX2020R-P ADVRP-S 990 watt supply GPS (CN pulse) GPS-TMG-HR-26N-100 GPS-MM/SMA-100-RA GPS-cable-CATS-C GPS mount SPF10GSR modules Fiber jumpers-LC Surger protector-CATS Surge protector-CATS Surge protector-GPS Shop supplies Misc. Risk TX2020R-P ADVRP-S 990 watt supply GPS-TMG-HR-26N-100	Mfg Cambium Cambium Cambium Cambium PC-Tel Mobilecomm Cambuim Misc Misc Misc Misc Misc Cambium Cambuim Cambuim Cambuim Cambuim Cambium	\$2,989.00 \$792.00 \$766.32 \$336.93 \$246.29 \$245.72 \$655.00 \$38.65 \$153.99 \$27.56 \$58.59 \$125.00 \$0.00 \$766.32 \$38.65 \$195.99 \$125.00 \$766.32 \$792.00 \$766.32 \$792.00 \$766.32 \$786.93	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73 \$112.50 \$50.00	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50 \$0.00	1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1	\$2,690.10 \$1,379.38 \$303.24 \$293.66 \$221.15 \$58.50 \$347.79 \$554.36 \$49.61 \$52.73 \$176.39 \$112.50 \$0.00 \$6,639.	Replace CMM5 Replace existing
700 701 702 703 704 705 706 707 708 709 710 711 711 712 713 714 800 801 801 802 803 804 805	MIRAMAR 17533 17543 3859 59251 47431 69355 69357 17373 59733 6406 61541 61543 11612 9996 MARKHAM F 17533 17543 3859 59251 47431	TX2020R-P ADVRP-5 930 watt supply GPS (CN pulse) GPS-TMG-HR-26N-100 GPS-LMR/SMA-100-RA GPS-CADIE-CATS-C GPS mount SPF1DGSR modules Fiber jumpers-LC Surger protector-CATS Surge protector-CPS Shop supplies Misc. Risk TX2020R-P ADVRP-5 930 watt supply GPS (CN pulse) GPS-LMR/SMA-100-RA	Mfg Cambium Cambium Cambium Cambium PC-Tel Mobilecomm Cambuim Cambium	\$2,989.00 \$792.00 \$766.32 \$336.93 \$326.29 \$245.72 \$655.00 \$38.65 \$153.99 \$27.56 \$88.59 \$195.99 \$1125.00 \$792.00 \$792.00 \$766.32 \$336.93 \$336.93 \$336.93 \$336.93 \$326.29 \$326.29 \$326.29	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50 \$0.00	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50 \$0.00	1 1 1 2 2 1 1 1 1 1 2 1 1 1 1 1 1 1 1 1	\$2,690.10 \$712.80 \$1,379.38 \$303.24 \$293.66 \$221.15 \$58.50 \$534.79 \$554.36 \$49.61 \$52.73 \$176.39 \$112.50 \$0.00 \$6,639.	Replace CMM5 Replace existing New New New New New New New Replace CMM5 Replace existing Replace existing Replace existing Replace existing Replace existing Replace existing
700 701 702 703 704 705 705 706 707 708 709 711 711 713 714 800 801 802 803 804 805 806 807	MIRAMAR 17533 17543 3859 59251 47431 69355 69357 17373 59733 6406 61541 61543 11612 9996 MARKHAM F 17533 17543 3859 59251 47431 69355	TX2020R-P ADVRP-S 930 watt supply GPS (CM pulse) GPS-TMG-HR-26M-100 GPS-TMG-HR-26M-100 GPS-TMG-HR-26M-100 GPS-TMG-HR-26M-100 GPS-TMG-HR-26M-100 GPS mount SPF10GSR modules Fiber jumpers-LC Surger protector-CATS Surge protector-CATS Surge protector-GPS Shop supplies Misc. Risk PARK TX2020R-P ADVRP-S 930 watt supply GPS-TMG-HR-26M-100 GPS-LMR/SMA-100-RA GPS-Cable-CATS-C	Mfg Cambium Cambium Cambium Cambium PC-Tel Mobilecomm Cambuim Cambuim Cambuim Cambuim Cambuim Cambuim Cambuim Cambuim Cambuim Cambium PC-Tel Mobilecomm	\$2,989.00 \$792.00 \$766.32 \$336.29 \$245.72 \$65.00 \$38.65 \$153.99 \$27.56 \$58.59 \$195.99 \$1195.99 \$1195.99 \$1195.99 \$125.00 \$792.00 \$792.00 \$786.32 \$336.	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50 \$0.00	\$2,690.10 \$712.80 \$689.69 \$303.24 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50 \$0.00 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15	1 1 1 2 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1	\$2,690.10 \$1,379.38 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$554.36 \$49.61 \$52.73 \$176.39 \$112.50 \$0.00 \$6,639. \$2,690.10 \$712.80 \$1,379.38 \$303.24 \$293.66 \$221.15	Replace CMM5 Replace CMM5 Replace CMM5 Replace existing
700 701 702 703 704 705 706 707 708 709 7110 711 712 713 714 800 801 802 803 804 805 807 808	MIRAMAR 17533 17543 3859 59251 47431 69355 69357 17373 6406 61541 61543 11612 9996 MARKHAM F 17533 3859 59251 47431 69355 69357	TX2020R-P ADVRP-5 990 wast supply GPS (CN pulse) GPS-TMG-HR-26N-100 GPS-MMS/SMA-100-RA GPS cable-CAT5-C GPS mount SPF10GSR modules Fiber jumpers-LC Surger protector-CAT5 Surge protector-GPS Shop supplies Misc. Risk TX2020R-P ADVRP-5 990 wast supply GPS-TMG-HR-26N-100 GPS-LMR/SMM-100-RA GPS-CABLE-CATS-C GPS mount	Mfg Cambium Cambium Cambium Cambium Cambium PC-Tel Mobilecomm Mobilecomm Cambuim Misc Misc Misc Misc Misc Cambium	\$2,989.00 \$792.00 \$766.32 \$336.93 \$326.29 \$245.72 \$65.00 \$38.65 \$153.99 \$27.56 \$58.59 \$125.00 \$0.00 \$766.32 \$38.65	\$2,690.10 \$712.80 \$689.69 \$222.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73 \$112.50 \$0.00 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$4.80 \$52.73 \$176.39 \$112.50 \$58.50 \$59	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$7221.15 \$88.50 \$34.79 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50 \$0.00 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$2,690.10 \$712.80 \$689.69 \$303.24 \$233.66 \$221.15 \$33.79	1 1 1 2 2 1 1 1 1 1 2 1 1 1 1 1 1 1 1 1	\$2,690.10 \$712.80 \$1,379.38 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$554.36 \$49.61 \$552.23 \$176.39 \$112.50 \$0.00 \$6,639. \$2,690.10 \$712.80 \$1,379.38 \$303.24 \$293.66 \$221.15 \$36.50	Replace CMM5 Replace existing
700 701 702 703 704 705 706 707 708 709 710 711 711 712 713 714 800 801 802 803 804 805 806 807 808	MIRAMAR 17533 17543 3859 59251 47431 69355 69357 17373 6906 61541 61543 11612 9996 MARKHAM F 17533 17543 3859 59251 47431 69355 69357 17373	TX2020R-P ADVRP-5 930 watt supply GPS (CM pulse) GPS-TMG-HR-26N-100 GPS-LMR/SMA-100-RA GPS-cable-CATS-C GPS mount SPF1DGSR modules Fiber jumpers-LC Surger protector-CATS Surge protector-CPS Shop supplies Misc. Risk TX2020R-P ADVRP-5 930 watt supply GPS (CN pulse) GPS-TMG-HR-26N-100 GPS-LMR/SMA-100-RA GPS cable-CATS-C GPS mount SPF1DGSR modules	Mfg Cambium Cambium Cambium Cambium PC-Tel Mobilecomm Cambuim Cambuim Cambuim Cambuim Cambuim Cambuim Cambuim Cambuim Cambuim Cambium	\$2,989.00 \$792.00 \$766.32 \$336.93 \$326.29 \$245.72 \$650.00 \$38.65 \$153.99 \$27.56 \$8.59 \$195.99 \$1125.00 \$792.00 \$766.32 \$336.93 \$326.29 \$245.75 \$336.93 \$326.29 \$245.76 \$38.65 \$3	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50 \$0.00	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50 \$0.00 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$158.50 \$158	1 1 1 2 1 1 1 1 1 4 2 2 1 1 1 1 1 1 1 1	\$2,690.10 \$712.80 \$1,379.38 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$554.36 \$49.61 \$52.73 \$176.39 \$112.50 \$0.00 \$6,639. \$2,690.10 \$712.80 \$1,379.38 \$303.24 \$293.66 \$221.15 \$555.50 \$34.79 \$555.50 \$34.79 \$555.73 \$75	Replace CMM5 Replace CMM5 Replace CMM5 Replace CMM5 Replace existing
700 701 702 703 704 705 706 707 708 709 711 712 713 714 800 801 802 803 804 805 806 807 808	MIRAMAR 17533 17543 3859 59251 47431 69355 69357 17373 6406 61541 61543 11612 9996 MARKHAM F 17533 3859 59251 47431 69355 69357	TX2020R-P ADVRP-S 930 watt supply GPS (CN pulse) GPS-TMG-HR-26H-100 GPS-TMG-HR-26H-100 GPS-TMG-HR-26H-100 GPS-TMG-HR-26H-100 GPS-TMG-HR-26H-100 GPS mount SPF10GSR modules Fiber jumpers-LC Surger protector-CATS Surge protector-GPS Shop supplies Misc. Risk PARK TX2020R-P ADVRP-S 930 watt supply GPS (CN pulse) GPS-TMG-HR-26H-100 GPS	Mfg Cambium Cambium Cambium Cambium Cambium PC-Tel Mobilecomm Mobilecomm Cambuim Misc Misc Misc Misc Misc Cambium	\$2,989.00 \$792.00 \$766.32 \$336.93 \$326.29 \$245.72 \$65.00 \$38.65 \$153.99 \$27.56 \$58.59 \$125.00 \$0.00 \$766.32 \$38.65	\$2,690.10 \$712.80 \$689.69 \$222.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73 \$112.50 \$0.00 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$4.80 \$52.73 \$176.39 \$112.50 \$58.50 \$59	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$7221.15 \$88.50 \$34.79 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50 \$0.00 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$2,690.10 \$712.80 \$689.69 \$303.24 \$233.66 \$221.15 \$33.79	1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1	\$2,690.10 \$712.80 \$1,379.38 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$554.36 \$49.61 \$552.23 \$176.39 \$112.50 \$0.00 \$6,639. \$2,690.10 \$712.80 \$1,379.38 \$303.24 \$293.66 \$221.15 \$36.50	Replace CMM5 Replace existing
700 701 702 703 704 705 706 707 708 709 711 712 713 714 800 801 801 802 803 804 805 806 807 808 809 810	MIRAMAR 17533 17543 3859 59251 47431 69355 69357 17373 59733 6406 61541 61543 11612 9996 MARKHAM F 17533 17543 3859 59251 47431 69355 69357 17373 59733 6406	TX2020R-P ADVRP-5 930 watt supply GPS (CM pulse) GPS-TMG-HR-26N-100 GPS-LMR/SMA-100-RA GPS-cable-CATS-C GPS mount SPF1DGSR modules Fiber jumpers-LC Surger protector-CATS Surge protector-CPS Shop supplies Misc. Risk TX2020R-P ADVRP-5 930 watt supply GPS (CN pulse) GPS-TMG-HR-26N-100 GPS-LMR/SMA-100-RA GPS cable-CATS-C GPS mount SPF1DGSR modules	Cambium Cambium Cambium Cambium Cambium PC-Tel Mobilecomm Cambuim Cambuim Misc Misc Misc Misc Misc Misc Misc Misc	\$2,989.00 \$792.00 \$766.32 \$336.93 \$236.29 \$245.72 \$65.00 \$38.65 \$153.99 \$125.00 \$766.32 \$36.93 \$27.56 \$58.59 \$125.00 \$792.00 \$766.32 \$336.93 \$326.29 \$245.72 \$65.00 \$38.65 \$38.6	\$2,690.10 \$712.80 \$689.69 \$233.24 \$293.66 \$221.15 \$58.50 \$138.59 \$24.80 \$52.73 \$112.50 \$0.00 \$712.80 \$689.69 \$221.15 \$689.69 \$221.15 \$689.69 \$221.15 \$689.69 \$221.15 \$689.69 \$221.15 \$689.69 \$221.15 \$689.69 \$221.15 \$689.69 \$221.15 \$233.66 \$222.15 \$233.66 \$233.66 \$	\$2,690.10 \$712.80 \$589.69 \$303.24 \$223.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50 \$0.00 \$712.80 \$589.69 \$221.15 \$50.00	1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1	\$2,690.10 \$712.80 \$1,379.38 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$554.36 \$49.61 \$52.73 \$112.50 \$0.00 \$6,639. \$2,690.10 \$712.80 \$1,379.38 \$303.24 \$293.66 \$221.15 \$303.24 \$293.66 \$203.24 \$203	Replace CMM5 Replace existing New New New New New Replace CMM5 Replace existing
700 701 702 703 704 705 705 706 707 708 709 710 711 712 713 714 800 801 802 803 804 805 806 807 808 809 810	MIRAMAR 17533 17543 3859 59251 47431 69355 69357 17373 59733 6406 61541 61543 11612 9996 MARKHAM F 17533 17543 3859 59251 47431 69355 69357 17373 59733 6406 61541	TX2020R-P ADVRP-5 930 watt supply GPS (CN pulse) GPS (CN pulse) GPS-TMG-HR-26H-100 GPS-TMG-HR-26H-100 GPS-TMG-HR-26H-100 GPS-TMG-HR-26H-100 GPS-TMG-HR-26H-100 GPS-TMG-HR-26H-100 SPF10GSR modules Fiber jumpers-LC Surger protector-CATS Surge protector-CATS Surge protector-CATS Surge protector-CATS MISC. RISK TX2020R-P ADVRP-5 930 watt supply GPS (CN pulse) GPS-TMG-HR-26H-100 GPS-TMG-HR-100 GPS-TM	Mfg Cambium Cambium Cambium Cambium Cambium PC-Tel Mobilecomm Cambuim Cambuim Cambuim Cambuim Cambuim Cambuim Cambuim Cambuim Misc Misc Misc Misc Misc Misc Misc Misc	\$2,989.00 \$792.00 \$766.32 \$336.29 \$245.72 \$555.00 \$38.65 \$153.99 \$125.00 \$50.00 \$766.32 \$36.59 \$153.99 \$125.00 \$0.00 \$792.0	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73 \$112.50 \$0.00	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50 \$0.00 \$712.80 \$689.69 \$303.24 \$23.66 \$221.15 \$58.50 \$10.25 \$1	1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1	\$2,690.10 \$712.80 \$1,379.38 \$303.24 \$293.66 \$221.15 \$58.50 \$534.79 \$554.36 \$49.61 \$52.73 \$176.39 \$112.50 \$0.00 \$6,639. \$2,690.10 \$712.80 \$1,379.38 \$303.24 \$221.15 \$55.50 \$34.79 \$554.36 \$249.61 \$552.73	Replace CMM5 Replace existing New New New New New New Replace EMM5 Replace existing New New New New New New New New New

ttachment 1	nt 1 BFSA EOI		BFSA EOL Q	DL Quotation 10-5-2024					KEYLITE POWER & LICHTING CORP State Strong - Punid Strong	
em	Item ID	Description	Mfg	List	List -10%	Unit Sell	Qty	Extended Sell	Maint. Scope/Comments	
	WEST	WOOD.								
	WEST HOLLYW			An an	laa ee	40.50	T .	40.500.40	la 1 aure	
	17533	TX2020R-P	Cambium	\$2,989.00	\$2,690.10	\$2,690.10	1	\$2,690.10	Replace CMM5	
	17543	ADVRP-5	Cambium	\$792.00	\$712.80	\$712.80	1	\$712.80	Replace CMM5	
	3859	930 watt supply	Cambium	\$766.32	\$689.69	\$689.69	2	\$1,379.38	New	
	59251	GPS (CN pulse)	Cambium	\$336.93	\$303.24	\$303.24	1	\$303.24	New	
	47431	GPS-TMG-HR-26N-100	PC-Tel	\$326.29	\$293.66	\$293.66	1	\$293.66	Replace existing	
	69355	GPS-LMR/SMA-100-RA	Mobilecomm	\$245.72	\$221.15	\$221.15	1	\$221.15	Replace existing	
	69357	GPS cable-CAT5-C	Mobilecomm	\$65.00	\$58.50	\$58.50	1	\$58.50	Replace existing	
	17373	GPS mount	Cambuim	\$38.65	\$34.79	\$34.79	1	\$34.79	Replace existing	
	59733	SPF10GSR modules	Cambuim	\$153.99	\$138.59	\$138.59	4	\$554.36	New	
	6406	Fiber jumpers-LC	Misc	\$27.56	\$24.80	\$24.80	2	\$49.61	New	
	61541	Surger protector-CAT5	Misc	\$58.59	\$52.73	\$52.73	1	\$52.73	New	
	61543	Surge protector-GPS	Misc	\$195.99	\$176.39	\$176.39	1	\$176.39	New	
	11612	Shop supplies	Misc	\$125.00	\$112.50	\$112.50	1	\$112.50	New	
914	9996	Misc. Risk	Misc	\$0.00	\$0.00	\$0.00	1	\$0.00	Temp1	
								, , , , , , ,		
1000	PLAYA DEL MA	AR								
	17533	TX2020R-P	Cambium	\$2,989.00	\$2,690.10	\$2,690.10	1	\$2,690.10	Replace CMM5	
	17543	ADVRP-5	Cambium	\$792.00	\$712.80	\$712.80	1	\$712.80	Replace CMM5	
	3859	930 watt supply	Cambium	\$766.32	\$689.69	\$689.69	2	\$1,379.38	New	
	59251	GPS (CN pulse)	Cambium	\$336.93	\$303.24	\$303.24	1	\$303.24	New	
	47431	GPS-TMG-HR-26N-100	PC-Tel	\$326.29	\$293.66	\$293.66	1	\$293.66	Replace existing	
1006	69355	GPS-LMR/SMA-100-RA	Mobilecomm	\$245.72	\$221.15	\$221.15	1	\$221.15	Replace existing	
	69357	GPS cable-CAT5-C	Mobilecomm	\$65.00	\$58.50	\$58.50	1	\$58.50	Replace existing	
	17373	GPS mount	Cambuim	\$38.65	\$34.79	\$34.79	1	\$34.79	Replace existing	
1009	59733	SPF10GSR modules	Cambuim	\$153.99	\$138.59	\$138.59	4	\$554.36	New	
1010	6406	Fiber jumpers-LC	Misc	\$27.56	\$24.80	\$24.80	2	\$49.61	New	
1011	61541	Surger protector-CAT5	Misc	\$58.59	\$52.73	\$52.73	1	\$52.73	New	
1012	61543	Surge protector-GPS	Misc	\$195.99	\$176.39	\$176.39	1	\$176.39	New	
1013	11612	Shop supplies	Misc	\$125.00	\$112.50	\$112.50	1	\$112.50	New	
1014	9996	Misc. Risk	Misc	\$0.00	\$0.00	\$0.00	1	\$0.00	Temp1	
								\$6,639.20		
								\$6,633.20		
								\$6,639.20		
ttachment 1			BFSA EOL Q	uotation 10	-5-2024			\$6,635.20	KEYLITE FOWER & LIGHTING CORF	
_	Itams ID	Description				Ilait Call	Otiv		KEYLITE FORME & LICHTING CORP. Start Strang - "Hand Strang Stay Strang	
	item ID	Description	BFSA EOL Q	uotation 10	-5-2024 List -10%	Unit Sell	Qty	Extended Sell		
m						Unit Sell	Qty		KEYLITE FORME & LICHTING CORP. Start Strang - "Hand Strang Stay Strang	
m 1100	POINT OF AMI	ERICAS	Mfg	List	List -10%			Extended Sell	KEYLITE ISSUE & LICITUDE ISS	
m 1100 1101	POINT OF AMI	ERICAS TX2020R-P	Mfg Cambium	List \$2,989.00	List -10% \$2,690.10	\$2,690.10	1	Extended Sell	KEYLITE POMR & LICHTING CORE Total Stage Stage Maint. Scope/Comments Replace CMM5	
1100 1101 1102	POINT OF AMI 17533 17543	ERICAS TX2020R-P ADVRP-5	Mfg Cambium Cambium	\$2,989.00 \$792.00	\$2,690.10 \$712.80	\$2,690.10 \$712.80	1 1	Extended Sell \$2,690.10 \$712.80	REPLACE COMPANY Maint. Scope/Comments Replace CMM5 Replace CMM5	
1100 1101 1102 1103	POINT OF AMI 17533 17543 3859	ERICAS TX2020R-P ADVRP-5 930 watt supply	Cambium Cambium Cambium	\$2,989.00 \$792.00 \$766.32	\$2,690.10 \$712.80 \$689.69	\$2,690.10 \$712.80 \$689.69	1 1 2	Extended Sell 52,690.10 5712.80 51,379.38	KEYLITE ISSUES & LOCATION State Street Maint. Scope/Comments Replace CMM5 Replace CMM5 New	
1100 1101 1102 1103 1104	POINT OF AMI 17533 17543 3859 59251	TX2020R-P ADVRP-5 930 watt supply GPS (CN pulse)	Cambium Cambium Cambium Cambium	\$2,989.00 \$792.00 \$766.32 \$336.93	\$2,690.10 \$712.80 \$689.69 \$303.24	\$2,690.10 \$712.80 \$689.69 \$303.24	1 1 2	\$2,690.10 \$712.80 \$13,79.38 \$303.24	Maint. Scope/Comments Replace CMM5 Replace CMM5 New New	
1100 1101 1102 1103 1104 1105	POINT OF AMI 17533 17543 3859 59251 47431	TX2020R-P ADVRP-5 930 watt supply GPS-(CN pulse) GPS-TMG-HR-26N-100	Mfg Cambium Cambium Cambium Cambium PC-Tel	\$2,989.00 \$792.00 \$766.32 \$336.93 \$326.29	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66	1 1 2 1	Extended Sell \$2,690.10 \$712.80 \$1,379.38 \$303.24 \$293.66	KEYLITE COMMES EXCHANGE Stay - Share Stay Maint. Scope/Comments Replace CMM5 Replace CMM5 New Replace existing	
1100 1101 1102 1103 1104 1105 1106	POINT OF AMI 17533 17543 3859 59251 47431 69355	TX202GR-P ADVRP-S 950 watt supply GPS (CN pulse) GPS-TMG-HR-26N-100 GPS-LMR/SMA-100-RA	Mfg Cambium Cambium Cambium Cambium Cambium PC-Tel Mobilecomm	\$2,989.00 \$792.00 \$766.32 \$336.93 \$326.29 \$245.72	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15	1 1 2 1 1	Extended Sell \$2,690.10 \$712.80 \$1,379.38 \$303.24 \$293.66 \$221.15	Maint. Scope/Comments Replace CMM5 Replace existing Replace existing Replace existing	
1100 1101 1102 1103 1104 1105 1106	POINT OF AMI 17533 17543 3859 59251 47431 69355 69357	TX2020R-P ADVRP-5 930 watt supply GPS (CN pulse) GPS-TMG-HR-26N-100 GPS-MR/SMA-100-RA GPS-CADIS-CATS-C	Cambium Cambium Cambium Cambium Cambium PC-Tel Mobilecomm Mobilecomm	\$2,989.00 \$792.00 \$766.32 \$336.93 \$326.29 \$245.72 \$65.00	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50	1 1 2 1 1 1	\$2,690.10 \$712.80 \$13,793.88 \$303.24 \$293.66 \$221.15 \$588.50	Replace existing	
1100 1101 1102 1103 1104 1105 1106 1107	POINT OF AMI 17533 17543 3859 59251 47431 69355 69357 17373	TX2020R-P ADVRP-5 930 watt supply GPS (CR) pulse) GPS-TMG-HR-26N-100 GPS-LMR/SMM-100-RA GPS cable-CATS-C GPS mount	Mfg Cambium Cambium Cambium Cambium Cambium Po-Tel Mobilecomm Mobilecomm Cambuim	\$2,989.00 \$792.00 \$766.32 \$336.93 \$326.29 \$245.72 \$65.00 \$38.65	\$2,690.10 \$712.80 \$69.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79	\$2,690.10 \$712.80 \$689.69 \$303.24 \$299.66 \$221.15 \$58.50 \$34.79	1 1 2 1 1	Extended Sell \$2,690.10 \$712.80 \$1,379.38 \$500.324 \$293.66 \$221.15 \$58.50 \$58.4.79	Replace existing	
1100 1101 1102 1103 1104 1105 1106 1107 1108	POINT OF AMI 17533 17543 3859 59251 47431 69355 69357 17373 59733	TX202GR-P ADVRP-S 930 watt supply GPS (CN pulse) GPS-TMG-HR-26N-100 GPS-LMR/SMA-100-RA GPS cable-CATS-C GPS mount SPF10GSR modules	Mfg Cambium Cambium Cambium Cambium Cambium PC-Tel Mobilecomm Mobilecomm Cambuim Cambuim	\$2,989.00 \$792.00 \$766.32 \$336.93 \$326.29 \$245.72 \$65.00 \$38.65 \$153.99	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59	1 1 2 1 1 1 1 1 4	Extended Sell 52,690.10 5712.80 51,379.38 5303.24 5293.66 5221.15 588.50 534.79 5554.36	Maint. Scope/Comments Replace CMM5 Replace CMM5 Replace existing	
1100 1101 1102 1103 1104 1105 1106 1107 1108	POINT OF AMI 17533 17543 3859 59251 47431 69355 69357 17373 59733 6406	TX2020R-P ADVRP-5 930 watt supply GPS (CN pulse) GPS-TMG-HR-26N-100 GPS-MR/SMA-100-RA GPS cable-CATS-C GPS mount SPF10GSR modules Fiber jumpers-LC	Mfg Cambium Cambium Cambium Cambium Cambium PC-Tel Mobilecomm Mobilecomm Cambuim Cambuim Cambuim Misc	\$2,989.00 \$792.00 \$766.32 \$336.93 \$326.29 \$245.72 \$65.00 \$38.65 \$153.99 \$27.56	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$88.50 \$34.79 \$138.59 \$24.80	1 1 2 1 1 1 1 1 1 4	S2,690.10 S712.80 S1,379.38 S303.24 S293.66 S221.15 S85.0 S34.79 S54.36 S49.61 S	Replace existing	
1100 1101 1102 1103 1104 1105 1106 1107 1108 11109	POINT OF AMI 17533 17543 3859 59251 47431 69355 69357 17373 59733 6406 6406 61541	TX2020R-P ADVRP-5 930 watt supply GPS (CN pulse) GPS-TMG-HR-26h-1:00 GPS-TMG-HR-26h-1:00 GPS-TMG-HR-26h-1:00 GPS-DBG-HR-26h-1:00 GPS-DBG-HR-26h-1:00 GPS-MBC-MS-1:00-RA GPS cable-CATS-C GPS mount SPF10GSR modules Fiber jumpers-LC Surger protector-CATS	Mfg Cambium Cambium Cambium Cambium Cambium Pc-Tel Mobilecomm Mobilecomm Cambuim Cambuim Cambuim Misc	\$2,989.00 \$792.00 \$796.32 \$336.93 \$326.29 \$35.72 \$65.00 \$38.65 \$153.99 \$27.56 \$58.59	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73	\$2,690.10 \$712.80 \$59.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73	1 1 2 1 1 1 1 1 4 2	Extended Sell \$2,690.10 \$712.80 \$1,379.38 \$303.24 \$293.66 \$221.15 \$58.50 \$58.4.79 \$554.36 \$49.61 \$52.73	Replace CMM5 Replace existing	
1100 1101 1102 1103 1104 1105 1106 1107 1108 1109 1110	POINT OF AMI 17533 17543 3859 59251 47431 69855 69855 69357 17373 59733 6406 61541 61543	TX2020R-P ADVRP-S 930 watt supply GPS (CN pulse) GPS-TMG-HR-26N-100 GPS-LMR/SMA-100-RA GPS cable-CATS-C GPS mount SPF10GSR modules Fiber jumpers-LC Surger protector-CATS Surger protector-GPS	Mfg Cambium Cambium Cambium Cambium PC-Tel Mobilecomm Mobilecomm Cambuim Cambuim Misc Misc Misc	\$2,989.00 \$792.00 \$766.32 \$336.93 \$326.29 \$245.72 \$65.00 \$38.65 \$153.99 \$27.56 \$58.59 \$195.99	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$55.50 \$34.79 \$138.59 \$24.80 \$52.73 \$176.39	1 1 2 1 1 1 1 1 4 2 1	Extended Sell \$2,690.10 \$712.80 \$13,79.38 \$303.24 \$293.66 \$221.15 \$88.50 \$34.79 \$554.36 \$49.61 \$52.73 \$176.39	Replace existing	
1100 1101 1102 1103 1104 1105 1106 1107 1108 1111 1111 1111	POINT OF AMI 17533 17543 3859 59251 47431 69355 69357 17373 59733 6406 61541 61543 11612	TX2020R-P ADVRP-5 930 watt supply GPS (CN pulse) GPS-TMG-HR-26N-100 GPS-TMG-HR-26N-100 GPS-MR/SMA-100-RA GPS cable-CAT5-C GPS mount SPF-10GSR modules Fiber jumpers-LC Surger protector-CAT5 Surge protector-GPS Shop supplies	Mfg Cambium Cambium Cambium Cambium PC-Tel Mobilecomm Mobilecomm Cambuim Cambuim Misc Misc Misc Misc	\$2,989.00 \$792.00 \$766.32 \$336.93 \$326.29 \$245.72 \$65.00 \$38.65 \$153.99 \$27.56 \$58.59 \$195.99 \$125.00	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73 \$176.39	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50	1 1 2 1 1 1 1 1 4 2 1 1 1	S2,690.10 S712.80 S1,379.38 S303.24 S203.24 S203.24 S203.24 S203.24 S203.24 S203.24 S203.25 S8.50 S34.79 S554.36 S40.61 S52.73 S176.39 S112.50 S112.50 S0.75 S112.50 S0.75 S0.75 S112.50 S0.75 S0.	Replace CMM5 Replace existing Replace ex	
m 1100 1101 1102 1103 1104 1105 1106 1107 1108 1109 1111 1111 11112	POINT OF AMI 17533 17543 3859 59251 47431 69855 69855 69357 17373 59733 6406 61541 61543	TX2020R-P ADVRP-S 930 watt supply GPS (CN pulse) GPS-TMG-HR-26N-100 GPS-LMR/SMA-100-RA GPS cable-CATS-C GPS mount SPF10GSR modules Fiber jumpers-LC Surger protector-CATS Surger protector-GPS	Mfg Cambium Cambium Cambium Cambium PC-Tel Mobilecomm Mobilecomm Cambuim Cambuim Misc Misc Misc	\$2,989.00 \$792.00 \$766.32 \$336.93 \$326.29 \$245.72 \$65.00 \$38.65 \$153.99 \$27.56 \$58.59 \$195.99	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$55.50 \$34.79 \$138.59 \$24.80 \$52.73 \$176.39	1 1 2 1 1 1 1 1 4 2 1	Extended Sell \$2,690.10 \$712.80 \$13,79.38 \$303.24 \$293.66 \$221.15 \$88.50 \$34.79 \$554.36 \$49.61 \$52.73 \$176.39	Replace CMM5 Replace existing Replace ex	
1100 1101 1102 1103 1104 1105 1106 1107 1108 1111 1111 1111	POINT OF AMI 17533 17543 3859 59251 47431 69355 69357 17373 59733 6406 61541 61543 11612	TX2020R-P ADVRP-5 930 watt supply GPS (CN pulse) GPS-TMG-HR-26N-100 GPS-TMG-HR-26N-100 GPS-MR/SMA-100-RA GPS cable-CAT5-C GPS mount SPF-10GSR modules Fiber jumpers-LC Surger protector-CAT5 Surge protector-GPS Shop supplies	Mfg Cambium Cambium Cambium Cambium PC-Tel Mobilecomm Mobilecomm Cambuim Cambuim Misc Misc Misc Misc	\$2,989.00 \$792.00 \$766.32 \$336.93 \$326.29 \$245.72 \$65.00 \$38.65 \$153.99 \$27.56 \$58.59 \$195.99 \$125.00	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73 \$176.39	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50	1 1 2 1 1 1 1 1 4 2 1 1 1	Extended Sell 52,690.10 5712.80 51,379.38 5303.24 5293.66 5221.15 558.50 534.79 5554.36 549.61 552.73 5176.39 5112.50 50.00	Replace CMM5 Replace existing Replace ex	
1100 1101 1102 1103 1104 1105 1106 1107 1108 11109 11111 1111 1111 1111	POINT OF AMI 17533 17543 3859 59251 47431 69355 69357 17373 59733 6406 61541 61543 11612	TX2020R-P ADVRP-5 930 watt supply GPS (CN pulse) GPS-TMG-HR-26N-100 GPS-TMG-HR-26N-100 GPS-MR/SMA-100-RA GPS cable-CAT5-C GPS mount SPF-10GSR modules Fiber jumpers-LC Surger protector-CAT5 Surge protector-GPS Shop supplies	Mfg Cambium Cambium Cambium Cambium PC-Tel Mobilecomm Mobilecomm Cambuim Cambuim Misc Misc Misc Misc	\$2,989.00 \$792.00 \$766.32 \$336.93 \$326.29 \$245.72 \$65.00 \$38.65 \$153.99 \$27.56 \$58.59 \$125.00 \$0.00	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73 \$176.39	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50	1 1 2 1 1 1 1 1 4 2 1 1 1	Extended Sell 52,690.10 5712.80 51,379.38 5303.24 5293.66 5221.15 558.50 534.79 5554.36 549.61 552.73 5176.39 5112.50 50.00	Replace CMM5 Replace existing Replace ex	
1100 1101 1102 1103 1104 1105 1106 1107 1110 1111 1111 1111 1111 1111	POINT OF AMI 17533 17543 3859 59251 47431 69855 69857 17373 59733 6406 61541 61543 11612 9996	TX2020R-P ADVRP-5 930 watt supply GPS (CN pulse) GPS-TMG-HR-26N-100 GPS-TMG-HR-26N-100 GPS-MR/SMA-100-RA GPS cable-CAT5-C GPS mount SPF-10GSR modules Fiber jumpers-LC Surger protector-CAT5 Surge protector-GPS Shop supplies	Mfg Cambium Cambium Cambium Cambium PC-Tel Mobilecomm Mobilecomm Cambuim Cambuim Misc Misc Misc Misc	\$2,989.00 \$792.00 \$766.32 \$336.93 \$326.29 \$245.72 \$65.00 \$38.65 \$153.99 \$27.56 \$58.59 \$125.00 \$0.00	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73 \$176.39	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50	1 1 2 1 1 1 1 1 4 2 1 1 1	Extended Sell 52,690.10 5712.80 51,379.38 5303.24 5293.66 5221.15 558.50 534.79 5554.36 549.61 552.73 5176.39 5112.50 50.00	Replace CMM5 Replace existing Replace ex	
1100 1101 1102 1103 1104 1105 1106 1107 1108 1110 1111 1111 1111 1114	POINT OF AMI 17533 17543 3859 59251 47431 69355 69355 69357 17373 59733 6406 61541 61543 11612 9996	TX2020R-P ADVRP-5 930 watt supply GPS (CN pulse) GPS-TMG-HR-26N-100 GPS-MR/SMA-100-RA GPS cable-CATS-C GPS mount SPF10GSR modules Fiber jumpers-LC Surger protector-CATS Swrge protector-CPS Shop supplies Misc. Risk	Mfg Cambium Cambium Cambium Cambium PC-Tel Mobilecomm Cambuim Cambuim Cambuim Misc Misc Misc Misc Misc Misc	\$2,989.00 \$792.00 \$766.32 \$336.93 \$326.29 \$245.72 \$65.00 \$38.65 \$153.99 \$27.56 \$58.59 \$195.99 \$125.00	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59 \$52.73 \$176.39 \$112.50 \$0.00	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50 \$0.00	1 1 2 1 1 1 1 4 2 1 1 1 1 1 1 1 1 1 1 1	S2,690.10 S712.80 S1,379.38 S303.24 S203.24 S203.24 S203.24 S203.24 S203.24 S203.24 S203.25 S34.79 S554.36 S49.61 S52.73 S112.50 S0.00 \$6,639.20	Replace CMM5 Replace existing Replace ex	
1100 1101 1102 1103 1104 1105 1106 1107 1108 11101 1111 1111 1111 1111 111	POINT OF AMI 17533 17543 3859 59251 47431 69355 69357 17373 59733 6406 61541 61543 11612 9996 DEERFIELD 17533	TX2020R-P ADVRP-S 930 watt supply GPS (CN pulse) GPS-TMG-HR-26h-1:00 GPS-TMG-HR-26h-1:00 GPS-LMR/SMA-1:00-RA GPS cable-CATS-C GPS mount SPF10GSR modules Fiber jumpers-LC Surger protector-CATS Surge protector-CATS Surge protector-CATS MISC. RISK	Mfg Cambium Cambium Cambium Cambium PC-Tel Mobilecomm Mobilecomm Cambuim Cambuim Misc Misc Misc Misc Misc Misc Cambium Cambium Cambuim Cambium Cambium Cambium	\$2,989.00 \$792.00 \$766.32 \$336.93 \$326.29 \$245.72 \$65.00 \$38.65 \$153.99 \$27.56 \$58.59 \$195.99 \$195.99 \$125.00 \$0.00	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50 \$0.00	\$2,690.10 \$712.80 \$589.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.78 \$176.39 \$112.50 \$0.00	1 1 2 1 1 1 1 1 4 2 1 1 1 1 1 1 1 1 1 1	Extended Sell S2,690.10 S712.80 S1,379.38 S303.24 S293.66 S221.15 S58.50 S58.79 S58.479 S554.36 S49.61 S52.73 S176.39 S112.50 S0.00 \$6,639.20 \$2,690.10	Replace CMM5 Replace existing	
1100 1101 1102 1103 1104 1105 1106 1107 1108 1109 1111 1112 1113 1114 1120 1200	POINT OF AMI 17533 17543 3859 59251 47431 69355 69357 17373 59733 6406 61541 61543 11612 9996 DEERFIELD 17533 17543	TX2020R-P ADVRP-S 930 watt supply GPS (CN pulse) GPS-TMG-HR-26N-100 GPS-TMG-HR-26N-100 GPS-TMG-MA-100-RA GPS cable-CATS-C GPS mount SPF10GSR modules Fiber jumpers-LC Surger protector-CATS Surge protector-CATS Surge protector-CATS Misc. Risk	Mfg Cambium Cambium Cambium Cambium PC-Tel Mobilecomm Mobilecomm Cambuim Cambuim Misc Misc Misc Misc Misc Misc Cambium Cambium Cambuim Cambium Cambium Cambium	\$2,989.00 \$792.00 \$766.32 \$336.93 \$226.29 \$245.72 \$65.00 \$38.65 \$153.99 \$27.56 \$58.59 \$125.00 \$0.00	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73 \$112.50 \$0.00	\$2,690.10 \$712.80 \$689.69 \$303.24 \$223.66 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50 \$0.00	1 1 2 1 1 1 1 1 4 2 1 1 1 1 1 1 1 1 1 1	Extended Sell \$2,690.10 \$712.80 \$1,379.38 \$530.324 \$293.66 \$221.15 \$58.50 \$54.79 \$554.36 \$49.61 \$552.73 \$176.39 \$112.50 \$0.00 \$6,639.20 \$6,639.20 \$712.80	Replace CMM5 Replace existing Replace EMM5 Replace CMM5	
1100 1101 1102 1103 1104 1105 1106 1107 1108 1119 1111 1111 1111 1111 1112 1108 1200 1201 1202 1203	POINT OF AMI 17533 17543 3859 59251 47431 698355 69857 17373 59733 6406 61541 61543 11612 9996 DEERFIELD 17533 17543	TX2020R-P ADVRP-5 930 watt supply GPS (CN pulse) GPS-TMG-HR-26N-100 GPS-LMR/SMA-100-RA GPS cable-CATS-C GPS mount SPF10GSR modules Fiber jumpers-LC Surger protector-CATS Surge protector-CATS Monos upplies Misc. Risk TX2020R-P ADVRP-5 930 watt supply	Mfg Cambium Cambium Cambium Cambium Cambium PC-Tel Mobilecomm Cambuim Cambuim Cambuim Misc Misc Misc Misc Cambium Cambuim Cambuim Cambuim Cambuim Cambuim Cambuim Cambuim Cambuim Cambuim Cambium Cambium Cambium Cambium	\$2,989.00 \$792.00 \$766.32 \$336.93 \$326.29 \$245.72 \$65.00 \$38.65 \$153.99 \$27.56 \$58.59 \$125.00 \$0.00	\$2,590.10 \$712.80 \$689.69 \$303.24 \$293.66 \$227.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50 \$0.00	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$88.50 \$34.79 \$138.59 \$24.80 \$52.73 \$112.50 \$0.00	1 1 2 1 1 1 1 1 1 4 2 1 1 1 1 1 1 1 1 1	S2,690.10	Replace CMMS Replace existing Replace ex	
1100 1101 1102 1103 1104 1105 1106 1107 1108 11109 1111 1111 1111 1111 1112 1113 1120 1201 1202	POINT OF AMI 17533 17543 3859 59251 47431 69355 69357 17373 59733 6406 61541 61543 11612 9996 DEERFIELD 17533 17543 3859 59251	TX2020R-P ADVRP-5 930 watt supply GPS (CN pulse) GPS-TMC-HR-26h-1:00 GPS-TMC-HR-26h-1:00 GPS-LMR/SMA-1:00-RA GPS cable-CATS-C GPS mount SPF10GSR modules Fiber jumpers-LC Surger protector-CATS Surge protector-CATS Surge protector-GPS Shop supplies Misc. Risk TX2020R-P ADVRP-5 930 watt supply GPS (CN pulse)	Mfg Cambium Cambium Cambium Cambium Cambium PC-Tel Mobilecomm Mobilecomm Cambuim Cambuim Misc Misc Misc Misc Misc Cambium Cambium Cambium Cambium Cambium Cambium Cambium	\$2,989.00 \$792.00 \$766.32 \$336.93 \$326.29 \$245.72 \$65.00 \$38.65 \$153.99 \$27.56 \$58.59 \$195.99 \$195.99 \$100.00	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50 \$0.00	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.65 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50 \$0.00	1 1 1 2 2 1 1 1 1 1 4 2 1 1 1 1 1 1 1 1	Extended Sell \$2,690.10 \$712.80 \$1,379.38 \$303.24 \$293.66 \$221.15 \$58.50 \$58.50 \$58.51 \$52.73 \$176.39 \$112.50 \$0.00 \$6,639.20 \$712.80 \$1,379.38 \$303.24	Replace CMM5 Replace existing	
1100 1101 1102 1103 1104 1105 1106 1107 1108 1109 1110 1111 1111 1111 1112 1200 1201 1202 1203 1204 1205	POINT OF AMI 17533 17543 3859 59251 47431 698355 69357 17373 59733 6406 61541 61543 11612 9996 DEERFIELD 17543 17543 3859 59251 47431	TX2020R-P ADVRP-S 930 watt supply GPS (CN pulse) GPS-TMG-HR-26N-100 GPS-MMS/SMA-100-RA GPS cable-CATS-C GPS mount SPF10GSR modules Fiber jumpers-LC Surge protector-CATS Surge protector-CATS Surge protector-CATS Shop supplies Misc. Risk TX2020R-P ADVRP-S 930 watt supply GPS-TMG-HR-26N-100	Mfg Cambium Cambium Cambium Cambium Pc-Tel Mobilecomm Mobilecomm Cambuim Misc Misc Misc Misc Misc Cambium	\$2,989.00 \$792.00 \$796.02 \$336.93 \$326.29 \$245.72 \$555.00 \$38.65 \$5153.99 \$27.56 \$58.59 \$125.00 \$0.00 \$766.32 \$36.93 \$36.93 \$36.93 \$36.93 \$36.93 \$36.93 \$36.93 \$36.93 \$36.93 \$36.93 \$36.93 \$36.93 \$36.93 \$36.93 \$36.93 \$36.93 \$36.93 \$36.93 \$36.93	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73 \$112.50 \$0.00	\$2,690.10 \$712.80 \$589.69 \$303.24 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50 \$0.00 \$712.80 \$689.69 \$589.69 \$293.66	1 1 2 1 1 1 1 2 1 1 1 1 1 1 1 1 1 1 1 1	Extended Sell \$2,690.10 \$712.80 \$1,379.38 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$554.36 \$49.61 \$552.73 \$176.39 \$112.50 \$0.00 \$6,639.20 \$6,639.20 \$712.80 \$1,379.38 \$30.24 \$293.66	Replace CMM5 Replace existing	
1100 1101 1102 1103 1104 1105 1106 1107 1108 1119 1111 1111 1112 1113 1114 1200 1201 1202 1203 1204 1205 1206	POINT OF AMI 17533 17543 3859 59251 47431 69355 69357 17373 59733 6406 61541 61543 11612 9996 DEERFIELD 17533 17543 3859 59251 47431	TX2020R-P ADVRP-5 930 watt supply GPS (CR pulse) GPS-TMG-HR-26N-100 GPS-LMR/SMA-100-RA GPS cable-CATS-C GPS mount SPF10SR modules Fiber jumpers-LC Surger protector-CATS Surge protector-CATS Surge protector-CATS MISC. RISK TX2020R-P ADVRP-5 930 watt supply GPS (CR pulse) GPS-TMG-HR-26N-100 GPS-LMR/SMA-100-RA	Mfg Cambium Cambium Cambium Cambium PC-Tel Mobilecomm Cambuim Cambuim Mobilecomm Cambuim Cambuim Misc Misc Misc Misc Misc Cambium	\$2,989.00 \$792.00 \$766.32 \$336.93 \$326.29 \$245.72 \$65.00 \$38.65 \$153.99 \$27.56 \$58.59 \$195.99 \$125.00 \$0.00	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50 \$0.00	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$38.50 \$34.79 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50 \$0.00 \$712.80 \$689.69 \$303.24 \$239.66 \$221.15	1 1 2 1 1 1 1 1 2 2 1 1 1 1 1 1 1 1 1 1	S2,690.10	Replace CMM5 Replace existing	
1100 1101 1102 1103 1104 1105 1106 1107 1108 1109 1110 1111 1112 1113 1114 1120 1201 1202 1203 1204 1205 1206 1207 1208	POINT OF AMI 17533 17543 3859 59251 47431 69355 69357 17373 59733 6406 61541 61543 11612 9996 DEERFIELD 17533 17543 3859 59251 47431 69355 69357	TX2020R-P ADVRP-5 930 watt supply GPS (CN pulse) GPS-TMG-HR-26N-100 GPS-LMR/SMA-100-RA GPS-able-CATS-C GPS mount SPF10GSR modules Fiber jumpers-LC Surge protector-CATS Surge protector-CATS Surge protector-CATS Surge protector-GPS Shop supplies Misc. Risk TX2020R-P ADVRP-5 930 watt supply GPS-TMR-S6N-100 GPS-LMR/SMA-100-RA GPS-LMR/SMA-100-RA GPS-CATS-C	Mfg Cambium Cambium Cambium Cambium Cambium Po-Tel Mobilecomm Mobilecomm Cambuim Cambuim Cambuim Misc Misc Misc Misc Misc Cambium Mobilecomm	\$2,989.00 \$792.00 \$766.32 \$336.93 \$336.93 \$336.93 \$324.72 \$65.00 \$38.65 \$153.99 \$27.56 \$58.59 \$195.99 \$195.99 \$125.00 \$792.00 \$792.00 \$792.00 \$336.93 \$326.29 \$245.72 \$56.20 \$336.93	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50 \$0.00	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.65 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50 \$0.00 \$712.80 \$689.69 \$303.24 \$293.66 \$293.66 \$293.66 \$52.73 \$52.73 \$53.73	1 1 2 1 1 1 1 1 1 1 2 1 1 1 1 1 1 1 1 1	Extended Sell S2,690.10 \$712.80 \$1,379.38 \$503.24 \$293.66 \$221.15 \$58.50 \$54.79 \$554.39 \$112.50 \$0.00 \$6,639.20 \$2,690.10 \$712.80 \$1,379.38 \$303.24 \$293.66 \$221.15 \$223.66 \$221.15 \$223.66 \$221.15 \$223.66 \$221.15 \$28.50	Replace CMM5 Replace existing	
1100 1101 1102 1103 1104 1105 1106 1107 1108 1109 1110 1111 1111 1112 1120 1201 1202 1203 1204 1205 1206 1207 1208	POINT OF AMI 17533 17549 3859 59251 47431 69355 69357 17373 6406 61541 61549 11612 9996 DEERFIELD 17543 3859 59251 47431 69355 69357 17373	TX2020R-P ADVRP-5 930 watt supply GPS (CR) pulse) GPS-TMG-HR-26N-100 GPS-LMR/SMM-100-RA GPS cable-CATS-C GPS mount SPF10SSR modules Fiber jumpers-LC Surger protector-CATS Surge protector-CATS Surge protector-CATS MISC. RISK TX2020R-P ADVRP-5 930 watt supply GPS (CN pulse) GPS-TMG-HR-26N-100 GPS-LMR/SMM-100-RA GPS-LMR/SMM-100-RA GPS cable-CATS-C GPS mount SPF10GSR modules	Mfg Cambium Cambium Cambium Cambium Pc-Tel Mobilecomm Mobilecomm Cambuim Misc Misc Misc Misc Misc Cambium Cambium Cambuim Misc Misc Misc Misc Misc Misc Misc Misc	\$2,989.00 \$792.00 \$766.32 \$336.93 \$326.29 \$245.72 \$650.00 \$38.65 \$5153.99 \$27.56 \$58.59 \$195.99 \$1125.00 \$792.00 \$792.00 \$766.32 \$336.93 \$326.29 \$245.72 \$356.93 \$326.29 \$245.72 \$356.93 \$326.29 \$245.72 \$356.93 \$326.29 \$245.72 \$356.93 \$326.29 \$245.72 \$356.93 \$326.29 \$245.72 \$356.93 \$326.29 \$245.72 \$356.93 \$326.29 \$245.72 \$356.93 \$326.29 \$245.72 \$356.93 \$326.29 \$245.72 \$356.93 \$326.29 \$245.72 \$356.93 \$326.29 \$356.93 \$326.29 \$356.93 \$326.29 \$356.93 \$3	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59 \$12.80 \$52.73 \$112.50 \$0.00	\$2,690.10 \$712.80 \$589.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50 \$0.00 \$712.80 \$689.69 \$303.24 \$239.66 \$221.15 \$58.50 \$34.79 \$35.69 \$35.73 \$	1 1 1 2 1 1 1 1 1 4 2 2 1 1 1 1 1 1 1 1	S2,690.10	Replace CMM5 Replace existing Replace CMM5 Replace existing	
1100 1101 1102 1103 1104 1105 1106 1107 1108 1109 1110 1111 1112 1113 1114 1120 1200 1200 1200 1200 1200 1200	POINT OF AMI 17533 17543 3859 59251 47431 69355 69357 17373 6406 61541 61543 11612 9996 DEERFIELD 17533 17543 3859 59251 47431 69355 69357 17373 59733	TX2020R-P ADVRP-S 930 watt supply GPS (CN pulse) GPS-TMG-HR-26N-100 GPS-MR/SMA-100-RA GPS cable-CATS-C GPS module SPFLOGSR modules Fiber jumpers-LC Surge protector-CATS Surge protector-CATS Surge protector-CATS Surge protector-GPS Shop supplies Misc. Risk TX2020R-P ADVRP-S 930 watt supply GPS-TMG-HR-26N-100 GPS-LMR/SMA-100-RA GPS-CATS-C GPS mount	Mfg Cambium Cambium Cambium Cambium PC-Tel Mobilecomm Cambuim Cambuim Mobilecomm Cambuim Cambuim Cambuim Cambuim Cambuim Cambuim Cambuim Cambium Cambuim Mobilecomm Mobilecomm	\$2,989.00 \$792.00 \$766.32 \$336.29 \$245.72 \$65.00 \$38.65 \$55.00 \$755.00	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$118.59 \$24.80 \$52.73 \$176.39 \$112.50 \$0.00	\$2,690.10 \$712.80 \$689.69 \$303.24 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50 \$0.00 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$34.79	1 1 2 1 1 1 1 1 1 1 1 2 1 1 1 1 1 1 1 1	S2,690.10	Replace CMM5 Replace existing Replace CMM5 Replace existing Replace commons Replace existing	
1100 1101 1102 1103 1104 1105 1106 1107 1108 1109 11101 1111 11112 1113 1114 1120 1200 1201 1202 1203 1204 1205 1206 1207 1208	POINT OF AMI 17533 17543 3859 59251 47431 69355 69357 17373 59733 6406 61541 61543 11612 9996 DEERFIELD 17533 17543 3859 59251 47431 669357 17373 59935 69357 17373 59933 6406	TX2020R-P ADVRP-S 930 watt supply GPS (CN pulse) GPS-TMG-HR-26H-100 GPS-LMR/SMA-100-RA GPS cable-CATS-C GPS mount SPF10GSR modules Fiber jumpers-LC Surge protector-CATS Surge protector-CATS Surge protector-CATS Surge protector-CATS Surge protector-GPS Shop supplies Misc. Risk TX2020R-P ADVRP-S 930 watt supply GPS-TMG-HR-26H-100 GPS-LMR/SMA-100-RA GPS cable-CATS-C GPS mount SPF10GSR modules Fiber jumpers-LC	Mfg Cambium Cambium Cambium Cambium Pc-Tel Mobilecomm Mobilecomm Misc Misc Misc Misc Misc Misc Misc Misc	\$2,989.00 \$792.00 \$796.02 \$336.93 \$2245.72 \$65.00 \$38.65 \$153.99 \$27.56 \$58.59 \$125.00 \$0.00 \$792.00 \$766.32 \$336.93 \$326.29 \$245.72 \$65.00 \$38.65 \$3	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73 \$112.50 \$0.00 \$712.80 \$689.69 \$23.24 \$23.66 \$221.15 \$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$33.24 \$293.66 \$221.15 \$34.79 \$34.79 \$35.73 \$36.73 \$	\$2,690.10 \$712.80 \$589.69 \$303.24 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73 \$112.50 \$0.00 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$303.24 \$293.66 \$221.15 \$303.24 \$293.66 \$221.15	1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1	Extended Sell S2,690.10 \$712.80 \$1,379.38 \$303.24 \$293.66 \$221.15 \$58.50 \$54.79 \$554.36 \$49.61 \$552.73 \$176.99 \$112.50 \$0.00 \$6,639.20 \$2,690.10 \$712.80 \$1,379.38 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$58.50 \$34.79 \$554.36 \$349.61 \$554.36 \$49.61 \$554.36 \$49.61 \$554.36 \$49.61 \$554.36 \$49.61 \$554.36 \$49.61 \$658.50 \$658.	Replace CMM5 Replace existing Replace existing New	
1100 1101 1102 1103 1104 1105 1106 1107 1108 1109 1110 1111 1112 1114 1120 1201 1202 1203 1204 1205 1206 1207 1208 1209 1210 1208 1209 1210 1209 1210 1209 1210 1209 1210 1209 1210 1209 1210	POINT OF AMI 17533 17543 3859 59251 47431 69355 69357 17373 59733 6406 61541 61543 11612 9996 DEERFIELD 17533 17543 3859 59251 47431 69355 69357 17373 59733 69406 61541 61541 61543	TX2020R-P ADVRP-5 930 watt supply GPS (CR) pulse) GPS-TMG-HR-26h-100 GPS-LMR/SMA-100-RA GPS and le-CATS-C GPS mount SPF10GSR modules Fiber jumpers-LC Surge protector-CATS Surge protector-CATS MISC. RISK TX2020R-P ADVRP-5 930 watt supply GPS (CR) pulse) GPS-TMG-HR-26h-100 GPS-LMR/SMA-100-RA GPS cable-CATS-C GPS mount SPF10GSR modules Fiber jumpers-LC Surge protector-CATS SURGE MISC. RISK TX2020R-P ADVRP-5 950 watt supply GPS (CR) pulse) GPS-TMG-HR-26h-100 GPS-LMR/SMA-100-RA GPS cable-CATS-C GPS mount SPF10GSR modules Fiber jumpers-LC Surger protector-CATS	Mfg Cambium Cambium Cambium Cambium PC-Tel Mobilecomm Cambuim Cambuim Cambuim Mobilecomm Cambuim Misc Misc Misc Misc Misc Misc Misc Misc	\$2,989.00 \$792.00 \$766.32 \$336.93 \$336.29 \$245.72 \$65.00 \$38.65 \$153.99 \$27.56 \$153.99 \$125.00 \$0.00 \$792.00 \$792.00 \$36.63 \$36.93 \$36.	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$113.59 \$52.73 \$112.50 \$0.00	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50 \$0.00 \$712.80 \$689.69 \$303.24 \$23.15 \$58.50 \$303.24 \$103	1 1 1 2 1 1 1 1 1 1 4 2 2 1 1 1 1 1 1 1	S2,690.10	Replace CMM5 Replace existing Replace CMM5 Replace existing	
1100 1101 1102 1103 1104 1105 1106 1107 1108 11109 11101 1111 1112 1113 1114 1120 1201 1202 1203 1204 1205 1206 1207 1208 1209 12101 1211 1211	POINT OF AMI 17533 17543 3859 59251 47431 69355 69357 17373 6406 61541 61543 115612 9996 DEERFIELD 17533 17543 3859 59251 47431 69355 69357 17373 6406 61541 61543	TX2020R-P ADVRP-5 930 watt supply GPS (CN pulse) GPS-TMG-HR-26N-100 GPS-LMR/SMA-100-RA GPS-CABIE-CATS-C GPS modules Fiber jumpers-LC Surger protector-CATS Surge protector-CATS MISC. RISK TX2020R-P ADVRP-5 930 watt supply GPS (CN pulse) GPS-TMG-HR-26N-100 GPS-LMR/SMA-100-RA GPS cable-CATS-C GPS mount SPS-LMR/SMA-100-RA GPS CRIP pulse) GPS-TMG-HR-26N-100	Mfg Cambium Cambium Cambium Cambium Cambium PC-Tel Mobilecomm Mobilecomm Cambuim Misc Misc Misc Misc Misc Misc Misc Misc	\$2,989.00 \$792.00 \$766.32 \$336.93 \$326.29 \$245.72 \$650.00 \$38.65 \$153.99 \$27.56 \$58.59 \$195.99 \$125.99 \$125.90 \$125.00 \$30.00	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50 \$0.00	\$2,690.10 \$712.80 \$589.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50 \$0.00 \$712.80 \$689.69 \$303.24 \$239.66 \$221.15 \$58.50 \$34.79 \$35.73 \$	1 1 2 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1	\$2,690.10 \$712.80 \$1,379.38 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$554.36 \$49.61 \$52.73 \$1176.39 \$1112.50 \$0.00 \$6,639.20 \$2,690.10 \$712.80 \$1,379.38 \$303.24 \$293.66 \$221.15 \$58.50 \$49.61 \$52.73 \$554.36 \$49.61 \$52.73 \$554.36 \$49.61 \$52.73 \$554.36 \$49.61 \$52.73 \$554.36 \$49.61 \$52.73 \$554.36 \$49.61 \$52.73 \$554.36 \$49.61 \$52.73 \$554.36 \$49.61 \$52.73 \$554.36 \$49.61 \$50.00	Replace CMM5 Replace existing Replace existing Replace EMM5 Replace existing Replace existi	
m 1100 1101 1102 1103 1104 1105 1106 1107 1108 1110 1111 1112 1113 1114 1200 1201 1202 1203 1204 1205 1206 1207 1208 1209 1210 1211 1211	POINT OF AMI 17533 17543 3859 59251 47431 69355 69357 17373 59733 6406 61541 61543 11612 9996 DEERFIELD 17533 17543 3859 59251 47431 69355 69357 17373 59733 6406 61541 61543	TX2020R-P ADVRP-S 930 watt supply GPS (CN pulse) GPS-TMG-HR-26N-100 GPS-LMR/SMA-100-RA GPS cable-CATS-C GPS mount SPF10GSR modules Fiber jumpers-LC Surger protector-CATS Surge protector-GPS Shop supplies Misc. Risk TX2020R-P ADVRP-S 930 watt supply GPS-TMG-HR-26N-100 GPS-LMR/SMA-100-RA GPS-CATS-C GPS mount SPF10GSR modules Fiber jumpers-LC Surger protector-CATS Shop supplies	Mfg Cambium Cambium Cambium Cambium Pc-Tel Mobilecomm Mobilecomm Misc Misc Misc Misc Misc Cambium Cambium Cambium Cambium Misc Misc Misc Misc Misc Misc Misc Misc	\$2,989.00 \$792.00 \$792.00 \$796.32 \$336.93 \$326.29 \$245.72 \$65.00 \$38.65 \$153.99 \$125.00 \$766.32 \$336.93 \$326.29 \$245.72 \$66.30 \$792.00 \$766.32 \$336.93 \$326.29 \$245.72 \$65.00 \$38.65 \$38.95 \$3	\$2,690.10 \$712.80 \$689.69 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$138.59 \$112.50 \$0.00 \$52.73 \$112.50 \$689.69 \$303.24 \$293.66 \$221.15 \$689.69 \$303.24 \$293.66 \$221.15 \$138.59 \$138.59 \$138.59 \$138.59 \$14.50 \$152.73 \$152.73 \$152.73 \$153.74 \$153.75 \$1	\$2,690.10 \$712.80 \$689.69 \$303.24 \$223.15 \$38.59 \$24.80 \$52.73 \$112.50 \$690.10 \$712.80 \$689.69 \$303.24 \$233.66 \$221.15 \$58.73 \$112.50 \$689.69 \$303.24 \$233.66 \$221.15 \$58.50 \$34.79 \$352.73 \$10.00	1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1	\$2,690.10 \$712.80 \$1,379.38 \$303.24 \$293.66 \$221.15 \$58.50 \$34.79 \$554.36 \$49.61 \$52,73 \$112.50 \$0.00 \$6,639.20 \$712.80 \$1,379.38 \$303.24 \$293.66 \$211.50 \$0.00 \$6,639.20	Replace CMM5 Replace existing Replace existing Replace EMM5 Replace existing Replace existi	

			BFSA EOL Quotation 10-5-2024						KEYLITE POWER & LIGHTING CORP. Stand Strong - Stand Strong
em	Item ID	Description	Mfg	List	List -10%	Unit Sell	Qty	Extended Sell	Maint. Scope/Comments
1300	TAMARAC								
	17533	TX2020R-P	Cambium	\$2,989.00	\$2,690.10	\$2,690.10	1	\$2,690.10	Replace CMM5
1302		ADVRP-5	Cambium	\$792.00	\$712.80	\$712.80	1	\$712.80	Replace CMM5
1303		930 watt supply	Cambium	\$766.32	\$689.69	\$689.69	2	\$1,379.38	New
1304	59251	GPS (CN pulse)	Cambium	\$336.93	\$303.24	\$303.24	1	\$303.24	New
1305	47431	GPS-TMG-HR-26N-100	PC-Tel	\$326.29	\$293.66	\$293.66	1	\$293.66	Replace existing
1306		GPS-LMR/SMA-100-RA	Mobilecomm	\$245.72	\$221.15	\$221.15	1	\$221.15	Replace existing
1307		GPS cable-CAT5-C	Mobilecomm	\$65.00	\$58.50	\$58.50	1	\$58.50	Replace existing
1308		GPS mount	Cambuim	\$38.65	\$34.79	\$34.79	1	\$34.79	Replace existing
1309	59733	SPF10GSR modules	Cambuim	\$153.99	\$138.59	\$138.59	4	\$554.36	New
1310	6406	Fiber jumpers-LC	Misc	\$27.56	\$24.80	\$24.80	2	\$49.61	New
1311	61541	Surger protector-CAT5	Misc	\$58.59	\$52.73	\$52.73	1	\$52.73	New
1312		Surge protector-GPS	Misc	\$195.99	\$176.39	\$176.39	1	\$176.39	New
	11612	Shop supplies	Misc	\$125.00	\$112.50	\$112.50	1	\$112.50	New
1314	9996	Misc. Risk	Misc	\$0.00	\$0.00	\$0.00	1	\$0.00	Temp1
								\$6,639.20)
4400									
	CORE			1	1	1		T	To a comment
1401		TX2020R-P	Cambium	\$2,989.00	\$2,690.10	\$2,690.10	1	\$2,690.10	Replace CMM5
1402	17543	ADVRP-5	Cambium	\$792.00	\$712.80	\$712.80	1	\$712.80	Replace CMM5
1403		930 watt supply	Cambium	\$766.32	\$689.69	\$689.69	2	\$1,379.38	New
1404		SPF10GSR modules	Cambuim	\$153.99	\$138.59	\$138.59	4	\$554.36	New
1405		Fiber jumpers-LC	Misc	\$27.56	\$24.80	\$24.80	2	\$49.61	New
1406		Surger protector-CAT5	Misc	\$58.59	\$52.73	\$52.73	1	\$52.73	New
1407	61543	Surge protector-GPS	Misc	\$195.99	\$176.39	\$176.39	1	\$176.39	New
1408		Shop supplies	Misc	\$125.00	\$112.50	\$112.50	1	\$112.50	New
	9996	Misc. Risk	Misc	\$0.00	\$0.00	\$0.00	1	\$0.00	Temp1
1403	5550	Milder Mak	inisc	Ç0.00	Ç0.00	90.00	-	\$5,727.87	
								\$3,727.87	
									A KEWLITE
ttachment 1			BFSA EOL C	uotation 10-	5-2024				KEYLITE POWER & LIGHTING CORP. State Stream - Punch Dramp State Stream
em	Item ID	Description	Mfg	List	List -10%	Unit Sell	Qty	Extended Sell	Maint. Scope/Comments
		•						\$5,727.87	
								7-7	
1500	PINES								
				1.	1.	1.	_	1.	T .
					\$2,690.10	\$2,690.10	1	\$2,690.10	Replace CMM5
1501		TX2020R-P	Cambium	\$2,989.00				\$712.80	Replace CMM5
		TX2020R-P ADVRP-5	Cambium Cambium	\$792.00	\$712.80	\$712.80	1	\$712.80	replace divines
1501 1502	17543	ADVRP-5	Cambium	\$792.00	\$712.80	\$712.80			
1501 1502 1503	17543 3859	ADVRP-5 930 watt supply	Cambium Cambium	\$792.00 \$766.32	\$712.80 \$689.69	\$712.80 \$689.69	2	\$1,379.38	New
1501 1502 1503 1504	17543 3859 59733	ADVRP-5 930 watt supply SPF10GSR modules	Cambium Cambium Cambuim	\$792.00 \$766.32 \$153.99	\$712.80 \$689.69 \$138.59	\$712.80 \$689.69 \$138.59	2	\$1,379.38 \$554.36	New New
1501 1502 1503 1504 1505	17543 3859 59733 6406	ADVRP-5 930 watt supply SPF10GSR modules Fiber jumpers-LC	Cambium Cambium Cambuim Misc	\$792.00 \$766.32 \$153.99 \$27.56	\$712.80 \$689.69 \$138.59 \$24.80	\$712.80 \$689.69 \$138.59 \$24.80	2 4 2	\$1,379.38 \$554.36 \$49.61	New New New
1501 1502 1503 1504 1505	17543 3859 59733 6406 61541	ADVRP-5 930 watt supply SPF10GSR modules Fiber jumpers-LC Surger protector-CAT5	Cambium Cambium Cambuim Misc Misc	\$792.00 \$766.32 \$153.99 \$27.56 \$58.59	\$712.80 \$689.69 \$138.59 \$24.80 \$52.73	\$712.80 \$689.69 \$138.59 \$24.80 \$52.73	2 4 2 1	\$1,379.38 \$554.36 \$49.61 \$52.73	New New New New
1501 1502 1503 1504 1505	17543 3859 59733 6406 61541	ADVRP-5 930 watt supply SPF10GSR modules Fiber jumpers-LC	Cambium Cambium Cambuim Misc	\$792.00 \$766.32 \$153.99 \$27.56	\$712.80 \$689.69 \$138.59 \$24.80	\$712.80 \$689.69 \$138.59 \$24.80	2 4 2	\$1,379.38 \$554.36 \$49.61	New New New
1501 1502 1503 1504 1505 1506 1507	17543 3859 59733 6406 61541 61543	ADVRP-5 930 watt supply SPF10GSR modules Fiber jumpers-LC Surger protector-CAT5 Surge protector-GPS	Cambium Cambium Cambuim Misc Misc	\$792.00 \$766.32 \$153.99 \$27.56 \$58.59 \$195.99	\$712.80 \$689.69 \$138.59 \$24.80 \$52.73 \$176.39	\$712.80 \$689.69 \$138.59 \$24.80 \$52.73 \$176.39	2 4 2 1	\$1,379.38 \$554.36 \$49.61 \$52.73 \$176.39	New New New New
1501 1502 1503 1504 1505 1506 1507 1508	17543 3859 59733 6406 61541 61543 11612	ADVRP-5 930 watt supply SPF10GSR modules Fiber jumpers-LC Surger protector-CAT5 Surge protector-GPS Shop supplies	Cambium Cambium Cambuim Misc Misc Misc Misc Misc	\$792.00 \$766.32 \$153.99 \$27.56 \$58.59 \$195.99 \$125.00	\$712.80 \$689.69 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50	\$712.80 \$689.69 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50	2 4 2 1 1	\$1,379.38 \$554.36 \$49.61 \$52.73 \$176.39 \$112.50	New New New New New New New
1501 1502 1503 1504 1505 1506 1507 1508	17543 3859 59733 6406 61541 61543	ADVRP-5 930 watt supply SPF10GSR modules Fiber jumpers-LC Surger protector-CAT5 Surge protector-GPS	Cambium Cambium Cambuim Misc Misc Misc	\$792.00 \$766.32 \$153.99 \$27.56 \$58.59 \$195.99	\$712.80 \$689.69 \$138.59 \$24.80 \$52.73 \$176.39	\$712.80 \$689.69 \$138.59 \$24.80 \$52.73 \$176.39	2 4 2 1	\$1,379.38 \$554.36 \$49.61 \$52.73 \$176.39 \$112.50 \$1,971.39	New New New New New Temp1
1501 1502 1503 1504 1505 1506 1507 1508	17543 3859 59733 6406 61541 61543 11612	ADVRP-5 930 watt supply SPF10GSR modules Fiber jumpers-LC Surger protector-CAT5 Surge protector-GPS Shop supplies	Cambium Cambium Cambuim Misc Misc Misc Misc Misc	\$792.00 \$766.32 \$153.99 \$27.56 \$58.59 \$195.99 \$125.00	\$712.80 \$689.69 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50	\$712.80 \$689.69 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50	2 4 2 1 1	\$1,379.38 \$554.36 \$49.61 \$52.73 \$176.39 \$112.50	New New New New New Temp1
1501 1502 1503 1504 1505 1506 1507 1508	17543 3859 59733 6406 61541 61543 11612	ADVRP-5 930 watt supply SPF10GSR modules Fiber jumpers-LC Surger protector-CAT5 Surge protector-GPS Shop supplies	Cambium Cambium Cambuim Misc Misc Misc Misc Misc	\$792.00 \$766.32 \$153.99 \$27.56 \$58.59 \$195.99 \$125.00	\$712.80 \$689.69 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50	\$712.80 \$689.69 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50	2 4 2 1 1	\$1,379.38 \$554.36 \$49.61 \$52.73 \$176.39 \$112.50 \$1,971.39	New New New New New Temp1
1501 1502 1503 1504 1505 1506 1507 1508 1509	17543 3859 59733 6406 61541 61543 11612 9996	ADVRP-5 930 watt supply SPF10GSR modules Fiber jumpers-LC Surger protector-CAT5 Surge protector-GPS Shop supplies Misc. Risk	Cambium Cambium Cambium Misc Misc Misc Misc Misc Misc	\$792.00 \$766.32 \$153.99 \$27.56 \$58.59 \$195.99 \$125.00 \$0.00	\$712.80 \$689.69 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50 \$0.00	\$712.80 \$689.69 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50 \$0.00	2 4 2 1 1 1 1	\$1,379.38 \$554.36 \$49.61 \$52.73 \$176.39 \$112.50 \$1,971.39 \$7,699.26	New New New New New New Temp1
1501 1502 1503 1504 1505 1506 1507 1508 1509	17543 3859 59733 6406 61541 61543 11612 9996 SPARES	ADVRP-5 930 wat supply SPF10GSR modules Fiber jumpers-LC Surger protector-CATS Surge protector-GPS Shop supplies Misc. Risk	Cambium Cambium Cambium Cambuim Misc Misc Misc Misc Misc Cambium Cambium Cambium	\$792.00 \$766.32 \$153.99 \$27.56 \$58.59 \$195.99 \$125.00 \$0.00	\$712.80 \$689.69 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50 \$0.00	\$712.80 \$689.69 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50 \$0.00	2 4 2 1 1 1 1	\$1,379.38 \$554.36 \$49.61 \$52,73 \$176.39 \$112.50 \$1,971.39 \$7,699.26	New New New New New Temp1
1501 1502 1503 1504 1505 1506 1507 1508 1509	17543 3859 59733 6406 61541 61543 11612 9996 SPARES 17533 3855	ADVRP-5 930 watt supply SPF10GSR modules Fiber jumpers-LC Surger protector-CAT5 Surge protector-GPS Shop supplies Misc. Risk	Cambium Cambium Cambium Misc Misc Misc Misc Misc Misc	\$792.00 \$766.32 \$153.99 \$27.56 \$58.59 \$195.99 \$125.00 \$0.00 \$2,989.00 \$766.32	\$712.80 \$689.69 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50 \$0.00 \$2,690.10 \$689.69	\$712.80 \$689.69 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50 \$0.00 \$2,690.10 \$689.69	2 4 2 1 1 1 1 2 3	\$1,379.38 \$554.36 \$49.61 \$52.73 \$176.39 \$112.50 \$1,971.39 \$7,699.26 \$5,380.20 \$2,069.06	New New New New New New Temp1
1501 1502 1503 1504 1505 1506 1507 1508 1509	17543 3859 59733 6406 61541 61543 11612 9996 SPARES 17533 3855	ADVRP-5 930 wat supply SPF10GSR modules Fiber jumpers-LC Surger protector-CATS Surge protector-GPS Shop supplies Misc. Risk	Cambium Cambium Cambium Cambuim Misc Misc Misc Misc Misc Cambium Cambium Cambium	\$792.00 \$766.32 \$153.99 \$27.56 \$58.59 \$195.99 \$125.00 \$0.00	\$712.80 \$689.69 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50 \$0.00	\$712.80 \$689.69 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50 \$0.00	2 4 2 1 1 1 1	\$1,379.38 \$554.36 \$49.61 \$52,73 \$176.39 \$112.50 \$1,971.39 \$7,699.26	New New New New New Temp1
1501 1502 1503 1504 1505 1507 1508 1509 1600 1601 1601	17543 3859 59733 6406 61541 61543 11612 9996 SPARES 17533 3855 59257	ADVRP-S 930 watt supply SPF10GSR modules Fiber jumpers-LC Surger protector-CAT5 Surge protector-GPS Shop supplies Misc. Risk TX2020R-P 930 watt supply GPS (CN pulse)	Cambium Cambum Cambum Misc Misc Misc Misc Misc Cambum Cambum Cambium Cambium Cambium Cambium	\$792.00 \$766.32 \$153.99 \$27.56 \$88.59 \$195.99 \$125.00 \$0.00 \$766.32 \$336.93	\$712.80 \$689.69 \$138.59 \$24.80 \$52.73 \$112.50 \$0.00 \$2,690.10 \$689.69 \$303.24	\$712.80 \$689.69 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50 \$0.00 \$2,690.10 \$689.69 \$303.24	2 4 2 1 1 1 1 1 1 1 1 1 2 3 3 2 2	\$1,379.38 \$554.36 \$49.61 \$52,73 \$176.39 \$112.50 \$1,971.39 \$7,699.26 \$52,069.06 \$606.47	New New New New New New New Spares Spares Spares Spares
1501 1502 1503 1504 1505 1506 1507 1508 1509 1600 1601 1602 1603 1604	17543 3859 59733 6406 61541 61543 11612 9996 SPARES 1753 3855 59251 47433	ADVRP-5 930 watt supply SPF10GSR modules Fiber jumpers-LC Surger protector-GPS Shop supplies Misc. Risk TX2020R-P 930 watt supply GPS-TMC-HR-26N-100	Cambium Cambium Cambium Misc Misc Misc Misc Misc Cambium Cambium Cambium Cambium PC-Tel	\$792.00 \$766.32 \$153.99 \$27.56 \$88.59 \$195.99 \$125.00 \$0.00 \$766.32 \$336.93 \$326.29	\$712.80 \$689.69 \$138.59 \$24.80 \$52.73 \$112.50 \$0.00 \$2,690.10 \$689.69 \$303.24 \$293.66	\$712.80 \$689.69 \$138.59 \$24.80 \$52.73 \$112.50 \$0.00 \$2,690.10 \$689.69 \$303.24 \$293.66	2 4 2 1 1 1 1 1 2 3 2 2	\$1,379.38 \$554.36 \$49.61 \$52,73 \$176.39 \$112.50 \$1,971.39 \$7,699.26 \$5,380.20 \$2,069.06 \$606.47 \$587.32	New New New New New Temp1 Spares Spares Spares Spares Spares
1501 1502 1503 1504 1505 1506 1507 1508 1507 1508 1509 1600 1601 1602 1603	17543 3859 59733 6406 61541 61553 11612 9996 SPARES 17533 3855 59251 47431 59733	ADVRP-5 930 watt supply SPF10GSR modules Fiber jumpers-LC Surger protector-CATS Surge protector-GPS Shop supplies Misc. Risk TX2020R-P 930 watt supply GPS (CN pulse) GPS-TMG-HR-26N-100 SPF10GSR modules	Cambium Cambium Cambium Cambium Misc Misc Misc Misc Cambium	\$792.00 \$766.32 \$153.99 \$27.56 \$58.59 \$195.99 \$125.00 \$0.00 \$766.32 \$336.93 \$326.29 \$153.99	\$712.80 \$689.69 \$138.59 \$24.80 \$52.73 \$112.50 \$0.00 \$2,690.10 \$689.69 \$303.24 \$293.66 \$138.59	\$712.80 \$689.69 \$138.59 \$24.80 \$52.73 \$112.50 \$0.00 \$2,690.10 \$689.69 \$303.24 \$293.66 \$138.59	2 4 2 1 1 1 1 1 1 2 3 2 2 8	\$1,379.38 \$554.36 \$49.61 \$52.73 \$176.39 \$112.50 \$1,971.39 \$7,699.26 \$5,380.20 \$2,069.06 \$606.47 \$560.47 \$57.32 \$1,108.73	New New New New New New Spares Spares Spares Spares Spares Spares Spares Spares
1501 1502 1503 1504 1505 1506 1507 1508 1509 1600 1601 1602 1603 1604 1605 1606	17543 3859 59733 6406 61541 61543 11612 9996 SPARES 17533 3855 59251 47431 59733 6406	ADVRP-S 930 watt supply SPF10GSR modules Fiber jumpers-LC Surger protector-GPS Shop supplies Misc. Risk TX2020R-P 930 watt supply GPS (TN pulse) GPS-TMG-HR-26N-100 SPF10GSR modules Fiber jumpers-LC	Cambium Cambuim Cambuim Misc Misc Misc Misc Cambium	\$792.00 \$766.32 \$153.99 \$27.56 \$58.59 \$195.99 \$125.00 \$0.00 \$766.32 \$336.93 \$326.29 \$153.99 \$27.56	\$712.80 \$689.69 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50 \$0.00 \$689.69 \$303.24 \$293.66 \$138.59 \$24.80	\$712.80 \$689.69 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50 \$0.00 \$2,690.10 \$689.69 \$303.24 \$293.66 \$138.59 \$24.80	2 4 2 1 1 1 1 1 1 2 3 2 2 2 8 8	\$1,379.38 \$554.36 \$49.61 \$52,73 \$176.39 \$112.50 \$1,971.39 \$7,699.26 \$52,069.06 \$606.47 \$587.32 \$1,108.73 \$198.43	New New New New New New Spares
1501 1502 1503 1504 1505 1506 1507 1508 1509 1600 1601 1602 1603 1604 1605 1606	17543 3859 59733 6406 61541 61543 11612 9996 SPARES 17533 3855 59257 47431 59733 64006 61541	ADVRP-5 930 watt supply SPF10GSR modules Fiber jumpers-LC Surge protector-GPS Shop supplies Misc. Risk TX2020R-P 930 watt supply GPS (CN pulse) GPS-TMG-RR-26N-100 SPF10GSR modules Fiber jumpers-LC Surge protector-CATS	Cambium Cambium Cambium Misc Misc Misc Misc Misc Cambium Cambium Cambium Cambium Cambium Cambium Cambium Misc Misc Misc Misc Misc Misc	\$792.00 \$766.32 \$153.99 \$27.56 \$58.59 \$125.00 \$0.00 \$766.32 \$336.93 \$326.29 \$153.99 \$27.56	\$712.80 \$689.69 \$138.59 \$24.80 \$52.73 \$112.50 \$0.00 \$2,690.10 \$689.69 \$303.24 \$293.66 \$138.59 \$24.80 \$52.73	\$712.80 \$689.69 \$138.59 \$24.80 \$52.73 \$112.50 \$0.00 \$2,690.10 \$689.69 \$303.24 \$293.66 \$138.59 \$24.80 \$52.73	2 4 2 1 1 1 1 1 1 2 3 2 2 8	\$1,379.38 \$55436 \$49.61 \$52.73 \$112.50 \$1,971.39 \$7,699.26 \$5,380.20 \$2,069.06 \$606.47 \$587.32 \$1,108.73 \$198.43 \$105.46	New New New New New New Spares Spares Spares Spares Spares Spares Spares Spares
1501 1502 1503 1504 1505 1506 1507 1508 1509 1600 1601 1602 1603 1604 1605 1606	17543 3859 59733 6406 61541 61543 11612 9996 SPARES 17533 3855 59257 47431 59733 64006 61541	ADVRP-5 930 watt supply SPF10GSR modules Fiber jumpers-LC Surge protector-GPS Shop supplies Misc. Risk TX2020R-P 930 watt supply GPS (CN pulse) GPS-TMG-RR-26N-100 SPF10GSR modules Fiber jumpers-LC Surge protector-CATS	Cambium Cambuim Cambuim Misc Misc Misc Misc Cambium	\$792.00 \$766.32 \$153.99 \$27.56 \$58.59 \$195.99 \$125.00 \$0.00 \$766.32 \$336.93 \$326.29 \$153.99 \$27.56	\$712.80 \$689.69 \$138.59 \$24.80 \$52.73 \$112.50 \$0.00 \$2,690.10 \$689.69 \$303.24 \$293.66 \$138.59 \$24.80 \$52.73	\$712.80 \$689.69 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50 \$0.00 \$2,690.10 \$689.69 \$303.24 \$293.66 \$138.59 \$24.80	2 4 2 1 1 1 1 1 1 2 3 2 2 2 8 8	\$1,379.38 \$554.36 \$49.61 \$52,73 \$176.39 \$112.50 \$1,971.39 \$7,699.26 \$52,069.06 \$606.47 \$587.32 \$1,108.73 \$198.43	New New New New New New Spares
1501 1502 1503 1504 1505 1506 1507 1508 1507 1508 1509 1600 1601 1602 1603 1604 1605 1606 1607 1608	17543 3859 59733 6406 61541 61543 11612 9996 SPARES 17533 3855 59251 47431 5973 6406 61541 61541	ADVRP-5 930 watt supply SPF10GSR modules Fiber jumpers-LC Surger protector-CAT5 Surge protector-GPS Shop supplies Misc. Risk TX2020R-P 930 watt supply GPS (CN pulse) GPS-TMG-HR-26N-100 SPF10GSR modules Fiber jumpers-LC Surger protector-CAT5 Surger protector-GPS	Cambium Cambium Cambium Cambium Misc Misc Misc Misc Cambium Cambium Cambium Cambium Cambium Cambium Cambium Misc Misc Misc Misc Misc Misc Misc Misc	\$792.00 \$766.32 \$153.99 \$27.56 \$58.59 \$195.99 \$125.00 \$0.00 \$766.32 \$336.93 \$326.29 \$153.99 \$27.56 \$58.59 \$195.99	\$712.80 \$689.69 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50 \$0.00 \$689.69 \$303.24 \$293.66 \$138.59 \$24.80	\$712.80 \$689.69 \$138.59 \$24.80 \$52.73 \$112.50 \$0.00 \$2,690.10 \$689.69 \$303.24 \$293.66 \$138.59 \$24.80 \$52.73 \$112.50	2 4 2 1 1 1 1 1 1 2 3 2 2 2 2 2	\$1,379.38 \$554.36 \$49.61 \$52.73 \$176.39 \$1,971.39 \$7,699.26 \$5,380.20 \$2,069.06 \$606.47 \$587.32 \$1,108.73 \$19.8.43 \$105.46 \$352.78	New New New New New New New Spares
1501 1502 1503 1504 1505 1506 1507 1508 1509 1600 1601 1602 1603 1604 1605 1606 1607 1608	17543 3859 59733 6406 61543 61543 11612 9996 SPARES 17533 3859 59251 47431 59733 6406 61543 Spare switches	ADVRP-S 930 watt supply SPF10GSR modules Fiber jumpers-LC Surger protector-GPS Shop supplies Misc. Risk TX2020R-P 930 watt supply GPS (CN pulse) GPS-TMG-HR-26N-100 SPF10GSR modules Fiber jumpers-LC Surger protector-CAT5 Surge protector-CAT5 Surge protector-GPS WS-C3560CX-12	Cambium Cambium Cambuim Misc Misc Misc Misc Misc Cambium Cambium Cambium Cambium Cambium PC-Tel Cambuim Misc Misc Misc	\$792.00 \$766.32 \$153.99 \$27.56 \$58.59 \$125.00 \$0.00 \$766.32 \$336.93 \$326.29 \$153.99 \$27.56 \$58.59 \$195.99 \$27.56 \$58.59	\$712.80 \$689.69 \$138.59 \$24.80 \$52.73 \$112.50 \$0.00 \$2,690.10 \$689.69 \$303.24 \$293.66 \$138.59 \$24.80 \$52.73 \$176.39	\$712.80 \$689.69 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50 \$0.00 \$2,690.10 \$689.69 \$303.24 \$293.66 \$138.59 \$24.80 \$52.73 \$176.39 \$1,971.39	2 4 2 1 1 1 1 1 1 2 3 2 2 8 8 8 2 2	\$1,379.38 \$554.36 \$49.61 \$52,73 \$176.39 \$1112.50 \$1,971.39 \$7,699.26 \$52,069.06 \$606.47 \$587.32 \$1,108.73 \$198.43 \$105.46 \$352.78 \$0.00	New New New New New New Spares
1501 1502 1503 1504 1505 1506 1507 1508 1507 1508 1509 1600 1601 1602 1603 1604 1605 1606 1607 1608	17543 3859 59733 6406 61543 61543 11612 9996 SPARES 17533 3859 59251 47431 59733 6406 61543 Spare switches	ADVRP-5 930 watt supply SPF10GSR modules Fiber jumpers-LC Surger protector-CAT5 Surge protector-GPS Shop supplies Misc. Risk TX2020R-P 930 watt supply GPS (CN pulse) GPS-TMG-HR-26N-100 SPF10GSR modules Fiber jumpers-LC Surger protector-CAT5 Surger protector-GPS	Cambium Cambium Cambium Cambium Misc Misc Misc Misc Cambium Cambium Cambium Cambium Cambium Cambium Cambium Misc Misc Misc Misc Misc Misc Misc Misc	\$792.00 \$766.32 \$153.99 \$27.56 \$58.59 \$195.99 \$125.00 \$0.00 \$766.32 \$336.93 \$326.29 \$153.99 \$27.56 \$58.59 \$195.99	\$712.80 \$689.69 \$138.59 \$24.80 \$52.73 \$112.50 \$0.00 \$2,690.10 \$689.69 \$303.24 \$293.66 \$138.59 \$24.80 \$52.73	\$712.80 \$689.69 \$138.59 \$24.80 \$52.73 \$112.50 \$0.00 \$2,690.10 \$689.69 \$303.24 \$293.66 \$138.59 \$24.80 \$52.73 \$112.50	2 4 2 1 1 1 1 1 1 2 3 2 2 8 8 8 2 2	\$1,379.38 \$554.36 \$49.61 \$52.73 \$176.39 \$112.50 \$1,971.39 \$7,699.26 \$5,380.20 \$2,069.06 \$606.47 \$587.32 \$1,108.73 \$198.43 \$105.46 \$352.78 \$0.00	New New New New New New New Spares
1501 1502 1503 1504 1505 1507 1508 1509 1601 1601 1602 1603 1604 1605 1606 1607 1608	17543 3859 59733 6406 61543 61543 11612 9996 SPARES 17533 3859 59251 47431 59733 6406 61543 Spare switches	ADVRP-S 930 watt supply SPF10GSR modules Fiber jumpers-LC Surger protector-GPS Shop supplies Misc. Risk TX2020R-P 930 watt supply GPS (CN pulse) GPS-TMG-HR-26N-100 SPF10GSR modules Fiber jumpers-LC Surger protector-CAT5 Surge protector-CAT5 Surge protector-GPS WS-C3560CX-12	Cambium Cambium Cambuim Misc Misc Misc Misc Misc Cambium Cambium Cambium Cambium Cambium PC-Tel Cambuim Misc Misc Misc	\$792.00 \$766.32 \$153.99 \$27.56 \$58.59 \$125.00 \$0.00 \$766.32 \$336.93 \$326.29 \$153.99 \$27.56 \$58.59 \$195.99 \$27.56 \$58.59	\$712.80 \$689.69 \$138.59 \$24.80 \$52.73 \$112.50 \$0.00 \$2,690.10 \$689.69 \$303.24 \$293.66 \$138.59 \$24.80 \$52.73 \$176.39	\$712.80 \$689.69 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50 \$0.00 \$2,690.10 \$689.69 \$303.24 \$293.66 \$138.59 \$24.80 \$52.73 \$176.39 \$1,971.39	2 4 2 1 1 1 1 1 1 2 3 2 2 8 8 8 2 2	\$1,379.38 \$554.36 \$49.61 \$52.73 \$176.39 \$112.50 \$1,971.39 \$7,699.26 \$5,380.20 \$2,069.06 \$606.47 \$587.32 \$1,108.73 \$198.43 \$105.46 \$352.78 \$0.00	New New New New New New New Spares
1501 1502 1503 1504 1505 1507 1508 1509 1601 1601 1602 1603 1604 1605 1606 1607 1608	17543 3859 59733 6406 61543 61543 11612 9996 SPARES 17533 3859 59251 47431 59733 6406 61543 Spare switches	ADVRP-S 930 watt supply SPF10GSR modules Fiber jumpers-LC Surger protector-GPS Shop supplies Misc. Risk TX2020R-P 930 watt supply GPS (CN pulse) GPS-TMG-HR-26N-100 SPF10GSR modules Fiber jumpers-LC Surger protector-CAT5 Surge protector-CAT5 Surge protector-GPS WS-C3560CX-12	Cambium Cambium Cambuim Misc Misc Misc Misc Misc Cambium Cambium Cambium Cambium Cambium PC-Tel Cambuim Misc Misc Misc	\$792.00 \$766.32 \$153.99 \$27.56 \$58.59 \$125.00 \$0.00 \$766.32 \$336.93 \$326.29 \$153.99 \$27.56 \$58.59 \$195.99 \$27.56 \$58.59	\$712.80 \$689.69 \$138.59 \$24.80 \$52.73 \$112.50 \$0.00 \$2,690.10 \$689.69 \$303.24 \$293.66 \$138.59 \$24.80 \$52.73 \$176.39	\$712.80 \$689.69 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50 \$0.00 \$2,690.10 \$689.69 \$303.24 \$293.66 \$138.59 \$24.80 \$52.73 \$176.39 \$1,971.39	2 4 2 1 1 1 1 1 1 2 3 2 2 8 8 8 2 2	\$1,379.38 \$554.36 \$49.61 \$52,73 \$176.39 \$1112.50 \$1,971.39 \$7,699.26 \$52,069.06 \$606.47 \$587.32 \$1,108.73 \$198.43 \$105.46 \$352.78 \$0.00	New New New New New New Spares
1501 1502 1503 1504 1505 1507 1508 1509 1601 1601 1602 1603 1604 1605 1606 1607 1608	17543 3859 59733 6406 61543 61543 11612 9996 SPARES 17533 3859 59251 47431 59733 6406 61543 Spare switches	ADVRP-S 930 watt supply SPF10GSR modules Fiber jumpers-LC Surger protector-GPS Shop supplies Misc. Risk TX2020R-P 930 watt supply GPS (CN pulse) GPS-TMG-HR-26N-100 SPF10GSR modules Fiber jumpers-LC Surger protector-CAT5 Surge protector-CAT5 Surge protector-GPS WS-C3560CX-12	Cambium Cambium Cambuim Misc Misc Misc Misc Misc Cambium Cambium Cambium Cambium Cambium PC-Tel Cambuim Misc Misc Misc	\$792.00 \$766.32 \$153.99 \$27.56 \$58.59 \$125.00 \$0.00 \$766.32 \$336.93 \$326.29 \$153.99 \$27.56 \$58.59 \$195.99 \$27.56 \$58.59	\$712.80 \$689.69 \$138.59 \$24.80 \$52.73 \$112.50 \$0.00 \$2,690.10 \$689.69 \$303.24 \$293.66 \$138.59 \$24.80 \$52.73 \$176.39	\$712.80 \$689.69 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50 \$0.00 \$2,690.10 \$689.69 \$303.24 \$293.66 \$138.59 \$24.80 \$52.73 \$176.39 \$1,971.39	2 4 2 1 1 1 1 1 1 2 3 2 2 8 8 8 2 2	\$1,379.38 \$554.36 \$49.61 \$52.73 \$176.39 \$112.50 \$1,971.39 \$7,699.26 \$2,069.06 \$606.47 \$587.32 \$1,108.73 \$198.43 \$105.46 \$352.78 \$0.00 \$0.00 \$10,408.45	New New New New New New New Spares
1501 1502 1503 1504 1505 1507 1508 1509 1601 1601 1602 1603 1604 1605 1606 1607 1608	17543 3859 59733 6406 61543 61543 11612 9996 SPARES 17533 3859 59251 47431 59733 6406 61543 Spare switches	ADVRP-S 930 watt supply SPF10GSR modules Fiber jumpers-LC Surger protector-GPS Shop supplies Misc. Risk TX2020R-P 930 watt supply GPS (CN pulse) GPS-TMG-HR-26N-100 SPF10GSR modules Fiber jumpers-LC Surger protector-CAT5 Surge protector-CAT5 Surge protector-GPS WS-C3560CX-12	Cambium Cambium Cambuim Misc Misc Misc Misc Misc Cambium Cambium Cambium Cambium Cambium PC-Tel Cambuim Misc Misc Misc	\$792.00 \$766.32 \$153.99 \$27.56 \$58.59 \$125.00 \$0.00 \$766.32 \$336.93 \$326.29 \$153.99 \$27.56 \$58.59 \$195.99 \$27.56 \$58.59	\$712.80 \$689.69 \$138.59 \$24.80 \$52.73 \$112.50 \$0.00 \$2,690.10 \$689.69 \$303.24 \$293.66 \$138.59 \$24.80 \$52.73 \$176.39	\$712.80 \$689.69 \$138.59 \$24.80 \$52.73 \$176.39 \$112.50 \$0.00 \$2,690.10 \$689.69 \$303.24 \$293.66 \$138.59 \$24.80 \$52.73 \$176.39 \$1,971.39	2 4 2 1 1 1 1 1 1 2 3 2 2 8 8 8 2 2	\$1,379.38 \$554.36 \$49.61 \$52.78 \$176.39 \$112.50 \$1,971.39 \$7,699.26 \$5,380.20 \$2,069.06 \$606.47 \$587.32 \$1,108.73 \$1105.46 \$352.78 \$0.00 \$0.00 \$10,408.45	New New New New New New New Spares

Attachment 1			BFSA EOL Q	uotation 10-5	-2024				KEYLITE POWER & LIGHTING CORP. State Comp Paried Comp.
ltem	Item ID	Description	Mfg	List	List -10%	Unit Sell	Qty	Extended Sell	Maint. Scope/Comments
SERVICES TO BE	PROCURED	ON SEPARATE PURCHASE ORDER	R						
201	Per Site	RF site installations	Keylite			\$3,337.20	13	\$43,383.60	\$43,383.60
202	Phase 1	Server0: Installation Site Support	Keylite			\$200.85	16	\$3,213.60	
203	Phase 1	Net0: Design, update configs, prototype test	Keylite			\$200.85	240	\$48,204.00	
204	Phase 1	Net1: Core Switch Upgrade	Keylite			\$200.85	16	\$3,213.60	
205	Phase 1	Net2: Core Router Upgrades	Keylite			\$200.85	24	\$4,820.40	
206	Phase 1	Net2.5: GaRI install, configure, test	Keylite			\$200.85	16	\$3,213.60	
207	Phase 1	Net3: Firewall updates	Keylite			\$200.85	16	\$3,213.60	\$65,878.80
208	Phase 2	Net4: Update edge routers , fiber convert	Keylite			\$200.85	22	\$4,418.70	
209	Phase 2	Net5: CMR Management	Keylite			\$200.85	8	\$1,606.80	
210	Phase 2	Net6: Test, Document	Keylite			\$200.85	40	\$8,034.00	
211	Phase 2	Pilot Test	Keylite			\$200.85	40	\$8,034.00	
212	Phase 2	ATP, punchlist	Keylite			\$200.85	24	\$4,820.40	
213	Phase 2	Net7: Solarwinds, grooming	Keylite			\$200.85	8	\$1,606.80	\$28,520.70
214	Final	Site Management	Keylite			\$108.15	128	\$13,843.20	
215	Final	Engineering Management	Keylite			\$200.85	40	\$8,034.00	
216	Final	Net 8: OES, Engineer 1	Keylite			\$200.85	40	\$8,034.00	
217	Final	Net 9: OES, Engineer 2	Keylite			\$200.85	40	\$8,034.00	\$37,945.20
								\$175,728.30	SERVICES TOTAL

Attachment 2 Project 2—EMS-Sunrise Site Project Equipment

Attachment 2				POWE	EYLIE	
				Start S	trong – Finish Strong Stay Strong	
	EMS-SND Microwave Frequency Change 6-11 GHz	9-4-2024				
	End-one inicionate requestly offange 6-11 off2	3-4-2024			Sell Price	
Part Number	Description	Quantity	Unit List Price	Extended List Price	Ext. List -10%	
C000065L007B	LPU and Grounding Kit (1 Kit per ODU)	4	\$440.00	\$1,760.00	\$1,584.00	
C110082B027	PTP 820S Radio 11WGHz,TR500,Ch7W13,Hi,11425-11725MHz	1	\$3,675.00	\$3,675.00	\$3,307.50	
C110082B028	PTP 820S Radio 11WGHz, TR500, Ch7W13, Lo, 10915-11207MHz	1	\$3,675.00	\$3,675.00	\$3,307.50	
AR-E0PT820S-WW	PTP820S Upgrade to All Risks Advance Replacement during Standard Warranty	2	\$89.00	\$178.00	\$160.20	
AR-E4PT820S-WW	PTP820S All Risks Advance Replacement, 4 Additional Years	2	\$447.00	\$894.00	\$804.60	
	OSP Armored Broadband Copper-clad CAT5E twisted pair cable, Black, 328' (100					
04-001-55-328	meters) spool, SOI	2	\$350.00	\$700.00	\$630.00	
N000082L014	PTP 820 Glands_x5_KIT	2	\$38.00	\$76.00	\$68.40	
N000082L116	Grounding Cable, 1m with M6 ring to M6 ring	2	\$8.00	\$16.00	\$14.40	
N000082L126	PTP 820/850 Act. Key - Capacity 650M with ACM Enabled, Per Tx Chan	2	\$1,270.00	\$2,540.00	\$2,286.00	
N000082L173	Grounding Kit for CAT5E F/UTP 8mm and Cat6A Cable	5	\$25.00	\$125.00	\$112.50	
N000082L174	Misc. Shop Supplies	2	\$100.00	\$200.00	\$180.00	
N110082D075	PTP 820 4' ANT,SP,11GHz,RFU-C TYPE&Std UBR100 - Andrew	2	\$2,650.00	\$5,300.00	\$4,770.00	
	Shipping & Handling				\$1,378.01	
				Materials Subtotal	\$18,603.11	
	Services		Hourly/unit Cost	Extended Cost		
	Microwave Engineering	12	\$200.76	\$2,409.12		
	System Engineering	8	\$200.76	\$1,606.08		
	Technician labor, onsite installation, configuration, burn in, test	24	\$108.15	\$2,595.60		
	Tower Structural Analysis EMS	0	\$4,200.00		County provided	
	Tower Work EMS	1	\$10,500.00	\$10,500.00	, p	
	Remeidal climb (if necessary)	0	\$5,000.00		to be quoted if nec	essarv
	Interference Analysis to date - Engineering Support	16	\$200.76	\$3,212.16		,
	Interference Analysis - Lift Rental	0	\$900.00	\$0.00	to be quoted if nec	essary
	FCC License				County Provided	
				Services Subtotal	\$20,322.96	
				Contingency	\$0.00	
				PROJECT TOTAL	\$38.926.07	

Attachment 3 Project 2—Acceptance Testing Procedures



Broward Fire Station Alerting System

Acceptance Test Procedure

Point to Point Microwave System

V5 - EMS-Sunrise Link Replacement

BFSA ATP: PTP Microwave System Introduction 3 Reference for Test Results **IP Connectivity** 4 Microwave Radio Parameters 5 SND to EMS 5 7 EMS-SND Review Installations 10 Review 30 Day Performance 11 Page 2 of 11



Introduction

This document specifies the acceptance tests for the **Point to Point Microwave System** provided under the Broward Fire Station Alerting contract RP1426611P2_1, revised as:

Project 2: Microwave System Repair: EMS-Sunrise Site Changeout of Frequency 6 GHz to 11 GHz

Note: Receive Signal Strength is modeled in the Link Planner based on minimum modulation (64QAM). These microwave radios are configured with *adaptive modulation*. Summary Test Results


Reference for Test Results

For each microwave link, collect active data from installed radios from the following fields:



For each link, collect Link Planner data. Review measured test results against LinkPlanner prediction model.

Link Planner version 4.91



Page 3 of 11



Test Date	
Test Results	Pass / Fail
Tested By	Tom Sullivan
Witnessed By	
Punchlist Items?	None

IP Connectivity

- 1. Connect to FireNet with VPN
- 2. Ping each of the following microwave radios three times with the PTPtest1.bat file

Site	Radio	Segment	IP Address	
SND	SND to EMS	MW Segment 1	172.29.101.250	
EMS	EMS to SND	MW Segment 2	172.29.101.5	

 Review the output file ptptest1.txt Ensure all specified devices respond to ping requests within 100 mSec

Test Date	
Test Results	Pass / Fail
Tested By	Tom Sullivan
Witnessed By	

Page 4 of 11




Punchlist Items? None


Microwave Radio Parameters

SND to EMS

- □ Log on to http://172.29.101.250/
- □ Review Unit Summary. [update with new radio output report]



☐ Review Current Alarms. Ensure no errors exist.



□ Review Radio Summary. [update with new radio output report]


Page 5 of 11





Review Radio Parameters

[update with new radio output report]

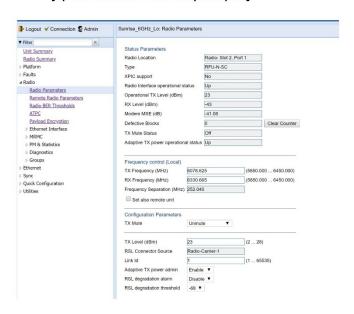

Test Date	12/4/2019
Test Results	Pass / Fail
Tested By	Deveson
Witnessed By	
Punchlist Items?	None


Page 6 of 11




EMS-SND

- □ Log on to http://172.29.101.5/
- □ Review Unit Summary

[update with new radio output report]

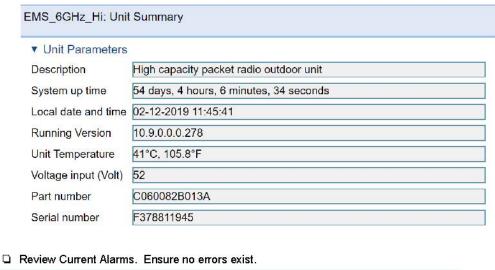




Page 7 of 11



□ Review Radio Summary.
[update with new radio output report]



Review Radio/Radio Parameters.[update with new radio output report]

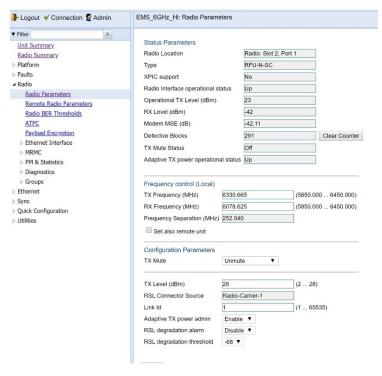

Page 8 of 11



Test Date	
Test Results	Pass / Fail
Tested By	Deveson
Witnessed By	
Punchlist Items?	None

Page 9 of 11



Review Installations

For each of the following sites, inspect the physical installations. Note any punchlist items.

Site	Date Inspected	Punchlist Notes
SND		
EMS		

Test Date		
Test Results	Pass / Fail	
Tested By		
Witnessed By		
Punchlist Items?		

Page 10 of 11





Review 30 Day Performance

Monitor new link for 30 days.

Compare against predicted reliability specification in Link Planner.

Create report showing signal anomalies during the test period.

Test Complete Date	
Test Results	Pass / Fail
Tested By	Deveson
Witnessed By	
Punchlist Items?	None

Page 11 of 11

Attachment 4

Attachment 4 Project 3—Markham Park—Davie Antenna Replacement Equipment

Attachme	nt 4								KEYLITE POWER & LIGHTING CORP. Seart Strong - Pinish Scrong Stay Strong	
		Markham - Davie Antenna Replacement Equipment & Service Cost								
quipment	:									
ltem	Part No	Description	Quantity	L	ist Price	Extended Price		Extended	Price Less 10%	
1	VHLP6-11W-3WH/A	1.8m 6' Valuline High Performance Low Profile	2	\$	6.742.00	\$	13,484.00	\$	12,135,60	
2	C000065L0078	CAM LPU and Grounding Kit 1 per ODU	2	\$	464.83		929.66		836.69	
		Total Equipment						\$	12,972,29	
		Shipping & Handling						\$	1,556.67	
		Total Equipment Cost						\$	14,528.96	
Services:										
Item		Description	Unit		Price	Extended Price				
,		Tower Crew Installation		•	7 500 00	•	15,000,00			
2		On-Site Technician	32	\$	7,500.00 114.57					
3		Project Management	8	\$	80.55					
4		Misc Materials	1	\$	500.00	•	500.00			
		Total Services						\$	19,810.64	
		Total Markham - Davie Antenna Replace	ement Project	Co	sts			\$	34,339.60	
